

**Grant 0599-LAO: Second Greater Mekong Subregion Tourism Infrastructure for
Inclusive Growth Project**

Quarterly Progress Report No. 18

Reporting Period: 1 April – 30 June 2023

July 2023

DRAFT FINAL

Ministry of Information, Culture and Tourism

TABLE OF CONTENTS

Location map of subprojects	3
1. Basic Data	4
2. Financing Plan and Allocation of Grant Proceeds	4
Financing Plan:	4
Detailed Cost Estimates by Expenditure Category and Financier:.....	4
3. Status of Grant Utilization.....	4
Contract Awards and Disbursements:	4
Weighted Progress, Contract Awards and Disbursement against Elapsed Time:	5
Contract Awards by Category:	5
Expenditure by Financier:	5
Government financing:.....	5
4. Implementation Arrangements	8
5. Implementation Progress.....	8
Project scope:	8
Progress to date:.....	9
Progress towards realizing contributions to ADB Results Framework:	45
Performance monitoring:.....	47
6. Financial Management	47
Disbursement Arrangement:	47
Advance Fund Procedure and Statement of Expenditure Procedure:.....	48
Counterpart Fund:.....	48
Accounting:	48
Auditing and Public Disclosure:.....	48
7. Procurement	49
Procurement Plan:	49
Procurement of Goods and Works:	49
Recruitment and Utilization of Consulting Services:	50
8. Safeguards Implementation and Submission of Semi-annual Integrated Safeguards Monitoring Report.....	50
9. Gender Action Plan Implementation Status.....	58
10. Compliance with Grant Covenants.....	58
11. Summary of Workplan for Next Quarter.....	59
Procurement packages/consulting services contracts to be awarded next quarter:	59
Main activities planned for Q3 2019:	59
Planned disbursements:.....	63
12. Issues and Recommendations	63

Annexes


1. Progress of Output 1 civil works by subproject as of 30 June 2023
2. Record of Output 2 and 3 and Project Management Activities implemented during Quarter 2 of 2023 (1 April – 30 June 2023)
3. Progress towards DMF targets and activity implementation as of 30 June 2023
4. Weighted implementation table with progress as of 30 June 2023
5. Project financial management action plan progress as 30 June 2023
6. Goods and works procurement monitoring table as of 30 June 2023
7. Consultant recruitment monitoring table as of 30 June 2023
8. Utilization of consulting services as of 30 June 2023
9. GAP implementation progress as of 30 June 2023
10. Status of compliance with Grant Covenants as of 30 June 2023
11. ASEAN Tourism Standards Certification in Target Provinces Since 2008
12. Eligible Project Support for ASEAN Tourism Standards
13. Progress of Accident Report's Preventive and Corrective Actions

Location map of subprojects

LAO PEOPLE'S DEMOCRATIC REPUBLIC

Vientiane Province

- | | | | |
|---------------|---|---------------|--|
| LAO-V1 | Nam Ngum Reservoir Access Improvements | LAO-V3 | Western Loop Rural Access Road and Bridge Improvements |
| LAO-V2 | Kaeng Yui Waterfall Access Improvements | LAO-V4 | Vang Vieng Urban Renewal (street beautification etc) |
| | | LAO-V5 | Vang Vieng Solid Waste Management Improvements |

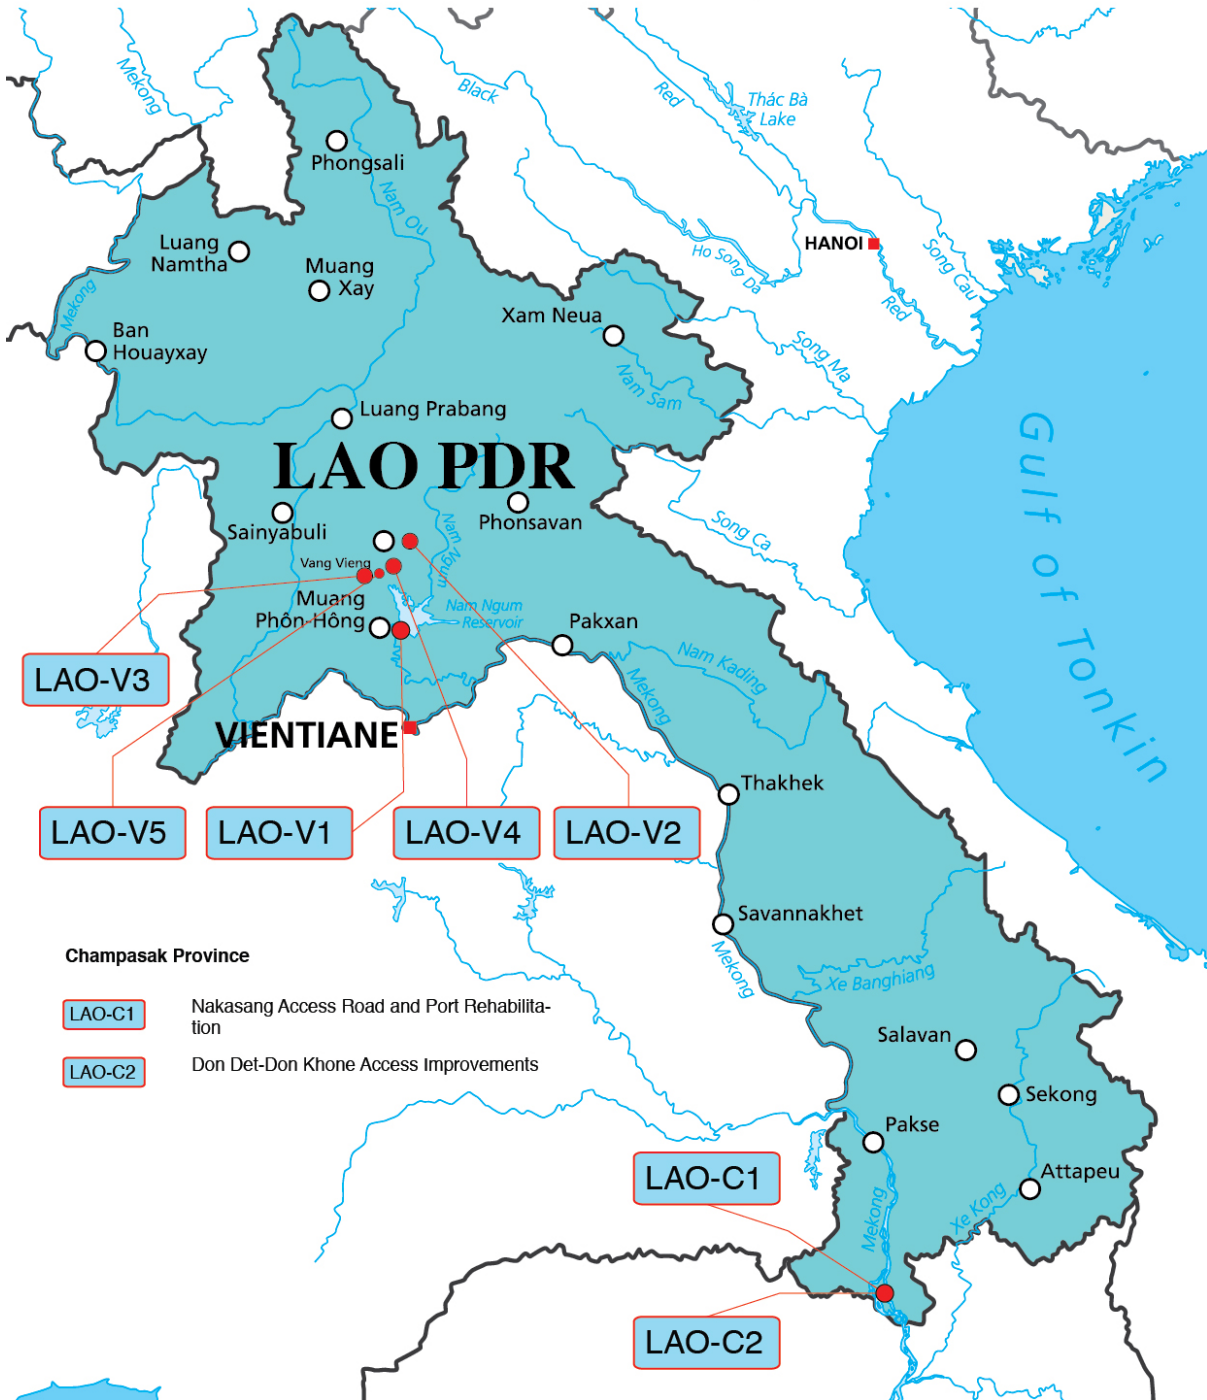

1. Basic Data

Grant number:	0599-LAO
Grant Amount:	USD 47,000,000
Board Approval:	31 August 2018
Financing Agreement Signed:	16 October 2018
Grant Effectiveness:	25 December 2018
Physical Completion Date:	31 December 2024
Grant Closing Date:	30 June 2025
Elapsed Grant Period:	54 months/78 months (69%) (from Grant Effectiveness to Closing)
Project Overall Progress:	72.49%
Recipient:	Ministry of Finance, Lao PDR
Executing Agency:	Ministry of Information, Culture and Tourism, Lao PDR
Implementing Agency:	Departments of Information, Culture and Tourism of Champasak, Luang Prabang, and Vientiane Province, and the Vang Vieng Urban Development Administration Authority
Date of Last Review Mission:	14 November – 5 December 2022 (regular Review Mission) 19-22 April 2023 (Special Project Administration: Social Safeguards Review Mission)

2. Financing Plan and Allocation of Grant Proceeds

Financing Plan:

Source	Amount (\$mill) ^a	Share of Total (%)
ADB Special Funds Resources	47.00	96.5
Government of Lao PDR	1.68	3.5
Total Project Costs	48.68	100

^a ADB approved on 27 August 2020 a minor change in the project's financing plan, shifting financing of land acquisition and resettlement (LAR) costs from government to ADB.

Detailed Cost Estimates by Expenditure Category and Financier:

The PAM table showing the Detailed Cost Estimates by Expenditure Category and Financier table is reproduced on page 6 for reference.

3. Status of Grant Utilization

Contract Awards and Disbursements:

As of 30 June 2023, based on GFIS

	2022 (\$ mln)					2023 (\$ mln)				
	Q1	Q2	Q3	Q4	Total	Q1	Q2	Q3	Q4	Total
CA Projections	0.339	0.629	0.690	1.200	2.858	1.037	1.980	0.960	1.030	5.007
Cum CA Projections	33.265	33.895	34.585	35.785		37.094	39.074	40.034	41.064	
Actual CA	1.370	0.929	0.524	1.633	4.456	0.363	0.329			0.692
Actual Cum CA	32.969	33.898	34.422	36.055		36.418	36.747	36.747	36.747	
Disb Projections	1.755	1.605	2.500	2.100	7.961	1.890	3.350	3.570	3.020	11.830
Cum Disb Projections	14.580	16.185	18.685	20.785		23.645	26.995	30.565	33.585	
Actual Disb	1.755	1.955	2.603	2.617	8.930	2.046	2.668			4.714
Actual Cum Disb	14.580	16.535	19.138	21.755		23.801	26.469	26.469	26.469	

CA = Contract Awards; Cum = Cumulative; Disb = Disbursement; LGFIS = Loan and Grant Financial Information Services; mln = million; Q = quarter.

Contract Awards by Category:

As of 30 June 2023

Category	Total ADB financing ^b (\$ mln)	Contract Awards (\$ mln)	Uncommitted (\$ mln)
A. Investment Cost			
1. Civil Works	27.60	21.05	6.55
2. Equipment and Vehicles	2.13	0.41	1.72
2. Consulting Services	8.00	8.07	(0.07)
4. Project Management	0.80	0.68	0.12
5. Capacity Building	4.40	4.04	0.36
6. Land Acquisition and Resettlement	1.30	1.17	0.13
Subtotal (A)	44.23	35.43	8.80
B. Recurrent Cost^a			
1. PCU and PIU Staff Cost	0.70	0.44	0.26
2. PCU and PIU Operations	1.07	0.53	0.54
3. PCU and PIU Vehicles and Office Equipment	0.40	0.36	0.04
Subtotal (B)	2.17	1.32	0.85
Total Base Cost (A+B)	46.40	36.75	9.65

^a The recurrent costs financed by ADB are in-cash and recurrent costs financed by the Government of Lao PDR are in-kind

^b Reflecting revised allocations agreed during ADB's Mid-term Review Mission conducted 16 May to 6 June 2022. ADB = Asian Development Bank; PCU is project coordination unit; PIU = project implementation unit.

Expenditure by Financier:

As of 30 June 2023

Expenditures	ADB (\$ mln)	Govt. (\$ mln)	Total (\$ mln)
Actual expenditure for Project Quarter 18 (Q2 2023)	2.668	0.064	2.733
Cumulative expenditure up end of Project Quarter 18 (Q2 2023)	23.800	0.763	24.563

ADB = Asian Development Bank; Govt. = Government; mln = million.

Government financing:

As per the original PAM (version 22 May 2018), the Government would finance: (i) government counterpart staff salaries and office space (in-kind); and (ii) land acquisition and resettlement (LAR) (in-cash). On 24 August 2020 the Ministry of Finance requested ADB to approve financing land acquisition and resettlement (LAR) costs from the grant proceeds, instead of government's counterpart funds. The justification for this request was fiscal constraints due to the COVID-19 pandemic, during which the government has been experiencing challenges meeting its revenue targets, and budget has been reallocated for the emergency COVID-19 pandemic response and recovery. These constraints are impeding the government's ability to make available and thus timely disburse the required LAR compensation payments to the project's affected households. On 27 August 2020, ADB approved a minor change in the project's financing plan to facilitate this, reducing government's counterpart funding from \$1.8 million (3.7% of total project costs) to \$1.68 million (3.5% of total project costs), and consequently, reducing the total project cost from \$48.8 million to \$48.68 million. This change is reflected in the updated PAM of 30 April 2021.

Weighted Progress, Contract Awards and Disbursement against Elapsed Time:

A graph showing cumulative weighted progress, contract awards and disbursement in percentage of total against elapsed time (by quarter) is presented on Page 7.

Detailed Cost Estimates by Expenditure Category and Financier

Item	ADB ^d				Government of Lao PDR				Total Cost
	Amount	Amount (Taxes & Duties)	Total	% of Cost Category	Amount	Amount (Taxes & Duties)	Total	% of Cost Category	
A. Investment Cost									
1. Civil Works	25.09	2.51	27.60	100.0%	-	-	-	0.0%	27.60
2. Equipment and Vehicles	1.94	0.19	2.13	100.0%	-	-	-	0.0%	2.13
2. Consulting Services	7.27	0.73	8.00	100.0%	-	-	-	0.0%	8.00
4. Project Management	0.73	0.07	0.80	100.0%	-	-	-	0.0%	0.80
5. Capacity Building	4.00	0.40	4.40	100.0%	-	-	-	0.0%	4.40
6. Land Acquisition and Resettlement ^c	1.30	-	1.30	100.0%	-	-	-	0.0%	1.30
Subtotal (A)	40.33	3.90	44.23	100.0%	-	-	-	0.0%	44.23
B. Recurrent Cost^a									
1. PCU and PIU Staff Cost	0.64	0.06	0.70	42.3%	0.87	0.09	0.96	57.7%	1.66
2. PCU and PIU Operations ^b	0.97	0.10	1.07	65.0%	0.52	0.05	0.58	35.0%	1.65
3. PCU and PIU Vehicles and Office Equipment	0.36	0.04	0.40	100.0%	-	-	-	0.0%	0.40
Subtotal (B)	1.97	0.20	2.17	62.0%	1.39	0.14	1.53	38.0%	3.70
Total Base Cost (A+B)	42.30	4.10	46.40	96.8%	1.39	0.14	1.53	3.2%	47.93
D. Contingencies									
Physical Contingency	0.30		0.30	83.5%	0.06		0.06	16.5%	0.36
Price Contingency	0.30		0.30	77.7%	0.09		0.09	22.3%	0.39
Sub-total (D)	0.60	-	0.60	80.5%	0.15	-	0.15	19.5%	0.75
Total Project Cost (A+B+C+D)	42.90	4.10	47.00	96.3%	1.54	0.14	1.68	3.4%	48.68
% of Total Project Cost			96.6%				3.4%		100.0%

^a The recurrent costs financed by ADB are in-cash and recurrent costs financed by the Government of Lao PDR are in-kind; ^b Externally hired staff, office supplies, and fuel.


^c Following a minor change in project's financing plan approved on 27 August 2020, the cost of land acquisition and resettlement, which was originally to be covered the Government of Lao PDR, is now funded by ADB grant.

^d Allocations reflect revised allocations approved by ADB during the MTR Mission of 16 May – 6 June 2022

Source: Project Administration Manual (PAM).

Weighted Progress, Contract Awards and Disbursement against Elapsed Time

As of 30 June 2023

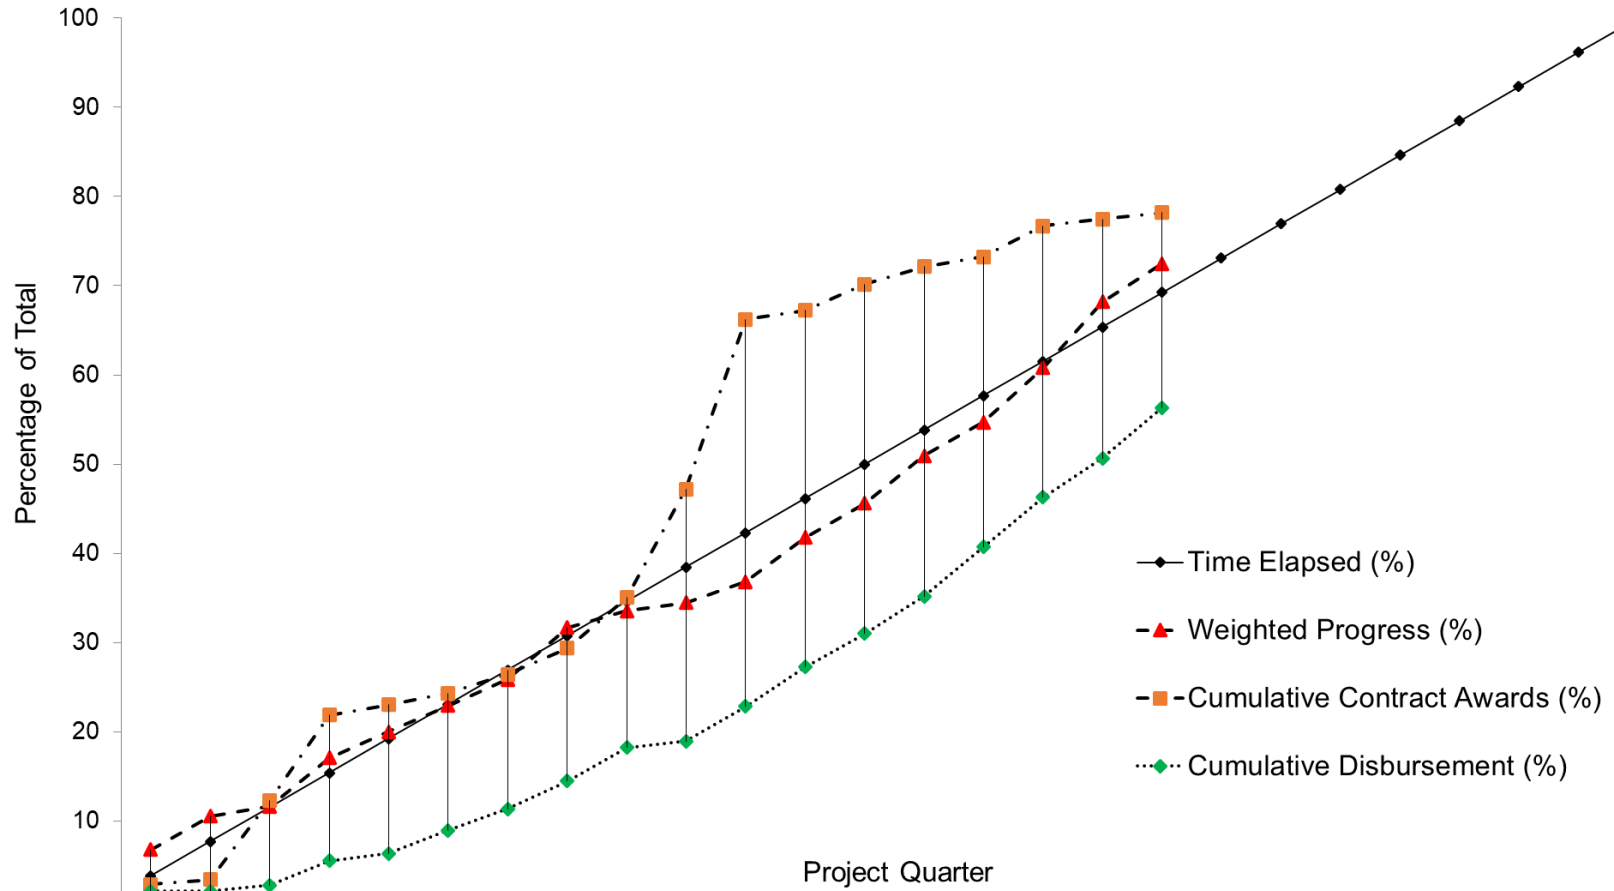

	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26
Time Elapsed (%)	3.85	7.69	11.54	15.38	19.23	23.08	26.92	30.77	34.62	38.46	42.31	46.15	50.00	53.85	57.69	61.54	65.38	69.23	73.08	76.92	80.77	84.62	88.46	92.31	96.15	100.00
Weighted Progress (%)	6.78	10.55	11.64	17.09	20.02	22.96	25.88	31.70	33.56	34.47	36.83	41.77	45.60	50.95	54.68	60.80	68.20	72.49								
Cumulative Contract Awards (%)	2.93	3.43	12.33	21.89	23.06	24.32	26.43	29.36	35.06	47.19	66.21	67.23	70.15	72.13	73.23	76.71	77.49	78.19								
Cumulative Disbursement (%)	2.13	2.13	2.80	5.56	6.34	8.97	11.34	14.48	18.21	18.97	22.86	27.29	31.02	35.17	40.72	46.29	50.64	56.32								

4. Implementation Arrangements

The GMS Tourism Working Group functions as the project's subregional steering committee and coordinates joint marketing and regional tourism standards adoption. The executing agency is MICT. A National Project Steering Committee (NPSC) has been established and meets periodically to review progress. As of 30 July 2021, the NPSC comprises the Vice Minister for Tourism, MICT (Chair), Director General of MICT's Planning and International Cooperation Department and Director Generals of the four tourism departments of MICT. NPSC members also serve on the project's bid evaluation and consultant selection committees. An 11-member project coordination committee has also been established, chaired by the project director, with members from various departments and units in MICT involved in project implementation.

MICT has established a Vientiane-based Project Coordination Unit (PCU) to handle overall project coordination and management, comprising a project director, project manager, financial controller, chief accountant, office manager, office assistant, and an internal auditor. As of 1 October 2021, the PCU financial administration capacity is strengthened with the appointment of an assistant accountant.

MICT has opened and is managing a project Advance Account and is responsible for overall financial management of the project. ADB has disbursed \$1m into the Advance Account to facilitate implementation of project activities identified in the approved 2019 costed annual workplan for the project using the Statement of Expenditure (SOE) procedure. On 4 December 2020, ADB has approved an increase of the ceiling of the advance account from \$1.0 million to \$1.5 million and then on 3 March 2022 by another \$800,000 to \$2,300,000 to finance the Land Acquisition and Resettlement (LAR) cost.

Provincial- and district-level implementing agencies have established Project Implementation Units (PIUs), embedded within the provincial DICTs of Champasak, Luang Prabang, and Vientiane Province, and the Vang Vieng UDAA, to manage output 1 and select output 3 activities. Each PIU comprises a supervisor, director, manager, finance officer, accountant and secretary, and full-time technical teams consisting of an infrastructure, tourism coordinator, standard and capacity building coordinator, a DMN coordinator, and a marketing and product development coordinator. The PIUs at the Champasak and Vientiane Province DICTs and at the Vang Vieng UDAA have both an infrastructure technical team to coordinate and support output 1 infrastructure activities, and a tourism technical team to coordinate and support output 2 implementation and manage select output 3 activities. Since there are no infrastructure subprojects in Luang Prabang Province, the PIU there only has a tourism technical team. PIUs have opened and are administering project sub-accounts to facilitate day-to-day project administration. Reporting, financial management, safeguards and knowledge management is led by the PCU in close coordination with all PIUs.

These implementation arrangements differ slightly from how they are described in the initial Project Administration Manual (PAM). During the project's Mid-term Review Mission, the PAM description has been revised to reflect the actual arrangements. These changes will be incorporated by ADB in an updated version of the PAM.

5. Implementation Progress

Project scope:

The project is designed to help transform secondary GMS central and southern corridor towns into economically inclusive, competitive international tourism destinations by improving road and water transport infrastructure, urban environmental services, and capacity to sustainably manage tourism growth. It will boost trade in services and deepen regional cooperation and integration among the GMS and Association of Southeast Asian Nations (ASEAN). About

88,000 residents are expected to directly benefit from climate-resilient infrastructure development and increased access to economic opportunities.

The project impact is sustainable, inclusive, and more balanced tourism development achieved. The outcome is tourism competitiveness of secondary towns in Cambodia and the Lao PDR increased. By 2025, Cambodia and Lao PDR's share of ASEAN's international visitor arrivals will increase from 8.0% to 8.3% and project areas will receive 700,000 more international tourists. This will increase aggregate annual visitor expenditure from \$0.55 billion to \$0.91 billion.

The project has three outputs: (i) urban-rural access infrastructure and urban environmental services improved; (ii) capacity to implement ASEAN tourism standards strengthened; and (iii) institutional arrangements for tourism destination management and infrastructure O&M strengthened. Project areas in Lao PDR include Champasak, Luang Prabang and Vientiane provinces, all located along the GMS Central Economic Corridor.

Progress to date:

Outcome: Tourism competitiveness of secondary towns in the Lao PDR increased

Progress towards the project's outcome in Lao PDR as of 30 June 2023 can be summarized as follows:

As of 30 June 2023

Outcome Performance Indicators	Baseline (2016)	Targets (2025)	Progress
a. Lao PDR's share of ASEAN international visitor arrivals increased	3.7%	3.8%	2017: 3.1% 2018: 3.1% 2019: 3.3% 2020: 3.4% 2021: no data 2022: no data
b. Annual international visitor arrivals in project areas increased	820,100	1,263,100	2017: 941,000 2018: 1,210,800 2019: 1,260,000 2020: 331,356 2021: no data (negligible due to COVID-19 pandemic country closure) 2022: 437,481
c. Aggregate annual visitor expenditure in project areas increased	\$380.2 million <i>corrected from \$363.9 million</i>	\$589.0 million	2017: \$337.4 million 2018: \$385.5 million 2019: \$474.3 million 2020: \$133.1 million 2021: no data (negligible due to COVID-19 pandemic country closure) 2022: data not yet available
d. Women comprise at least 55% of tourism workers in project areas	50%	55%	Female workers account for 57% of the total workforce in Lao PDR's tourism and hospitality sector. ¹ Champasak Province: 55.9% Vientiane Province: 57.5% Luang Prabang Province: 52.1% Aggregate for the three target provinces: 54.3%

^a Source: Skills for Tourism Project (LAO/029), Ministry of Education and Sports

International arrival and expenditure results for 2020 and 2021 are heavily impacted by the border closures and travel restrictions in response to the COVID-19 pandemic. The country

¹ Ministry of Education and Sports, Lao PDR. 2021. *Tourism and Hospitality Enterprise Survey of Employment and Skills in Lao PDR*. Vientiane.

re-opened for international tourism in May 2022. It was thought the recovery period may be long, and that as a result performance during the 2022-2024 period will be significantly lower than originally projected. While this was true for 2022, international arrivals to Lao PDR during the first six months of 2023 topped 1.6 million, 75% of the arrivals recorded in the same period in pre-pandemic 2019, an indication that arrivals may be rebounding quicker than expected.

Output 1: Urban-Rural Access Infrastructure and Urban Environmental Services Improved

Output 1 will upgrade transport infrastructure and improve environmental conditions at tourist destinations to boost tourist arrivals and receipts and catalyze additional private investment in accommodations and other tourism-related enterprises.

The Project includes the following seven infrastructure subprojects, packaged into five² works packages, as follows:

Works Package: TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements

Subproject C1: Nakasang Access Road and Port Rehabilitation

Subproject C2: Don Det-Don Khone Access Improvements

Works Package: TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements

Subproject V1: Nam Ngum Reservoir Access Improvements

Works Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements

Subproject V2: Kaeng Yui Waterfall Access Improvements

Subproject V3: Western Loop Rural Access Road and Bridge Improvements

Works Package TIIGP2-LAO-W03a: Vang Vieng Urban Renewal

Subproject V4: Vang Vieng Urban Renewal

Works Package: TIIGP2-LAO-W04: Vang Vieng Landfill Improvements

Subproject V5: Vang Vieng Solid Waste Management Improvements

For Works Packages TIIGP2-LAO-W01 and TIIGP2-LAO-W04, detailed engineering design (DED), bill of quantities (BOQ), technical specification, bidding documents, updated safeguards documents, and recommendations for equipment for O&M were prepared during the Project Preparation Technical Assistance (PPTA) by NorConsult under a direct contract with ADB. These two packages (for subprojects C1, C2 and V5) are referred to as “Stage 1” packages/subprojects.

For Works Packages TIIGP2-LAO-W02 and TIIGP2-LAO-W03/W03a, feasibility studies, preliminary designs, preliminary cost estimates and safeguards documents were prepared during project preparation by the PPTA Consultant PM Group under a direct contract with ADB. These two packages (for subprojects V1, V2, V3 and V4) are referred to as “Stage 2” packages/subprojects.

The Project Management and Civil Engineering Support (PMCES) Consultant - Ramboll Danmark A/S in association with Specity Solutions Consulting Co. Ltd., mobilized on 5 August 2019 to assist the PCU and PIUs with (i) review and update DED for Stage 1 subprojects; (ii) preparation of DED for Stage 2 subprojects, (iii) safeguards document updating and compliance monitoring, (iv) construction supervision, (v) preparation of operations and maintenance (O&M) plans and asset management technical training, and (vi) project management and administration.

² Originally there were four works packages, when Subproject V4: Vang Vieng Urban Renewal was included in Package TIIGP-LAO-W03. However, during the course of 2020 it became clear that coordination and alignment with the ADB-financed Water Supply and Sanitation Sector Project in Vang Vieng was needed to minimize LAR impacts and streamline execution. To not delay Subprojects V2 and V3, it was decided in September 2020 to separate Subproject V4 from Works Package TIIGP2-LAO-W03 and create a new Works Package for V4, namely TIIGP2-LAO-W03a.

Progress of Output 1: Urban-Rural Access Infrastructure and Urban Environmental Services Improved as of 30 June 2023, is summarized as follows:

As of 30 June 2023

	Activity	W01: Nakasang and Don Det - Don Khone Access Improvements	W02: Nam Ngum Reservoir Access Improvements	W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements	W03a: Vang Vieng Urban Renewal	W04: Vang Vieng Landfill Improvements
1	Prepare civil works design and bidding documents	✓	✓	✓	✓ (DED completed, bidding documents pending)	✓
2	Safeguards document approval	✓	✓	✓	Not yet started	✓
3	Complete land acquisition and resettlement Compensation	✓	→	✓	Not yet started	✓
4	Civil works procurement	✓	✓	✓	Not yet started	✓
5	Implement civil works construction, supervision, and supply equipment	✓	→	→	Not yet started	→
6	Safeguard Monitoring	→	→	→	Not yet started	→

Stage-1: TIIGP2-LAO-W01 and TIIGP2-LAO-W04 (subprojects C1, C2 & V5)

Stage 1 subprojects are packaged as follows:

Works Package: TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements

Subproject C1: Nakasang Access Road and Port Rehabilitation

Subproject C2: Don Det-Don Khone Access Improvements

Works Package: TIIGP2-LAO-W04: Vang Vieng Landfill Improvements

Subproject V5: Vang Vieng Solid Waste Management Improvements

TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements

The commencement letter was issued to the Contractor on 12 May 2020 and the construction work commenced on 26 May 2020. The period of performance is 731 calendar days, and the Intended Completion Date is therefore 25 May 2022. Contract Variation Order No. 1 (VO No. 1) and time extension request was approved by ADB with (i) extending the contract completion date by 319 days (10.6 months) from the intended completion date of 25 May 2022 to 10 April 2023 and (ii) changing of the original quantities of few work items in Bill No.2: Nakasang Access Road Improvements and Bill No.3: Det and Khone Island and Footpath Improvements. The proposed changes will increase the contract amounts under Bill No.2 and Bill No.3, which will be covered by the savings identified under Provisional Sum for 3 Bridges and Physical Contingencies.

Contract Variation Order (VO No. 2) was approved by ADB with (i) extending the contract by 81 days (2.7 months) from the extended completion date of 10th April to up to 30 June 2023 to complete all of outstanding works on site, especially (i) Nakasang Port Rehabilitation, (ii) Road Shoulder Improvements of all the access roads in Nakasang, Don Det and Don Khone including restoration of Nakasang, Don Det and Don Khone Accessibility, (iii) Sodding for embankment, (iv) Site Drainage of IRL-01 with Graveling Course; (v) Street light for the port, Road furniture installation of Nakasang, Don Det and Don Khone Access Roads; (vi) replacing the existing wooden bridge with concrete deck slab on Nakasang Port Access Road; and (vii) Nakasang Parking Drainage Improvement and changing the quantities of work items savings identified from the Bill No. 1, Bill No. 2, Day Works and Physical Contingency. The Contract Amount will be remained same as the original Contract of USD3,964,308.36.

The overall implementation progress, 30th June 2023 was 100.00% (Nakasang access improvement was 28.65%, Don Khone access improvement was 57.81% and Don Det access improvement was 13.54% completed) against the implementation schedule of 100.00% (with reference to new revised schedule on 10 May 2023) including 1.82% of work progress made in June 2023, especially installation of miscellaneous works for Nakasang Access Road, Don Det – Don Khone Access Roads including reflectorized road marking, traffic signs (single and double posts), guide post, kilometer posts, and street lighting Solar DC system & floating pontoon for Nakasang Port.

As of 30th June 2023, there are 21.11km out of 21.11Km Concrete Road Works completed. The detailed of the completed road matrix is as follows:

Road No	Completed, Km	Don-Det	Don-Khone,	Nakasang
Road No. IRL-01	1.35	1.35		
Road No. IRL-02	2.07	2.07		
Road No. IRL-03	2.49	2.49		
Road No. IRL-04	4.62		4.62	
Road No. IRL-05	5.65		5.648	
Road No. IRL-06	1.34		1.335	
Road No. IRL-07	0.10		0.104	
Road No. IRL-08	0.59		0.594	
Nakasang Access Road including River Port	2.90			2.90
Total	21.11	5.91	12.30	2.90

Summary of the facilities:

- 21.112 Km Road (2.904 Km at Nakasang, 5.907 Km in Don Det and 12.301 Km in Don Khone)
- 3 Bailey Bridges on Access Road IRL-05 in Don Khone
- 178.00 m Culvert (16.00 m Culvert at Nakasang)
- 3 Parking Areas (1 Nakasang, 1 Don Det old Port and 1 Ban Hang Khone)
- 11 Sets of Solar Light (9 Sets Nakasang Port and 2 Sets Railway Bridge _ Both Sides)
- 2 Boat Ramps (Nakasang River Port)
- 1 Pontoon (Nakasang River Port)
- 106.00 m Retaining Wall (Nakasang River Port) upstream side (U/S) & downstream side (D/S)
- 140.00 m Slope Protection by Rubble Stones (Nakasang River Port)
- 153.00 m Footpath (Nakasang River Port) U/S & D/S
- 25.00 m Drainage & Discharge RC Pipe
- Locomotive Area Improvements in Don Khone
- View Point in Don Det old Port

- Safety Guardrail on Approach road to Mekong Bridge in both sides Don Det and Don Khone (French Bridge)
- Renovation of Port Ticket Office/Waiting area of the Tourists
- Renovation of Ticket Office at Nakasang Parking area
- Cross Drainage at end of Nakasang River Port (U/S)
- Renovation of wooden bridge to concrete deck slab on access road along Nakasang Port (U/S)

By following to the Section 7 – General Conditions of Contract, Clause 69: Completion and Clause 70: Taking Over, The Project Manager certified that the Works under the Contract has been executed and completed in all respects in strict compliance with the provisions of the Contract including all plans, designs, drawings, specifications and all modifications thereof as per direction and satisfaction of the Project Manager. All defects in workmanship and materials reported during construction have been duly corrected.

The Employer issued the Completion Certificate on the date of 30th June 2023 to the Contractor for the Works Package No. TIIGP2-LAO-W01: Nakasang and Don Det - Don Khone Access Improvements.

The project was continuously implementing the preventive measures for the COVID -19 in accordance with the Prime Minister's Office Order No.06/PM regarding COVID-19 regulations. In response, the Contractor was taking safety measures of the COVID-19 Pandemic prevention including detailed specific measures to ensure health and safety for workers and inhabitants of the sub-project area were developed and included in the Contractor Environmental Management Plan (CEMP) which is being implemented at site.

The following activities being carried out by the contractor during the reporting period are given below:

TIIGP2-LAO-W04: Vang Vieng Landfill Improvements

Review findings of the DED for Package TIIGP2-LAO-W04 (Subproject V5) carried out in Q3 2019 for the landfill subproject revealed that the existing design required revision, entailing substantial alterations to the design, drawings, BoQ and technical specifications. It was further decided that an environmental compliance audit (ECA) needed to be conducted to test the design information. The PMCES Consultant engaged an ECA sub-consultant team to carry out this work, and the ECA report was approved by ADB on 22 March 2020.

The design revisions commenced during Q2 of 2020. A day-long stakeholder consultative meeting on the Draft Design was held on 26 June 2020 in Vientiane in the presence of the Vice Minister Mr. Ounthouang Khoaphanh, National Project Steering Committee, Head of DICT, Head of UDAA, Department of Housing and Urban Planning, Chief of Villages, other private and public sectors. The stakeholders provided feedback including the need for an O&M capacity assessment for solid waste management as a basis for the development of an O&M capacity building program for the Vang Vieng landfill and a financial assessment of the Vang Vieng landfill viability to be undertaken for the analysis of economical sustainability to form basis for the site management modality to be selected.

The final detailed design, safeguards documents and bidding documents were submitted for ADB's review during Q3 of 2020 and ADB cleared the design modification, safeguards and bidding documents in September, which were then sent for provincial approval. The invitation for Bids (IFB) for this Package was published on 14 September 2020, with a submission deadline and bid opening on 27 October 2020. The BER was approved in Q4 2020.

The Contract was signed on 19th February 2021. The Site possession was issued on 24 March 2021. The Notice to Proceed (NTP) was given on 5th April, 2021 with the commencement of works from 19th April 2021. The period of performance is 731 calendar days, and the intended completion date is therefore 20th April 2023.

The Works consist of:

- Construction of 2 (two) controlled landfill cells out of a total of 5 (five) cells;
- Preparatory earthworks and installation of a perimeter runoff interceptor drainage system;
- Construction of capped cell for the old waste;
- Construction of non-mechanical type material recovery facility (MRF);
- Construction of leachate collection, storage, and treatment system;
- Construction of treated leachate recirculation system;
- Construction of Faecal Sludge Treatment Plan (FSTP)/Septage Treatment Facility
- Construction of office, workshop, electrical and security buildings at the landfill site;
- Installation of Weighbridge and construction of office building
- Upgrading and elevating 0.8 km of the access road to the landfill site to be above flood levels;
- Construction of internal road and rainwater drainage system along with peripheral embankments;
- Construction of boundary wall and entrance gate:
- Construction of car washing facility;
- Construction of hazardous waste storage and landfill facility; and
- Construction of Incineration Facilities

The overall implementation progress, as of 30th June 2023, was 75.37% against the schedule of 91.72% (the revised work programme).

During this reporting period of April-June 2023, 3.24% of works progress made against 11.26% due to (i) delayed supplying building materials; (ii) delay in construction of hazardous waste

storage and incinerator buildings, and (iii) delay in construction of Planted Drying Bed and Administration Office because of lack of resources working on site.

During this quarter, the contractor progressed the construction work including (i) construction of MRF, workshop and administration buildings including fixing of doors and windows, installing of electrical network, fixing of floor tiles and ceilings; (ii) construction of incinerator room; (iii) construction of the planted drying bed (PDB); (iv) construction of landfill hazardous waste storage; and (v) waste disposal in Cell-5.

The Contract Variation Order No. 01 was approved by the ADB on 2 March 2023 including (i) the extension of the contract's intended completion date by 365 days, from 20 April 2023 to 20 April 2024, to enable completion of the remaining works; (ii) the revision of original quantities of some work items and adjust the corresponding budget allocations; and (iii) the utilization of savings under Bills No. D, G, H, K, M, P, Q, S, T, V, W, AB and Contingencies to cover the total cost changes.

The PMCES national experts (a Resident Engineer and a Supervisor) continued supervising the construction works on site to assist PIU and UDAA Vang Vieng.

The project was continuously implementing the preventive measures for the COVID -19 in accordance with the Prime Minister's Office Order No.06/PM regarding COVID-19 regulations. In response, the Contractor was taking safety measures of the COVID-19 Pandemic prevention including detailed specific measures to ensure health and safety for workers and inhabitants of the sub-project area were developed and included in the Contractor Environmental Management Plan (CEMP) which is being implemented at site.

The following activities being carried out by the contractor during the reporting period are given below:

Item	Description	Unit	Rate (USD)	April 2023 to June 2023		
				Quantity	Amount (USD)	Progress
BILL No. P: WORKSHOP / SERVICE BUILDING						8,498.18
P.07 Doors, Windows and Glass work						
P.07.4	AD3 Exterior & Interior door 0.8m x 2.15m	Set	262.00	3.00		786.00
P.07.5	AD4 Exterior&Interior door 0.7m x 2.15m	Set	247.00	1.00		247.00
P.07.6	AW1 Sliding window with steel grill 1270 x 1500	Set	370.00	1.00		370.00
P.07.7	AW2 Sliding window with steel grill 550 x 1270	Set	300.00	5.00		1,500.00
P.08.1	600mm x 600mm ceramic tiles	Metre Square	32.00	9.20		294.40
P.08.2	300 mm x 300 mm ceramic tiles (non-skid)	Metre Square	32.00	9.20		294.40
Wall finish						
P.08.3	300 mm x 600 mm ceramic tiles (glazed for cr)	Metre Square	35.00	24.00		840.00
P.09 Water/sanitary/drainage						
Water lines						
P.09.1	Supplying, laying, fitting and fixing of best quality 20 mm Ø PVC pipe incl. fittings	Metre	4.00	14.00		56.00
P.09.2	Supplying, laying, fitting and fixing of best quality 25 mm Ø PVC pipe incl. fittings	Metre	4.00	8.00		32.00
P.09.3	Supplying, laying, fitting and fixing of best quality 63 mm Ø PVC pipe incl. fittings	Metre	7.00	25.00		175.00
P.09.4	25 mm Gate valve incl. fittings	pc	6.00	1.00		6.00
P.09.5	Supplying, laying, fitting and fixing of best quality 50 mm ØPVC pipe incl. fittings	Metre	5.00	8.00		40.00
P.09.6	Supplying, laying, fitting and fixing of best quality 100 mm Ø PVC pipe incl. fittings	Metre	10.50	40.00		420.00
P.09.7	Supplying, laying, fitting and fixing of best quality 150 mm Ø PVC pipe incl. fittings	Metre	13.00	25.00		325.00
P.09.8	75 mm x 75 mm Floor drain	pc	7.00	4.00		28.00
P.09.9	100 mm Ø Cleanout w/ end cap	pc	7.00	1.00		7.00
P.09.10	50 mm Ø P-trap	pc	7.00	1.00		7.00
P.09.11	Water closet	Set	231.00	1.00		231.00
P.09.12	Urinal	Set	260.00	1.00		260.00
P.09.13	Lavatory Sink w/ counter top	Set	189.00	1.00		189.00
P.10 Electric wiring Service and workshop building						
P.10.1	THW wire 1x1.5 sqmm	Metre	0.58	750.00		435.00
P.10.2	THW wire 1x2.5 sqmm	Metre	0.74	300.00		222.00
P.10.3	THW wire 1x4 sqmm	Metre	1.05	300.00		315.00
P.10.4	XLPE 4x16-1x10 sqmm in PVC pipe	Metre	3.68	112.50		414.00
P.10.5	XLPE 4x10-1x5 sqmm in PVC pipe	Metre	3.15	112.50		354.38
P.10.6	DB1 main CB 32A, 3P	Set	21.00	1.00		21.00
P.10.7	DB1 main CB 32A, 2P	Set	21.00	1.00		21.00
P.10.8	Tube light with LED 20 W (wp)	Set	21.00	2.00		42.00
P.10.9	Tube light with LED 20 W (bare type)	Set	21.00	24.00		504.00
P.10.10	Tube light with LED 16 W (bare type) basin	Set	21.00	1.00		21.00
P.10.114	Down light with LED bulb 18 W	Set	21.00	2.00		42.00
BILL No. Q: PLANTED DRYING BED (PDB)						30,822.79
Q.01 Civil						
Q.01.7	RCC 30MPa, stone chips (SC)	Metre Cube	262.50	35.00		9,187.50
Q.01.8	PCC concrete work	Metre Cube	189.00	101.61		19,204.29
Q.01.9	Reinforcement Steel	Tonne	780.00	2.00		1,560.00
Q.02 Plumbing						
Waste water pipe line						
Q.02.2	Supplying and laying of 150 mm Ø uPVC pipe incl. fittings etc	Metre	13.00	67.00		871.00
BILL No. R: HAZARDOUS WASTE STORAGE						1,644.00
R.01 Civil						
Substructure works:						
R.01.9	125mm brick work with good quality bricks in cement mortar (1:4) 1 (as per specification)	Metre Square	12.60	11.68		147.12
Superstructure works:						
R.01.17	Minimum 12mm thick cement plaster (1:4) with portland composite cement	Metre Square	4.20	356.40		1,486.88
BILL No. S: INCINERATOR ROOM						6,722.65
Superstructure works:						
S.01.13	16mm dia bar wind bracing as per design drawings	Kg	2.00	404.22		808.44
S.01.14	supplying and fabrication of mild steel	kg	2.21	1346.80		2,974.21
S.01.15	Providing bearing joints fixed	Number	52.50	18.00		945.00
S.01.16	(Non corrugated) GI sheet for gable wall	Metre Square	8.40	35.00		294.00
S.01.17	Lighting roof sheet as per design drawings	Metre Square	9.45	4.00		37.80
S.01.18	Corrugated GI roof sheet as per design drawings	Metre Square	8.40	162.00		1,360.80
S.01.19	Supplying J - hook of 16mm dia MS rod (RB 300) (600mm meter long)	Number	2.10	144.00		302.40
BILL No. T: LANDFILL HAZARDOUS WASTE						443.52
T.01.3	400 mm thick drainage layer with sand + gravel- (20 mm size)	Metre Cube	8.40	52.80		443.52
BILL No. W: BOUNDARY WALL						3,640.00
W.01.5 Cement concrete work						
W.01.6	RCC 20MPa, stone chips (SC)	Metre Cube	150.00	1.50		225.00
W.01.7	Reinforcement Steel	Tonne	800.00	2.00		1,600.00
BILL No. AC: PLANTATION AND TURFING						2,576.00
AC.01.4	Supplying lawn grass of approved quality by truck	Metre Square	3.68	700.00		2,576.00
Total Executed Amount						100,191.28
						3.22%

Status of Stage-1 Works Packages:

Sub-project-W01	Status at start	Present Status	Outstanding Works
TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvement • C1: Nakasang Access Road and Port Rehabilitation • C2: Don Det-Don Khone Access Improvements	<ul style="list-style-type: none"> • DED prepared • IEE/EMP prepared • Social DDR prepared 	<ul style="list-style-type: none"> • DED Review submission by PMCES on 28 August 2019 • IEE and EMP approved by ADB on 12 September 2019 • ADB No Objection to the Bidding Document on 17 September 2019 • IFB issued on 18 September 2019 • Environmental Compliance Certificate (ECC) on (IEE/EMP) by PONRE/Champasak Province on 07September for the period of 17 October 2019 to 17 October 2020 • DED clearance certificates by DPWT/Champasak on 22 October 2019 • Bid opening on 30 October 2019 • Bid Evaluation Report, 16 December 2019 • ADB No Objection to the Bid Evaluation Committee's recommendation to award the contract on 23 December 2019 • ADB No objection to the DDR on 23 December 2019 	<ul style="list-style-type: none"> • List of minor pending works/punch list by Q3 2023

Sub-project-W01	Status at start	Present Status	Outstanding Works
		<ul style="list-style-type: none"> • Contract Award on 26 December 2019 • Contract Signing on 30 December 2019 • Kick-off meeting on 20 January 2020 • Site possession on 7 January 2020 • CEMP on 12 May 2020 • Revised Work Program on 12 May 2020 • UXO clearance on 29 April 2020 • Notice to proceed by 12 May 2020 • Commencement of Works on 26 May 2020 • Water quality tests carried out in September 2020 • CAP No Objection for the Safeguards Non-compliance at Nakasang River Port on 25 November 20 • CEMP revised based on comments from ADB and resubmitted to ADB on 06 December 2020 • CEMP training conducted during 21-23 December 2020 • GRM Training with District Authority, Contractor and Supervision Engineer on 18 January 2021 • Training on awareness and implementing HIV/AIDS, STI, Human Trafficking, Child Labour Exploitation Prevention Information to all workers (including Gender Action Plan Implementation) on 10 February 2021 at construction site • Approval of Preliminary Design of 3 Bridges in Don Khone in August 2021 • Approval of Detailed Engineering Design (DED) of 3 Bridges in Don Khone including BOQ in February 2022 • ADB MTR Mission visited the project site on 17 May 2022 • Variation Order No. 01 was approved on 26 May 2022 by ADB • ADB No Objection to extend the contract completion date by 319 days from the intended completion date of 25 May 2022 to 10 April 2023 • ADB No Objection Change of the original quantities of few work items in Bill No.2: Nakasang Access Road Improvements and Bill No.3: Det and Khone Island and Footpath Improvements. The proposed changes will increase the contract amounts under Bill No.2 and Bill No.3, which will be covered by the savings identified under Provisional Sum for 3 Bridges and Physical Contingencies • ADB provided no-objection for the CV No. 2 on 07 April 2023 • Request for the Certificate of Completion on 23 June 2023 by the Contractor • The Civil Works Contract has been taken over and the 365days Defects Liability Period has been started from 1st July 2023. 	

Sub-project-W04	Status at start	Present Status	Outstanding Works
TIIGP2-LAO-W04: Vang Vieng Landfill Improvements V5: Vang Vieng Solid Waste Management Improvements	<ul style="list-style-type: none"> • DED prepared • IEE/EMP prepared • IP drafted 	<ul style="list-style-type: none"> • DED Reviewed in September 2019 • ECA completed on 12 March 2020 • DED and BD Submission by PMCES on 18 August 2020 • ADB No Objection to the DED on 8 September 2020 • ADB No Objection to the Bidding Document on 11 September 2020 • ADB No Objection to the IEE and EMP on 15 September 2020 • ADB No Objection to the EGDRP on 15 September 2020 • IFB issued on 15 September 2020 • Bid opening on 27 October 2020 • DED clearance certificate by DPWT/Vientiane Province on 04 November 2020 • GRM training for PIU and the resettlement committee conducted (Vang Vieng District) on 14 December 2020 • UXO clearance by the Vang Vieng District Governor/Vientiane Province on 16 Dec 2020 • Compensation Payment to the affected people on dated 17 December 2020 • Environmental Compliance Certificate (ECC) on (IEE/EMP) issued by PONRE/Vientiane Province on 22 December for a period of 21 Dec 2020 to 20 Dec 2021 • ADB No Objection to the BER on 28 December 2020 • The Letter of Acceptance was issued on 12 February 2021 • The Contract was signed on 19 February 2021 • The site possession was given on 24 March 2021 • Kick-off meeting was conducted on 2nd April 2021 • The CEMP was approved with conditions by PMCES on 5th of April 2021 • The Notice to Proceed (NTP) was given on 5th of April 2021 with commencement of works from 19th of April 2021 • CEMP Training for the Contractor dated 18 June 2021 • Groundwater monitoring in Sep-Dec 2021 • Surface water monitoring in Sep-Dec 2021 • ADB MTR Mission visited the project site on 19th May 2022 • Groundwater monitoring in July 2022 • Surface water monitoring in July 2022 • CCR for Vang Vieng Solid Waste Management Improvements has been posted on the web. https://www.adb.org/projects/documents/lao-49387-002-smr dated 12Sep22 • ADB approved SMR No. 5 and disclosed on 27 Dec 2022 including accident Report 	<ul style="list-style-type: none"> • Approval of Additional Slope Protection by Q3 2023 • Approval of Variation order for additional work by Q3 2023 • Approval of Weighing Bridge by Q3 2023 • Continue Surface water quality: pH, To, TSS, DO, BODS, COD, Total N, Turb, Oil,CaCO3 and Grease, Hg, Cd, Pb, Ni, Zn, Cu, Cr (VI), Fe, Cl-, Coliform by every 6 months • Continue monitoring of groundwater quality pH, TSS, DO, BODS, COD, Total N, Turb., P043-, Oil,CaCO3 and Grease, Hg, Cd, Pb, Ni, Zn, Cu, Cr (VI), Fe, Cl-, Coliform by every 6 months • Continue Leachate samples: pH, BODS, COD, Turb., and heavy metal such as Cd, As, Zn, Cr (VI), Pb, and Cu by every 6months interval. • Compensation completion report (CCR) and closure report by Q3 2023

		<ul style="list-style-type: none"> • ADB No Objection on Contract Variation (CV No. 1) on dated 02 March 2023 including the Extension of the intended completion date by 365 days, from 20 April 2023 to 20 April 2024, to enable completion of the remaining works. • Extend the contract's intended completion date by 365 days, from 20 April 2023 to 20 April 2024, to enable completion of the remaining works 	
--	--	---	--

Stage-2: TIIGP2-LAO-W02, TIIGP2-LAO-W03 and TIIGP2-LAO-W03a (subprojects V1, V2, V3 & V4)

In parallel to the work on the Stage-1 subprojects, the PMCES Consultant completed the final detailed design, engineering-related and safeguard-related bidding documents and updated safeguards documents, and provided inputs in the bidding documents, which have been prepared in collaboration with the Financial Management and Procurement Specialists (individual consultants engaged by the Project) for the stage-2 subprojects V1, V2, V3 & V4, packaged as follows:

Works Package: TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements

Subproject V1: Nam Ngum Reservoir Access Improvements

Works Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements

Subproject V2: Kaeng Yui Waterfall Access Improvements

Subproject V3: Western Loop Rural Access Road and Bridge Improvements

Works Package TIIGP2-LAO-W03a: Vang Vieng Urban Renewal

Subproject V4: Vang Vieng Urban Renewal

Following the split of the original package W03 (V1-V4) into W03 (V1-V3) and W03a (V4), the bidding documents and safeguards documents for package W03a (subproject V4) would be updated and finalized during Q2 2023 subject to the physical completion of Contracts TIIGP2-LAO-W02 and TIIGP2-LAO-W03 being 50% as recommended by the ADB during the Midterm Review mission in May 2022. This is now the case and planning for W03a has re-started aiming for an issuance of an invitation for bids by October 2023, contract award by April 2024 and commencement of works by July 2024.

TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements (Subproject V1)

During Q2 2020, a stakeholder consultative meeting on Draft Design for the subproject Nam Ngum Reservoir Access Improvements (V1) was held. The Detailed Engineering Design (DED), incorporating feedback from the consultation meeting, was submitted to MICT and ADB and was cleared by ADB in Q3 2020. The invitation for Bids (IFB) for this Package was published on 18th September 2020, with a submission deadline and bid opening on 30th October 2020.

ADB issued NOL to the BER on 20 April 2021. The Letter of Acceptance was issued on the same day to the Contractor. The contract was awarded on 26th April 2021. The site possession was given on 4th June 2021. The Notice to Proceed (NTP) was given on 16 June 2021 with commencement of works from 1st July 2021. The period of performance is 731 calendar days, and the intended completion date is therefore 30th June 2023.


The Works for TIIGP2-LAO-W02 Consists of:

- Construction of a 1,200m² parking area which has a capacity of 4 buses and 34 cars and an overflow parking area, which has a capacity of around 27 cars.

- Improving the existing public marina to safely accommodate 50 to 60 local tour boats and launch small recreational vessels, e.g. kayaks and sailboats;
- Renovation of the existing walkway into a friendly walking path and boardwalk, with view decks and a step landscape allowing visitors to relax, improve the accessibility of disable.
- Redevelopment of unsanitary and poorly constructed market stalls and small shops/restaurants into new 3,860m2 public market and shop houses that incorporate Lao traditional architectural design
- Construction of five private pavilions, and one iconic circular pavilion, which is the landmark of this recreational area.
- Installation of septic tanks in all public buildings and a wastewater pump out station/ holding tank at the marina, wetland treatment and Construction new site storm drainage and slope protection
- Improve domestic water supply by construction new treatment tank.
- Install new outdoor lighting, landscape fixture and waste bins.
- Construction access road and install of floating ferry dock.
- Construction of 32 Nos of Shop houses

The overall implementation progress, as of 30th June 2023 was 60.51% against the schedule of 100.00%. However, the outstanding works of 39.49% will be completed within the extended period of 12 months from 1st July 2023 to 30th June 2024.

During this report period of April-June 2023, 8.42% of works progress made against 23.96% planned. The progress of works was delayed due to (i) lack of resources at site for landscape and buildings marina works; (ii) delay in construction fill slope at marina because of lack of stone for gabion terramesh; (iii) high water level of marina which stopped working on circular pavilion; (iv) delay in installing the drainage works for access road; and (v) delay in building works particularly Public Plaza construction, Circular Pavilion Construction, and shophouses.

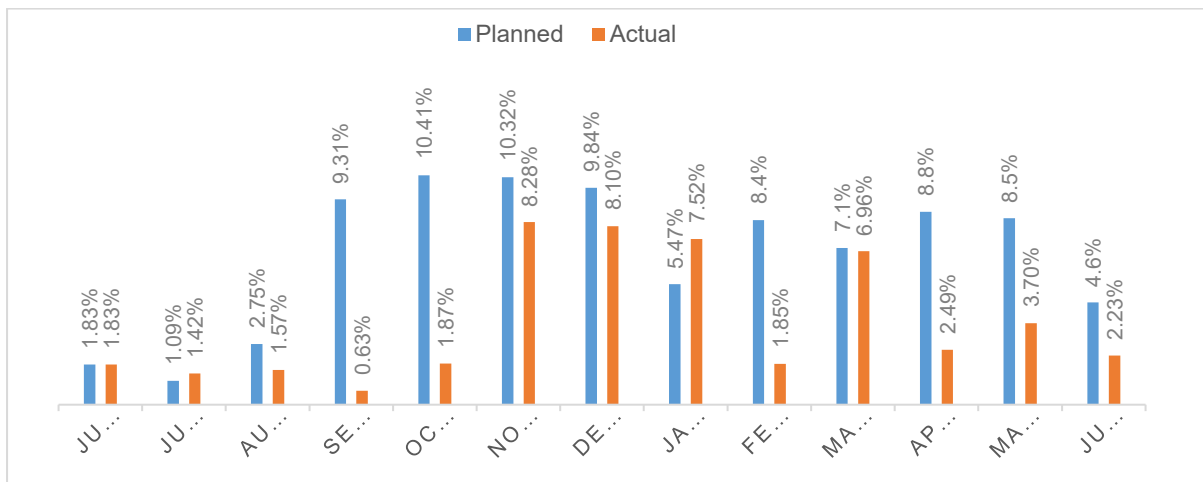

During the reporting period, the Contractor carried out (i) the general provision related to the contractor's and the engineer's facilities; (ii) the installation of U-ditches (cast-in-situ U-ditches); (iii) RC pavement; (iv) Cast-in-situ Road Kerb; (v) stone loose ripap for slope protection of internal access road AL-03 to Circular Pavilion; (vi) fill slope protection by using Terramesh system along the internal access road AL-02; (vii) the construction of foundation of shophouses Types A, B, C and D; (viii) the construction of concrete deck slab for Circular Pavilion; (ix) the construction of Stairs ST-02, ST-03, ST-5 and ST-06 ; and (x) the construction of intake pumphouse for water supply system.

The PMCES team joined with the ADB Midterm Review Mission in the field on 19 May 2022 and suggested to terminate this Contractor if the progress continues to slide further till 31st

July 2022 and no improved performance is being achieved. The Contractor provided (i) Updated Recovery Plan; (ii) Updated Resources Plan and (iii) Updated Priority List agreement to execute the Works. The EA starts monitoring the performance of the Contractor bi weekly basis.

The detailed work progress of each major activity, as of the end of this reporting period, are given below:

1. Landscape Marina was 23.95% completed
2. Buildings Marina was 17.23% completed
3. Road Improvement was 82.26% completed
4. Roadside Drainage system was 68.80% completed

The Contractor was continuing with implementing the 14-priority action plans (agreed in June 2022) and the progress status, as of the end of this reporting period, is summarized below:

- 4 - actions fully completed (100% completed)
- 2 – actions partially completed (more than 85%)
- 8 – actions significantly delayed – Not completed (more than 40% or above)

The overall progress of works was behind the schedule (the revised work program) delayed due to (i) **Road Works:** The Works commenced from the 1st of July 2021 and the clearing and grubbing of Road Works were impossible due to pick up of the rainy season. The Contractor could do only temporary and preparation works until the end of October 2021 as no earth movement was possible, which caused a delay of 4 months, (ii) **Soil Disposal:** The Local authority including PONRE approval for the designated soil disposal area was delayed from October 2021 until April 2022 which delayed the sub-grade works of the access road, causing a 6 months delay, (iii) **Marina Works:** The site possession was delayed until April 2022, 10 months delayed due to updating of the resettlement plan, (iv) **The COVID-19 pandemic** and lockdown in Lao PDR since the 24th of April to the 30th of October 2021 all factories, logistics, and laborers were forced to stop by the local government authorities to prevent spread of COVID-19, and as a result only some construction activities could be carried out on-site subject to materials provision which delayed activities planned during this 6 months period, (v) **Design Changes:** Due to change of the cut and fill slope of the marina, we could not start the marina buildings and landscaping works until September 2022, causing a 5 months delay, (vi) **Water Level of Marina:** Due to high water level, we could not start the fill slope of the marina until March 2023 which was a 6 months delay, (vii) **Consequences of Force Majeure:** The Contractor is prevented from performing its substantial obligations under the Contract by Force Majeure of which notice has been given, therefore, the Contractor proceedings was slow over 6 months period, (viii) **Rock Exploration:** Interrupted supply of rock due to lack of rock at the marina site with 10km hauling distance caused delay of works 3 months from March to May 2023 and (ix) **the Contractor's poor planning**, inadequate resources management and slow performance.

With reference to MICT letter dated 22 June 2023 and the agreements reached during the mid-term review mission from 16 May to 6 June 2022, ADB provided no objection to the propose contract variation No.1 on 28th June 2023 to extend the contract's intended completion date by 365 days, from 1 July 2023 to 30 June 2024, to enable the completion of the remaining 41.7% of works with no cost implication and unchanged total contract amount.

The original detailed engineering design of the Contract was done in 2020. When the contract commenced in July 2021, the Contractor carried out topographical survey of the existing ground and prepared the constructional/working drawings. During the Consultant's review of the working drawings as per the ground prevailing condition, some of the parameter of the soil properties were not the same as per design. For these unforeseen circumstances, it was found out that the factor of safety was not adequate against slope stability, should we follow the DED. Therefore, during the implementation of Civil Works under this package, there was site adaptation works as a basis of revisions. In addition of ground conditions, the DED failed to

address some of the resettlement issues which required either design modification or additional design as per the Revised Resettlement Plan.

The Variation Order No.1 is cost implication to the project due to modification of design for (i) the slope stability against overturning and sliding for both the marina and access road, (ii) extension of Kitchen behind the shop houses, (iii) quantities missed in the BoQ, and (iv) construction of the MPS temporary Facilities, and (v) Additional rock transportation cost outside of the project area. Due to the above factors, it changes the quantities of some work items in Bill No. 1: General Provisions, Bill No. 2: Landscape Marina, Bill No. 3: Building Marina and Bill No. 4 Road Improvement. The summary of Variation Order is as follow:

Bill No.	Original Contract, USD	Revised Contract, as per VO-1, USD	Difference , USD
Bill No. 1: General Provisions	158,560.00	170,660.00	12,100.00
Bill No. 2: Landscape Marina	959,903.28	2,073,356.94	1,113,453.66
Bill No. 3: Building Marina	819,067.15	987,148.47	168,081.32
Bill No. 4: Road Improvement	2,173,320.43	2,351,256.74	177,936.31
Bill No. 5: Pipe Culverts	124,418.68	124,418.68	-
Bill No. 6: Dayworks Provisional Sum	9,335.13	9,335.13	-
Sub-Total (Bill No. 1 to Bill No. 6)	4,244,604.67	5,716,175.96	1,471,571.29
Contingencies 10%	424,460.47	424,460.47	
Total of Contractor's Bill and Contingency	4,669,065.14	6,140,636.43	1,471,571.29

The proposed Variation Order will be needing additional USD 1,471,571.29 which is 31.52% of the original contract value. It changes of the original quantities of few work items in Bill No.1: General Provisions, Bill No. 2: Landscape Marina, Bill No. 3: Building Marina and Bill No. 4: Road Improvement keeping contingency amount in the same as previous USD 424,460.47.

Based on the additional cost, the total contract amount in US dollars will increase by USD 1,471,571.29, from USD 4,669,065.14 to USD 6,140,636.43. The VO were submitted in 22nd June 2023. ADB is in the process of reviewing this proposal, its justifications and its cost implications.

Progress Status of 14-Priority Action Plans as of 30th June 2023

Priority	Srl	Discussion points	Action by Khamfong Group (KFG)		Target as of 30 June 2023	Progress as of 30 June 2023	Progress Status	Justification
			Date: Start	Date: End				
	I	Access Road-1 (Sta. 3+500 to Sta. 6+372)						
1	1.1	Earth Works -Common Excavation: 64,887.47 m ³ -Embankment: 2,963.30 m ³	Start: 1-June-2022 End: 1-October-2022	100.00%	100.00%	In Progress	Total Length=2.83 Km	
2	1.2	Drainage Works (Side Drain + RC Pipe Culvert)	Start: 18-June-2022 End:15-December-2022	100.00%	78.00%	Delay	Total Length= 4,967m, Completed= 3,912m=> Remaining= 1055m	
3	1.3	Sub-base Materials Mixing -Soil 60% -Gravel 40%	Start: 4-June-2022 End: 15-November-2022	100.00%	100.00%	In Progress		
4	1.4	Concrete Pavement -Length 2,872 m -Width 6 m -Thickness 0.175 m	Start: 15-September-2022 End: 15-December-2022	100.00%	92.00%	Delay	Total Length= 2,827m, Completed= 2,607m=> Remaining= 220m	
	II	Access Road-2 (Sta. 0+000 to Sta. 3+500)						
5	2.1	Earth Works -Common Excavation: 84,117.30 m ³ -Embankment: 3,112.00 m ³	Start: 1-October-2022 End: 1-January-2023	100.00%	100.00%	In Progress		
6	2.2	Drainage Works (Side Drain + RC Pipe Culvert)	Start: 15-November-2022 End: 15-March-2023	100.00%	62.00%	Delay	Total Length= 3,000m, Completed= 1,860m=> Remaining= 1140m	
7	2.3	Sub-base Materials Mixing -Soil 60% -Gravel 40%	Start: 15-January-2023 End: 15-April-2023	100.00%	100.00%	In Progress		
8	2.4	Concrete Pavement -Length 3,500 m -Width 6 m -Thickness 0.175 m	Start: 25-February-2023 End: 25-May-2023	100.00%	85.00%	Delay	Total Length= 3,500m, Completed= 2,985m=> Remaining= 515m	
	III	Landscape Marina						
9	3.1	Slope protection & Drainage	Start: 15-June-2022 End: 15-December-2022	100.00%	75.00%	Delay	Cut Slope Protection 275m (behind Shop House) Completed = 80% and Fill Slope Protection 320 m (Namngum Riverside) Completed= 20%	
10	3.2	Step Landscape	Start: 18-June-2022 End: 18-February-2023	100.00%	19.00%	Delay		
11	3.3	Circular Pavilion	Start: 15-June-2022 End: 15-March-2023	100.00%	34.40%	Delay		
12	3.4	Public Plaza	Start: 15-June-2022 End: 15-February-2023	100.00%	38.00%	Delay		
13	3.5	Shophouse	Start: 1-August-2022 End: 1-May-2023	100.00%	15.00%	Delay		
14	3.6	Internal Road	Start: 1-December-2022 End: 30-June-2023	100.00%	50.00%	Delay		

The PMCES national Resident Engineer continued supervising the construction work on site to assist PIU/DICT of Vientiane Province.

The project was continuously implementing the preventive measures for the COVID -19 in accordance with the Prime Minister’s Office Order No.06/PM regarding COVID-19 regulations. In response, the Contractor was taking safety measures of the COVID-19 Pandemic prevention including detailed specific measures to ensure health and safety for workers and inhabitants of the sub-project area were developed and included in the Contractor Environmental Management Plan (CEMP) which is being implemented at site.

The following activities being carried out by the contractor during the reporting period are given below:

Works executed in Q2 2023 (April – June 2023)

Item	Description	Unit	Rate (USD)	April-June 2023		
				Quantity	Amount (USD)	Progress
BILL No. 01 GENERAL PROVISIONS					6,990.00	
102	General Obligation					
102-1	Maintenance of Road, Bridges and Culvert	month	410.00	3.00	1,230.00	
102-3	Maintenance of Traffic	month	200.00	3.00	600.00	
103	Contractor's Establishments			-	-	
103-2	Maintenance of Contractor's Establishments	month	820.00	3.00	2,460.00	
104	Facilities for the Engineer			-	-	
104-2	Maintenance of Main Office and Facilities including administration	Month	300.00	3.00	900.00	
104-15	Maintenance of Vehicles including Driver and Fuel	Vehicle Month	500.00	3.00	1,500.00	
105	Testing and Control			-	-	
105-2	Maintenance of Main/Field Laboratory	month	100.00	3.00	300.00	
Bill No. 2: Landscape Marina					109,725.53	
	The slope protection hill side at landscap marina	LS	211,275.14	0.01	2,142.00	
	The riverbank protection (Fill slope) at landscap marina	LS	354,321.02	0.16	56,520.00	
405	MINOR DRAINAGE STRUCTURES			-	-	
405-3	U-RC Open Ditch Storm Drainage Size: W0.5xD0.7-1.0mx0.15m (Wall Thickness), Including MH@35-40m	Metre	60.00	9.00	540.00	
701-3	Stair ST03	LS	19,268.96	0.20	3,800.00	
701-4	Stair ST04	LS	34,048.52	-	-	
701-5	Stair ST05	LS	15,572.50	0.29	4,500.00	
701-6	Stair ST06	LS	21,088.65	0.81	17,098.73	
704	WASTE WATER AND WATER SUPPLY			-	-	
704-1	Intake Pump House	LS	24,135.86	0.23	5,483.90	
802E	Septic Tank Cap. 6.4m3/day of Shop house (Total 3 no.)	LS	26,187.84	0.75	19,640.90	
Bill No. 3: Building Marina					52,852.78	
802B	Shop house type A	LS	195,091.48	0.03	6,123.36	
802B	Shop house type B	LS	166,156.40	0.08	13,550.26	
802B	Shop house type C	LS	134,035.31	0.06	7,669.31	
802B	Shop house type D	LS	63,621.81	0.05	3,418.17	
804	CIRCULAR PAVILION	LS	107,226.97	0.21	22,091.68	
Bill No. 4: Road Improvement					223,386.00	
300	PAVEMENT WORKS			-	-	
313-1	Sand Layer	Metre Cube	4.10	120.00	492.00	
	Plastic Sheet	m2	0.50	2,400.00	1,200.00	
314-2	Reinforced Concrete Pavement, 175 mm thick (Class 30Mpa)	Metre Square	29.00	3,870.00	112,230.00	
404	DITCHES, APRON PROTECTION, INLET AND OUTLET STRUCTURES			-	-	
404-4	Stone Masonry (Replac construction by reinforceconcte U-ditch)	Metre Cube	36.00	2,250.00	81,000.00	
507-1	Concrete Slab from Kerb to Side drain(C 20MPa, Thickness= 0.08 m)	Metre Cube	90.00	60.00	5,400.00	
607-4	Precast Concrete Kerb	Metre	3.75	1,328.00	4,980.00	
	Slope Protection for the Access road Km 1+400 by Gabion Box	LS	130,082.35	0.14	18,084.00	
Total Executed Amount					392,954.31	8.42%

TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements (subprojects V2, V3)

During the period of Q2 2020, a stakeholder consultative meeting on draft design for the subprojects Kaeng Yui Waterfall Access Improvements (V2), Western Loop Rural Access Road and Bridge Improvements (V3), Vang Vieng Urban Renewal (V4) was held. The Detailed Engineering Design (DED), incorporating feedback from the consultation meeting, was submitted to MICT and ADB and was cleared by ADB the last reporting period. The invitation for Bids (IFB) for this Package was published on 1 October 2020, with a submission deadline and bid opening on 12 November 2020. The BER was approved on dated 15 July 2021. The contract was awarded on 23 July 2021. The Notice to Proceed (NTP) was given on 24th August with commencement of works from 1st September 2021. The period of performance is 731 calendar days, and the intended completion date is therefore 1st September 2023.

The Works for the updated TIIGP2-LAO-W03 Package (Subprojects V2 and V3) consists of:

Key Scopes	V2	V3	Total
Road Rehabilitation in Km	6.0 (Rigid pavement)	26.595 (Flexible pavement/DBST)	32.595 km Pavement
Pipe culverts Nos.	12 (5 nos. of 600 dia., 2 nos. of 800 dia., 4 nos. of 1000 dia., 1 no. of 1200 dia.)	52 (20 nos. of 600 dia., 11 nos. of 800 dia., 13 nos. of 1000 dia., 8 no. of 1200 dia.)	64 nos. pipe culverts
Causeway Culvert Nos.	1 (with sluice gate)	3	4 nos.
New Bridge	NA	1 no. bridge of 3 spans (27.9 x 3 = 83.70m) simply supported pre-stressed concrete I-girder bridge of deck width 11.6m	1 no.
Nos. of Bridge Repair	1 no.	3 nos.	4 nos.
Existing bridge slope protection	2 nos.	3 nos.	5 nos.
Retaining Wall (m)	60m	NA	60m
Breast Wall (m)	520m	540m	1,060m
Roadside Drains	V-shaped unlined, Lined trapezoidal and RCC Rectangular	V-shaped unlined, Lined trapezoidal and RCC Rectangular	
Landscape and building	<ul style="list-style-type: none"> - Renovating dining pavilions, kitchen, public toilet - Building changing hut - Renovating suspension bridge - Building 2 arch bridge in reinforced concrete - Improving forest walkway (trekking and stone stairs) - Construction of new view deck near waterfall 	<ul style="list-style-type: none"> - Remove existing deck and its support - Install new decking and support frame - Install new railing 	

The overall implementation progress, as of 30th June 2023, was 56.27% against the revised schedule of 96.41%.

During this reporting period of April - June 2023, 10.31% of works progress made against 20.61% planned. The overall progress was delayed because of (i) lack of proper resources at site (manpower and equipment) and poor planning, (ii) delay in static load test for the bored


piles of the bridge work, and (iii) delay in daily progress of construction work particularly earthworks and drainage works.

During the reporting period, the contractor carried out (i) the general provision related to the contractor’s and the engineer’s facilities, (ii) the preparation works on site such as survey work, laboratory testing (base course materials testing, and RC pipe culvert compressive strength test) (iii) shop drawings, (iv) road maintenance, (v) RC drain work (cast-in-situ U-ditches, installation of U-ditches; (vi) RC pipe culverts with apron protection, Inlet and outlet for RC pipe culverts, (vii) the construction of 3 causeways on Western Loop Rural Access Road-R1; (viii) the construction of Base course for Western Loop Rural Access Road-R2; (ix) the trial pavement of 300m long on Western Loop Rural Access Road-R1 including Prime Coat MC70 and first sealing coat AC80/100; (x) the surface treatment for Western Loop Rural Access Road-R2 (first sealing coat), (xi) Repairing of existing Bailey bridges on Road R1&R2 including Abutment protection; (xii) Earthwork for Kaeng Yui access road at Km 5+600-5+850, and (xiii) the RC pavement of Kaeng Yui Access Road; (xiv) the construction of foundation and column of Public Toilet at Kaeng Yui landscape; (xv) the completion of Bridge No. 01 and the construction of Bridge No. 03 at Kaeng Yui landscape; (xvi) the construction of Pier P2 for Nam Xong bridge; and (xvii) cast-in-situ I-girders for Nam Xong bridge.

The PMCES team joined with the ADB progress review mission in the field on 16th November 2022 and the ADB suggested to keep monitoring the progress continuously. The mission team suggested to terminate this Contractor if there is no progress of bored pile static load test of Nam Xong bridge done till 31ST December 2022, no progress of environmental and safety measures and no improved performance is being achieved.

- NamXong bridge: if no progress by end of Dec 2022, reduce the scope and rebid.
- W03: Renovation of existing NamXong bridge: reduce the scope due to budget limitation, suggests to explore PPP arrangement.
- Add 2 new bridges to Kaengyui Waterfall Access Road and to process contract variations in Mar 2023 if satisfactory progress.

The average physical progress executed by the contractor during this reporting period is 3.44% against the average planned rate of 6.87% as detailed progress shown in the below chart.

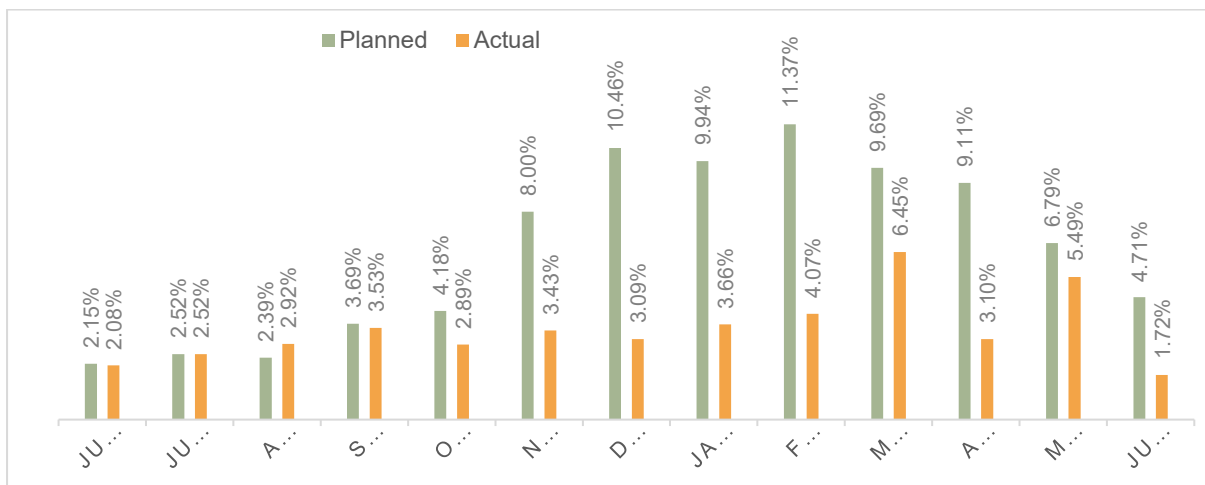

The detailed work progress of each major activity, as of the end of this reporting period, are given below:

1. V2-subproject: Kaeng Yui Waterfall Access Improvements was 60.37% completed
2. V3-subproject: Watern Loop Rural Access Road Improvements was 53.87% completed
3. Nam Xong Bridge construction was 51.79% completed

Regarding the Health and Safety measurement, the following activities were being implemented by the Contractor on site during the reporting period are:

- Emergency and first aid drill conducted, safety procedure plans are being implemented and monitored.
- CEMP revision completed.
- Prepared a health and safety handbook and Emergency contact of project site
- Conducted construction toolbox meeting regularly by contractor
- Develop safety procedures and measures for hazardous construction activities and Conducted the Hazard Assessment Training.

The Contractor was also continuing with implementing the 11-priority action plans (agreed in June 2022) and the progress status, as of the end of this reporting period, is summarized below.

11 Priority Action List agreed in the Management Meeting No. 08 dated 5th May 2022						
Items	Discussion points	Who/ Take	When/ action will be taken	Target as of 30th June 2023	Actual Progress as of 30th June 2023	Progress Status
1	Earth Works	Contractor	Continue: 5 May 2022 to 30 January 2023	KY: 100% WL: 100%	<ul style="list-style-type: none"> • Kaeng Yui: 100% • Western Loop: 93.0% 	Completed (96.5%)
2	Bored pile load test: Static Tests – 2 Nos • High strength Dynamic Test – 2 Nos • PIT Test – 28 Nos • Sonic Test – 28 Nos	Contractor	Start: 19 May 2022 to 11 June 2022	100%	<ul style="list-style-type: none"> • Static load: 100% • High strength Dynamic Test: 100% • PIT Test: <ul style="list-style-type: none"> – Abutment A1 – 8 Nos: 100% – Abutment A2 – 8 Nos: 100% – Pier P1 – 6 Nos: 100% – Pier P2 – 6 Nos: 100% • Sonic Test: <ul style="list-style-type: none"> – Abutment A1 – 8 Nos: 100% – Abutment A2 – 8 Nos: 100% – Pier P1 – 6 Nos: 100% – Pier P2 – 6 Nos: 100% 	Completed
3	Pile cap construction: – 1 st Group (A1+P1) – 2 nd Group (P2+A2)	Contractor	Start: 25 May 2022 to 17 June 2022	100%	<ul style="list-style-type: none"> – Abutment A1: 100% – Abutment A2: 100% – Pier P1: 100% – Pier P2: 100% 	Completed
4	Exposed unfinished U-Drain or Cover Drain Construction	Contractor	Continue: 6 May 2022 to 1 st week of June 2022	100%	<ul style="list-style-type: none"> • Kaeng Yui: 100.0% • Western Loop: 98.0% (Km 17+940 ~ 18+820 L/S, R/S) 	Completed
5	Pipe Culvert Construction both subprojects	Contractor	Continue: 5 May 2022 to 31 July 2022	100%	<ul style="list-style-type: none"> • Kaeng Yui: 94.12% <ul style="list-style-type: none"> – Total 17 locations – Completed 16 locations • Western Loop: 89.75% <ul style="list-style-type: none"> – Total 78 locations – Completed 70 locations 	Completed (92%)
6	Sub-base Construction – WL & KY	Contractor	Continue: 12 May 2022 to 28 March 2023	KY: 100.0% WL: 100.0%	<ul style="list-style-type: none"> • Kaeng Yui: 100% <ul style="list-style-type: none"> – Total 6.0 km – Completed 6.0 km • Western Loop: 93.0% <ul style="list-style-type: none"> – Total 26.0 km – Completed 24.0 km 	Completed (96.5%)
7	Base Course Construction - WL	Contractor	Start: 15 May 2022 to 10 April 2023	100.0%	<ul style="list-style-type: none"> • Western Loop: 64.00% <ul style="list-style-type: none"> – Total 26 km – Completed 24.0 km of 1st layer, 100 mm THK & 9.3 km of 2nd layer, 100 mm THK. 	Uncompleted (36.0%)
8	Pavement Concrete - KY	Contractor	Start: 25 May 2022 to 31 December 2022	100.0%	<ul style="list-style-type: none"> • Kaeng Yui: 91.66% <ul style="list-style-type: none"> – Total 6.0 km = 36,000 m2 – Completed 5.5 km full width W=6.0 m 	Completed (91.66%)
9	Landscape - KY	Contractor	Continue: 5 May 2022 to 30 August 2023	Landscape:96.0% Building: 98.0%	<ul style="list-style-type: none"> • Landscape Work: 13.65% • Building Work: 56.80% 	Uncompleted (64.70%)
10	Health & Safety	Contractor	Continue: 5 May 2022		85.0%	In progress
11	Revision of overall work programme + Resources Plan + S - Curve:	Contractor	Submission: 12 May 2022	100%	100%	Completed

Works executed in Q2 2023 (April – June 2023)

Item	Description	Unit	Rate (USD)	April 2023 to June 2023		
				Quantity	Amount (USD)	Progress
BILL No. 01 GENERAL PROVISIONS					7,258.88	
100	General Provisions					
102	General Obligations					
102-1	Maintenance of Roads, Bridges and Culverts	Month	1,000.00	3.00	3,000.00	
102-3	Maintenance of Traffic	Month	250.00	3.00	750.00	
103	Contractor's Establishments					
103-2	Maintenance of Contractor's Establishments	Month	150.00	3.00	450.00	
104	Facilities for the Engineer					
104-2	Maintenance of Main Office and Facilities including administration	Month	150.00	3.00	450.00	
104-15	Maintenance of Vehicles including Driver and Fuel	Vehicle Month	200.00	3.00	600.00	
105	Testing and Control					
105-2	Maintenance of Main / Field Laboratory	Month	200.00	3.00	600.00	
107	General Environmental & Social Impact Requirement					
107-2	Implementation of Contractor Environmental Management Action Plan (CEMAP)	Lump Sum	3,612.50	0.15	541.88	
107-4	Public Consultation During Construction Phase	Lump Sum	5,780.00	0.15	867.00	
BILL No. 1: LANDSCAPE FOR KAENG YUI					1,970.00	
200	EARTH WORKS					
201-1	Clearing and Grubbing	Metre Square	0.23	1,591.75	366.10	
400	DRAINAGE AND CULVERT WORK					
405-1	U-RC Storm Drainage Size: W6.4x D0.6m x 0.10m (Wall Thickness) With RC-Cover 12Cm Thk, Including MH - for Overflow Parking	Metre	16.83	95.30	1,603.90	
BILL No. 2: BUILDING FOR KAENG YUI					11,478.88	
703	Kitchen					1,075.47
703-A	Architecture					
703-A.1	Masonry Wall and Plastering (Specification Division 4)					
703-A.1.1	Clay brick masonry wall 100mm thick, with water repellent coating	Square Metre	7.27	147.98	1,075.47	
705	PUBLIC TOILET					7,841.68
705-S	STRUCTURE					
705-S.1	EARTH WORKS (SPECIFICATION DIVISION 31)					
705-S.1.5	Sand filling including pouring water and compaction under slab	Metre Cube	6.50	71.40	464.28	
705-S.4	BEAM WORKS (SPECIFICATION DIVISION 3)					
705-S.4.1	1st FLOOR BEAM WORKS					
705-S.4.1	Concrete Grade 15 MPa (for lean concrete under beam)	Metre Cube	72.68	2.00	145.35	
705-S.4.2	Concrete Grade 25 MPa	Metre Cube	179.78	8.00	1,438.20	
705-S.4.3	Steel reinforcement DB14 Grade SD40	Tonne	726.75	0.80	581.40	
705-S.4.4	Steel reinforcement DB12 Grade SD40	Tonne	726.75	0.30	218.03	
705-S.4.5	Steel reinforcement RB6 Grade SR24	Tonne	726.75	0.20	145.35	
705-S.4.6	Tie Bar	Kilogram	6.12	25.00	153.00	
705-S.4.7	Formwork	Metre Square	11.48	100.00	1,147.50	
705-S.5	1st FLOOR SLAB WORKS (SPECIFICATION DIVISION 3)					
705-S.5.1	Concrete Grade 25 MPa	Metre Cube	179.78	6.40	1,150.56	
705-S.5.2	Steel reinforcement DB10 Grade SD40	Tonne	726.75	0.90	654.08	
705-S.5.3	Tie Bar	Kilogram	6.12	13.10	80.17	
705-S.5.4	Plastic sheeting	Metre Square	0.88	73.20	64.40	
705-S.3.7	1st FLOOR COLUMN WORKS					
705-S.3.7	Concrete Grade 25 MPa	Metre Cube	179.78	6.25	1,123.59	
705-S.3.8	Steel reinforcement DB14 Grade SD40	Tonne	726.75	0.14	107.75	
705-S.3.9	Steel reinforcement RB6 Grade SR24	Tonne	726.75	0.10	72.68	
705-S.3.10	Tie Bar	Kilogram	6.12	3.30	20.20	
705-S.3.11	Formwork	Metre Square	11.48	24.50	281.14	

Item	Description	Unit	Rate (USD)	April 2023 to June 2023		
				Quantity	Amount (USD)	Progress
CAUSEWAY CULVERT-1 CH: 2+578					5,420.73	
204	CONSTRUCTION OF EMBANKMENTS					
204-2	Embankment from Borrow Materials	Mette Cube	3.44	156.00	537.03	
402	PIPE CULVERTS					
402-8	Reinforcing Steel in Headwalls, Wing-walls and Aprons	Tonne	726.75	0.80	581.40	
507	STRUCTURAL CONCRETE					
507-4	Concrete Grade 30 (for Headwall, Apron, Encasing etc.)	Mette Cube	110.00	14.43	1,587.30	
602	SLOPE PROTECTION and MASONRY STRUCTURES					
602-1	Loose Rip-rap Slope Protection	Mette Cube	24.30	50.00	1,215.00	
602-2	Grouted Rip-rap Slope Protection	Mette Cube	30.00	50.00	1,500.00	
CAUSEWAY CULVERT-2 CH: 5+783					49,110.65	
204	CONSTRUCTION OF EMBANKMENTS					
204-2	Embankment from Borrow Materials	Mette Cube	3.44	250.00	860.63	
402	PIPE CULVERTS					
402-5	Pipe Culvert, 1200/1250 mm diameter	Mette	216.00	48.10	10,389.60	
402-8	Reinforcing Steel in Headwalls, Wing-walls and Aprons	Tonne	726.75	9.18	6,671.57	
507	STRUCTURAL CONCRETE					
507-4	Concrete Grade 30 (for Headwall, Apron, Encasing etc.)	Mette Cube	110.00	283.54	31,188.85	
CAUSEWAY CULVERT-3 CH: 6+777					63,431.77	
204	CONSTRUCTION OF EMBANKMENTS					
204-2	Embankment from Borrow Materials	Mette Cube	3.44	250.00	860.63	
402	PIPE CULVERTS					
402-5	Pipe Culvert, 1200/1250 mm diameter	Mette	216.00	61.75	13,338.00	
402-8	Reinforcing Steel in Headwalls, Wing-walls and Aprons	Tonne	726.75	9.30	6,758.05	
507	STRUCTURAL CONCRETE					
507-1	Concrete Grade 15 (for minor unreinforced concrete works)	Mette Cube	95.00	30.00	2,850.00	
507-4	Concrete Grade 30 (for Headwall, Apron, Encasing etc.)	Mette Cube	110.00	354.86	39,034.60	
602	SLOPE PROTECTION and MASONRY STRUCTURES					
602-1	Loose Rip-rap Slope Protection	Mette Cube	24.30	24.30	590.49	
BILL No. 5: BRIDGE FOR WESTERN LOOP					108,855.25	
506	STEEL REINFORCEMENT					
506-1	Steel Reinforcement	Tonne	726.75	49.44	35,932.16	
507	STRUCTURAL CONCRETE					
507-5	Concrete Grade 40 (for precast post-tensioned girders)	Mette Cube	200.00	190.26	38,062.40	
507-8	Concrete Grade 35 (for pile caps, piers, pier cap, abutments, return wall, dirt wall, retaining walls and approach slabs, pedestal, stopper etc.)	Mette Cube	200.00	137.25	27,450.00	
508	PRESTRESSING OF CONCRETE					
508-1	Prestressing Steel	Tonne	726.75	9.11	6,620.69	
Total Executed Amount					828,524.13	10.32%

The PMCES Resident Engineer and two Supervisors were continuously working on site for supporting/assisting the PIU/UDAA Vang Vieng District in inspecting and supervising all of the ongoing construction works for V2&V3 subprojects. The PMCES supervision team were also following-up the daily implementation progress and addressing the issues as required.

The project was continuously implementing the preventive measures for the COVID -19 in accordance with the Prime Minister's Office Order No.06/PM regarding COVID-19 regulations. In response, the Contractor was taking safety measures of the COVID-19 Pandemic prevention including detailed specific measures to ensure health and safety for workers and inhabitants of the sub-project area were developed and included in the Contractor Environmental Management Plan (CEMP) which is being implemented at site.

Status of Stage-2 Works Packages:


Sub-project W02	Status at start	Present Status	Outstanding Works
TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements • V1: Nam Ngum Reservoir Access Improv	<ul style="list-style-type: none"> • Preliminary design • IEE/EMP drafted • RP drafted • IP drafted 	<ul style="list-style-type: none"> • Conceptual design prepared and confirmed following consultation with stakeholders on 15 August 2019 and 16 September 2019 • Technical Engineering Survey both Topographical and Geotechnical completed on 29 February 2020 • Updated FS cost on 31 March 2020 • DED and BD Submission by PMCES on 28 July 2020 • ADB No Objection to the DED on 14 August 2020 • DED clearance certificates by DPWT/ Vientiane Province on 04 September 2020 • ADB No Objection to the Bidding Document on 16 September 2020 • ADB No Objection subject to condition to the IEE and EMP on 17 September 2020 • IFB issued on 18 September 2020 • ADB No Objection to the RP on 25 September 2020 • Bid opening, on 30 October 2020 • DED clearance certificates by DPWT/Vientiane Province on 04 September 2020 • Environmental Compliance Certificate (ECC) on (IEE/EMP) by PONRE/Vientiane Province on 	<ul style="list-style-type: none"> • Further update the IEE and EMP based on outcome of design modification by Q3 2023; • Public Consultation regarding DED modification by Q3 2023 • Approval of Modified DED by Q3 2023 • Approval of Variation order for additional work by Q3 2023 • Compensation completion report (CCR) and closure report by Q3 2023 • Second Evaluation of the Contractor's performance on 14-

Sub-project W02	Status at start	Present Status	Outstanding Works
		<p>07September for the period of 01 September 2020 to 31 August 2021</p> <ul style="list-style-type: none"> • GRM training for PIU and the resettlement committee conducted on 07 December 2020 • Public consultations conducted at the village level with project beneficiaries and affected households on dated 08 Dec 2020; • Obtain the government's approval on the use of the protected forest areas on 11 Dec 20 • Further updated the IEE and EMP based on outcome of these consultations to the ADB on 29 December 2020 • ADB No objection to updated IEE/EMP dated on 26 January 2021 • ADB Disclosed updated IEE/EMP on the Website dated on 26 February 2021 • The National Regulatory Authority (NRA) office did the UXO survey issued a certificate of no risk of UXOs at site for the Nam Ngum Access Improvement subproject on 11 March 2021 • ADB No Objection to the BER on 20 April 2021 • The Letter of Acceptance was issued on 20 April 2021 • The Contract was signed on 26 April 2021 • The site possession was given on 4 June 2021 • Kick-off meeting was conducted on 2nd April 2021 • The Notice to Proceed (NTP) was given on 16th of June 2021 with commencement of works from 1st of July 2021 • CEMP Training for the Contractor was conducted on 26 August 2021 • CEMP monitoring training was conducted during 25-26 November 2021 by the PMCES Environment Specialists. • ADB No Objection to the Revised RP on 29 March 2022 • Compensation to AHs in Marina was fully implemented in April 2022 • Soil disposal area was confirmed/approved in April 2022 by DONRE • Site possession to the Marina was given on 22 April 2022 with commencement of marina works from 6th May 2022 • CEMP was approved in May 2022 • ADB MTR Mission visited the project site on 19th May 2022 • ADB approved SMR No. 5 and disclosed on 27 Dec 2022 including accident Report • Variation Order No. 01 was submitted on 22 June 2023 to ADB for consideration and approval • ADB provided no-objection on 28 June 2023 to the Variation Order No.01 related to the Extension of the Intended Completion Date until 30 June 2024 	<p>priority action plans by Q3 2023</p>

Sub-project-W03	Status at start	Present Status	Outstanding Works
<p>TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western</p>	<ul style="list-style-type: none"> • Preliminary design • IEE/EMP drafted • RP drafted • IP drafted 	<ul style="list-style-type: none"> • Conceptual design prepared and confirmed following consultation with stakeholders on 16 August 2019 and 17 September 2019 • Technical Engineering Survey both Topographical and Geotechnical completed on 29 February 2020 	<ul style="list-style-type: none"> • Continue with approving of Shop-drawings by Q3 2023 • Continuation of RC Pipe Culverts

Sub-project-W03	Status at start	Present Status	Outstanding Works
<p>Loop Rural Access Road and Bridge Improvements</p> <ul style="list-style-type: none"> • V2: Kaeng Yui Waterfall Access Improvements, • V3: Western Loop Rural Access Road and Bridge Improvements, 		<ul style="list-style-type: none"> • Updated FS cost on 31 March 2020 • DED and BD Submission by PMCES on 07 August 2020 • ADB No Objection to the DED on 24 September 2020 • ADB No Objection to the EGDRP on 28 September 2020 • ADB No Objection subject to conditions to the IEE and EMP on 29 September 2020 • ADB No Objection to the Bidding Document 29 September 2020 • IFB issued on 01 October 2020 • Bid opening on 12 November 2020 • DED clearance certificate by DPWT/Vientiane Province on 04 November 2020 • The Governor of Vang Vieng District issued a certificate of no risk of UXOs at site for the Western Loop Rural Access Road and Bridge Improvements subproject on 16 December 2020 • GRM training for PIU and the resettlement committee conducted (Vang Vieng District) on 14 December 2020 • Public consultations with affected people conducted on 15 and 16 December 2020 • Compensation Payment to the affected people on dated 16 December 2020 • IEE/EMP Safeguard is updated and submitted by PMCES on 12-Feb-2021 based on outcome of additional consultations and pending approval from ADB • The Sang Seng Xor 1 Division of Army office at Vang Vieng District who did the UXO survey issued a certificate of no risk of UXOs at site for the Kang Yui Waterfall subproject on 18 February 2021 • Environmental Compliance Certificate (ECC) on (IEE/EMP) by PONRE/Vientiane Province on 07April for the period of 01 April 2021 to 31 March 2022 • Government assurances regarding /CB Works Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements on 7 July 2021 • ADB No Objection to the BER on 15 July 2021 • The Letter of Acceptance was issued on 20 July 2021 • The Contract was signed on 23 July 2021 • The Notice to Proceed (NTP) was given on 24th August with commencement of works from 1st of September 2021 • The site possession was given on 03 September 2021 • Kick-off meeting was conducted on 03 September 2021 • CEMP monitoring training was conducted on 29 November 2021 by the PMCES Environment Specialists. • The 28 Nos of Bored Pile Construction completed by 10th of April 2022 • ADB MTR Mission visited the project site on 20th May 2022 • ADB approved SMR No. 5 and disclosed on 27 Dec 2022 including accident Report 	<p>installation by Q3 2023</p> <ul style="list-style-type: none"> • Continuation of DBST by Q3 2023 • Updated IEE/EMP for ADB endorsement and disclosure on ADB website by Q3 2023 • Compensation completion report (CCR) and closure report by Q3 2023 • Approval of Variation order for additional work by Q3 2023 • Second Evaluation of the Contractor's performance on 11-priority action plans by Q3 2023

Overall progress of Output 1 implementation as of Q2 2023 is 70.49% against 97.21% planned. Detailed progress of Output 1 civil works subproject implementation as of 30 June 2023 is summarized in Annex 1.

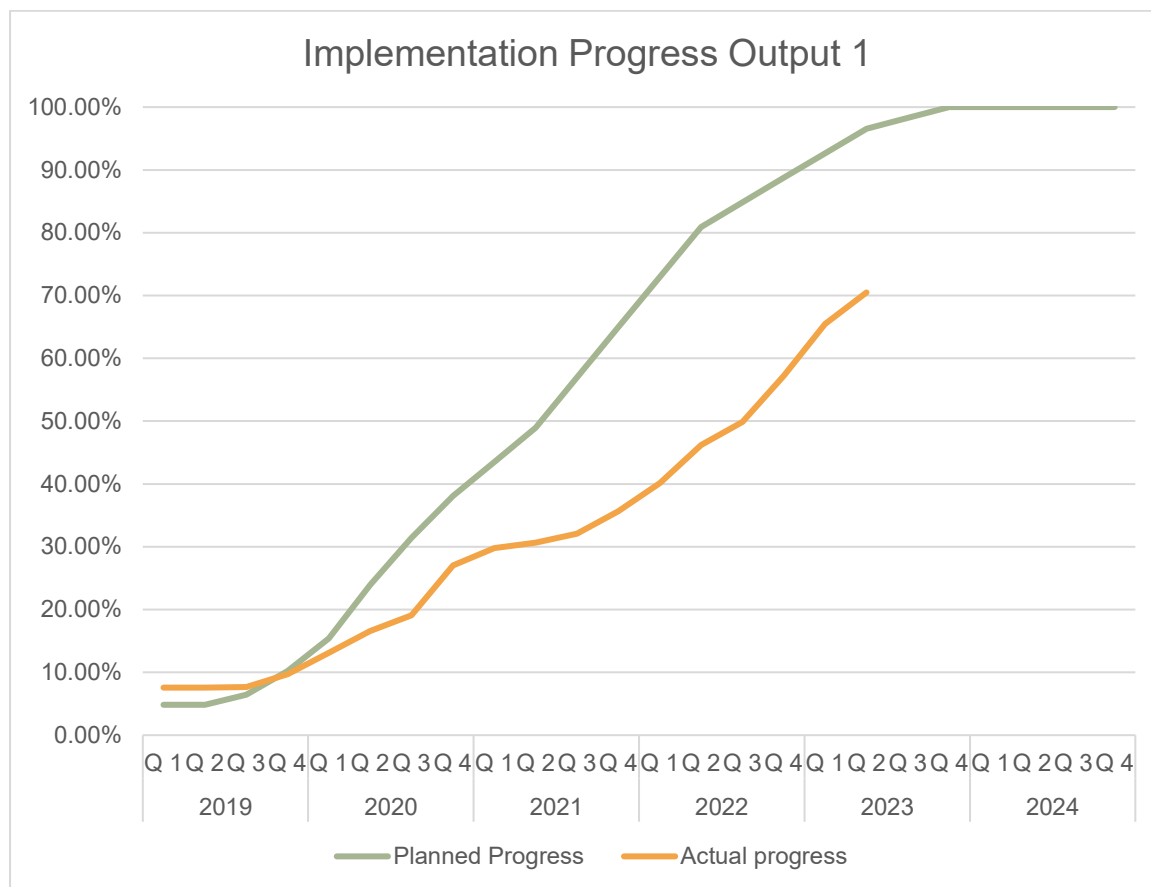

Output 2: Capacity to implement ASEAN Tourism Standards strengthened

Output 2 will: (i) support the ASEAN Tourism Standards national implementation by establishing and strengthening certification bodies and assessment frameworks, promoting and facilitating adoption of the standards by the tourism sector, and establishing sustainable financing mechanisms; and (ii) support the implementation of selected ASEAN Tourism Standards and the ASEAN Sustainable Tourism Awards.

There are seven ASEAN Tourism Standards currently being applied in Lao PDR: (i) Clean Tourist City; (ii) Homestay; (iii) Community-Based Tourism; (iv) Public Toilet; (v) Green Hotel; (vi) Spa Service; and (vii) Meetings, Incentives, Conferences and Exhibitions (MICE). In addition, Lao PDR also implements the ASEAN Sustainable Tourism Awards (ASTA).

Six of the seven Standards have been adapted to the Lao context and one is applied in the original ASEAN format (Green Hotel Standard). The MICE Standard is broken down into three sub-categories of Meeting Rooms, Exhibition Venues and Event Venues. These three are currently being adapted to the Lao context.

As per the rules governing the use of ASEAN Standards, each ASEAN Member State can make minor modifications to each Standard in order to reflect the local context. These can be awarded as ASEAN Standards by member countries at the Asian Tourism Forum once every two years (Green Hotel, Clean Tourist City, MICE Venue, MICE Special Events and ASTA, in even years and Homestay, Public Toilet, Spa Services and Community Based Tourism in odd

years). There is no limit to the number of ASEAN Standard certificates that can be issued in each country.

There are however limits set by the ASEAN Secretariat for the number of certificates that can be awarded at the annual ASEAN Tourism Forum (ATF). This showcases certificates that have been awarded by each country. Quotas apply for each Standard in order to keep the ATF award ceremony manageable. The ATF awards covering the Project's timeframe are as follows:

Year	Award per Country	Total	Host
2022	Green Hotel (5) Clean Tourist City (3) ASTA (2) MICE Venue (5) MICE Special Events (5)	20 per country	Cambodia
2023	Homestay (5) Public Toilet (5) Spa Services (5) Community Based Tourism (3)	18 per country	Indonesia
2024	Green Hotel (5) Clean Tourist City (3) ASTA (2) MICE Venue (5) MICE Special Events (5)	20 per country	Laos

Implementation of the ASEAN Tourism Standards in Laos is subject to: (i) translation into Lao; (ii) adaptation to become a Lao – ASEAN Tourism Standard; (iii) translation into English; (iv) approval by the Tourism Vice Minister; (v) publication; (vi) preparation of assessment and certification manuals; (vii) dissemination to National and Provincial Assessment Committees; (viii) training of trainers; and (ix) training of all members of Assessment Committees and National Steering Committees. Once these assessment frameworks are in place and operational, the standards will be widely promoted within the sector to encourage implementation leading to certification.

Progress of ASEAN Tourism Standards Implementation Capacity Strengthening:

As of 31 December 2022

ASEAN Tourism Standard Adaptation	ASEAN Standard							
	Clean Tourist City	Homestay	Community-Based	Public Toilet	Green Hotel	Spa Service	MICE	ASTA
Translation of ASEAN Tourism Standards into Lao language	√	√	√	√	√	√	√	√
National ASEAN Tourism Standard adaptation	√	√	√	√	x	~	√	x
Publication of Lao language version of National or ASEAN Tourism Standard	√	√	√	√	√	√	√	√
Translation of National Tourism Standard into English language	√	√	√	√	x	~	√	x
Approval of adapted Standards by Minister	~	~	~	~	x	~	~	x
Awareness / dissemination workshops with National and Provincial Assessment Committees (ASEAN and adapted standards)	√	√	√	√	√	~	√	~
Publication of adapted standards in Lao and English language	√	√	√	√	x	~	√	x
Preparation of assessment and certification manuals	√	√	√	√	√	~	√	~
Training of national-level assessor trainers	~	~	~	~	~	~	~	~
Training of national-level assessors	~	~	~	~	~	~	~	~
Training of provincial/district-level assessors	~	~	~	~	~	~	~	~
ASEAN Tourism Standard promotion	~	~	~	~	~	~	~	~

ASEAN Tourism Standard Adaptation	ASEAN Standard							
	Clean Tourist City	Homestay	-Based Community	Public Toilet	Green Hotel	Spa Service	MICE	ASTA
ASEAN Tourism Standard implementation support	√	√	√	√	√	√	√	√

√ = completed; ~ = ongoing; x = not required

2.1 National ASEAN Tourism Standards adaptation

All of the ASEAN Tourism Standards for Community Based Tourism, Homestay, Public Toilets, Clean Tourist City, MICE Meeting Room and Spa Services have been adapted to become Lao Tourism Standards. The Green Hotel Standard will be applied in an unmodified form. The Tourism Vice Minister has yet to approve all of the Lao Tourism Standards that have been adapted. Until the Lao Tourism Standards are approved by the Vice Minister, the Project's intention is to continue using the full ASEAN Tourism Standards (also refer 2.4 ASEAN Tourism Standards Promotion).

2.2 Establishment of certification bodies and processes

National and Provincial Steering Committees (also known as Certification Bodies) have been established to guide and certify ASEAN Tourism Standards. At the provincial level, there is one Certification Body/Committee covering all tourism standards. Provincial Committees coordinate with National Standards Committees during the certification process.

The composition of national and provincial level Certification Bodies was adjusted in 2021 to increase participation by women. This is now completed with 41% participation by women, on average, across all Certification Bodies.

2.3 Assessor Training

As of 30 June 2023, there are 12 (5 women) ASEAN Master Trainers within MICT who will continue to train trainers and assessors from the national and provincial Assessment Committees / Certification Bodies. There is also 62 National Trainers (34 women) and 106 Provincial Trainers (38 women), 94 National Assessors (48 women) and 106 Provincial Assessors. This provides the capacity considered necessary to achieve most, if not all, of the Output 2 DMF targets. Training will continue in the second half of 2023, focusing on building the capacity of assessors at provincial level.

2.4 ASEAN Tourism Standards promotion

The status of promotion of the standards as end of Q2 2023 is as follows:

- Further input is required from the private sector to raise awareness and increase the uptake of the ASEAN Tourism Standards. The benefits of being certified need to be discussed and agreed with the industry before any financing mechanism can be put in place.
- The Tourism Standards website is expected to be finally launched in September, 2023. Once the adapted Standards for Lao have been approved by the Vice-Minister, these will be uploaded to the website.

2.5 ASEAN Tourism Standards and ASEAN Sustainable Tourism Awards implementation

Although the earliest awards of ASEAN Tourism Standard certifications date back to 2008, over 70% of certifications have occurred since 2012. Due to a possible misunderstanding of the need to re-certify every 2 to 3 years, there is a high number of certificates that have expired in the Project Provinces:

Category	Certified since 2008	Expired	Valid	DMF Target
Green Hotel	32	24	8	64
Homestay providers*	45	0	45	113
Clean Tourist City	2	0	2	3
Community Based Tourism (CBT)	4	0	4	-
Public Toilet	16	3	13	-
MICE all categories	5	3	2	-
Spa Services	6	2	4	-
ASEAN Sustainable Tourism Award	6	4	2	-

Notes:

* Homestay providers include 42 certified under Homestay Standard and 3 under the CBT standard

An ongoing priority for 2023 is to re-certify all expired certificates for Green Hotel, Homestay and Clean Tourist City Standards. Getting Vang Vieng City ready for certification to ASEAN Clean Tourist City Standard in 2026 is also a priority for the 2023 and 2024 work plans. A process of self-assessment by expired award-holders, with quality control checks by the EA, was agreed as the best way to fast-track the re-certification process and potentially attain the DMF targets (refer Annex 3).

Laos was awarded 35 ASEAN Tourism Standards at the 2023 ASEAN Tourism Forum in Indonesia. As a result, progress towards the DMF targets for Output 2 have been updated for this quarter as well as targets re-set for project completion. These are presented in the following table:

	Clean Tourist City			Green Hotel			Homestay		
	Plan for 2024/25	Cert*	Balance	Plan for 2024/25	Cert*	Balance	Plan for 2024/25	Cert*	Balance
Luang Prabang	1	1	0	27	13	14	55	19	36
Vientiane Province	0	0	0	5	1	4	18	0	18
Vang Vieng	1	0	1	13	4	9	24	8	16
Champasak	1	1	0	22	14	8	36	18**	18
Total	3	2	1	67	32	35	133	45	88
DMF Target	3			64			113		

Notes


* 'Cert' = Certified and includes expired certifications that are being renewed

** Includes 15 certified under Homestay Standard and 3 under the CBT Standard

The certification cycle for Green Hotels and Homestays is every two-years. The next and final opportunity to certify new Green Hotels and Homestays, and re-certify those that are expired, is in 2024. If the project is extended by 1 year, there is another opportunity in early 2026 to certify additional Green Hotels and Homestays and still be included in the project's completion report.

Annex 11 includes an overview of certifications for ASEAN Tourism Standards since 2008.

Overall progress of Output 2 implementation as of Q1 2023 is 84.3% against 92.6% planned. Annex 2 includes a complete overview of Output 2 activities implemented during Q1 of 2023. The DMF, in Annex 3, also includes progress updates on Output 2 activities.

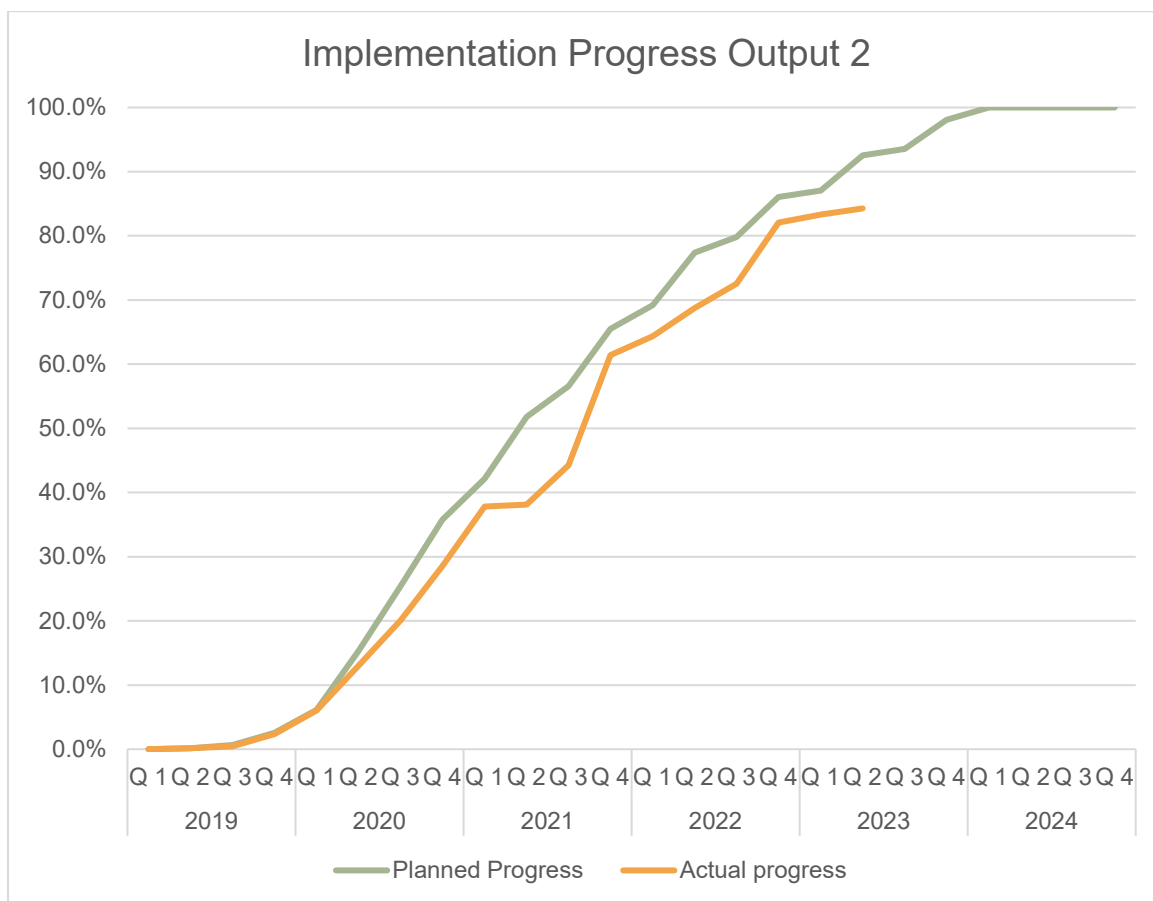

Output 3 progress: Institutional capacity for tourism destination management and infrastructure O&M strengthened

Output 3 will: (i) build capacity among public and private stakeholders in the tourism sector to sustainably develop, manage, and market tourist destinations; and (ii) build capacity for infrastructure operation and maintenance (O&M) through the preparation of O&M plans and training to implement the plans.

The project is supporting the establishment and capacity building of destination management networks (DMNs) for: Lao PDR (National DMN), Luang Prabang Province, Southern Laos (incl. Champasak, Sekong, Attapeu and Salavan Provinces), Vientiane Province and Vang Vieng Town.

3.1 Destination Management Network Institutional Strengthening
3.2 Destination Management Plan Preparation

These two activities will: (i) establish and strengthen destination management networks (DMNs) for joint public-private destination planning and raise destination management practices to international standards, (ii) build capacity within these DMNs to strengthen/develop comprehensive destination management plans (DMPs); and (iii) strengthen policies and procedures needed to ensure the effective implementation of DMPs, including through joint implementation of Output 2 and 3 activities.

The DMNs for Lao PDR, Luang Prabang and Southern Laos, supported under the TIIGP1, were reviewed and membership was updated, and new DMNs for Vientiane Province and Vang Vieng were established in 2019. Strengthening of DMNs is ongoing through training and exchanges. DMPs, including action plans, for all five target destinations were completed during Q4 2019 and published in Q1 2020.

The national-level DMN was also restructured to be better prepared to facilitate the implementation of the DMP and the public and private sector action plan. All DMN memberships were reviewed and updated to improve the gender balance to ensure gender targets of the project (30 % of DMN managers and 40% of DMN membership are women) are met.

During the course of the project, significant progress has been made regarding effectiveness of the national level DMN to fulfil its envisioned role to direct joint public-private destination planning and address issues faced by the tourism industry. This is partially due to adopting the first two recommendations made in a 2015 ADB-commissioned report entitled “Establishment of a National Tourism Destination Management Network in Lao PDR”, which recommends that (i) the DMN is co-chaired by a senior MICT official and a representative from the private sector, and (ii) that issue papers are prepared prior to the DMN meetings to ensure structured discussions can be held to explore and agree on policy interventions to facilitate the industry. Was the DMN initially chaired by a MIC official only, as of 2022, it has a co-chair from the private sector, illustrating the trust that has been built through the earlier period of collaboration in the framework of the DMN. Moreover, were issues raised by the private sector at DMN meetings initially ad hoc, during more recent public-private sector consultation meetings, issues papers were prepared outlining pertinent concerns from the private sector as well as the public sector to facilitate the discussion between public and private sector DMN members and representatives from other, related government offices invited based on the issues to be discussed, and development partners.

During Q2 of 2023, DMN meetings were held in Champasak province, Luang Prabang province and at national level. The purposes were to review the 2023 DMN action plan implementation progress and plan for the 2nd semester of 2023. In Champasak and Luang Prabang provinces, the DMN action plans include participation in and organization of local tourism promotional events, regional and international travel trade fairs, implementation of ASEAN tourism standards and skills development. The draft Laos tourism marketing campaign plan for Visit Laos Year 2024 was also presented at the national DMN meeting.

3.3 Policy, Regulation and Master Planning Support

This activity supports the work on tourism policy in the framework of the DMNs, the development of subregional, national and provincial/local-level tourism regulations and national-level tourism standards not covered by the ASEAN tourism standards, and the preparation and implementation of tourism master plans for project supported destinations.

DMN Policy Taskforces meet regularly to identify and discuss policy issues affecting tourism sector in project target destinations. Recent focus has been on plans for post-COVID-19 recovery, easing visa requirements for target markets etc.

Tourism masterplanning work for the project target areas of Siphandone, Nam Ngum 1 Reservoir and Luang Prabang City commenced in Q4 2019 but was delayed as a result of the COVID-19 pandemic. Following the country re-opening post-COVID-19 in May 2022, work continued. However, in response to an urgent request from the Government the project agreed to support updating of the Vang Vieng tourism masterplan. Contracts with the tourism masterplanning consultants were amended to include this task. As a result, the focus of tourism masterplanning work during the second half of 2022 and the first half of 2023 was on completing the Vang Vieng masterplan update, and is now shifting back to complete the plans for Luang Prabang (integrated with a Tourism Management Plan requested by UNESCO), Nam Ngum and Siphandone. It is expected that this work will be completed by Q2 2024.

3.4 Destination Marketing and Promotion Support

This activity supports destination marketing and promotion, with a strong emphasis on public-private collaboration. It includes support for market research, branding, print and online promotion, including the use of social media, familiarization programs, and participation in tourism forums and trade events. Training for DMN members, including implementation of ASEAN guidelines for promotional materials, will also be provided.

Destination marketing activities were included in the public and private sector action plan on destination management for 2021, 2022 and 2023.

During Q2 of 2023, support was given through DMN mechanisms to public and private sector in participating in BITE (Beijing International Tourism Expo) in China during 16 – 18 June 2023. See Travel Trade Fair Participation Result below. Public and private stakeholders have been informed about upcoming travel trade fairs, including Thai Tiew Thai in Aug, ITE Ho Chi Minh, CITIE China, and Adventure Travel World Submit in Sep, ITB Asia in Singapore in Oct, WTM London in Nov and ITB Berlin in Mar 2024. The project has been working closely with the tourism marketing department in coordination with target participants and event organizers. Further, a Laos tourism marketing campaign plan for Visit Laos Year 2024 has been developed in consultation with public and private stakeholders, and content will be prepared in Aug and the campaign plan will be executed in Q3-Q4 of 2023. ATF 2024 will be featured as part of the campaign. Key local tourism events have been identified in the national and project target area DMN action plans, the support is being given to the public and private sector in preparing the events, including Pakse Half Marathon in Sep, cycling promotional event between Cambodia and Lao PDR at Don Det-Don Khone in Sep, Luang Prabang Ultra Trail in Oct, Luang Prabang Ngam Tae Oh in Oct, and Vang Vieng Half Plus Marathon in Dec 2023.

Travel Trade Fair Participation Results

No.	Travel Trade Fairs	Number of Businesses from Laos	Name of Businesses from Laos	Number of Meetings	Number of clients who have been provided information after the events	Number of Contracts made during / after the events
1	ITB Asia Singapore, 16 - 22 Oct 2022	5	1) Inthira Group 2) Namkat & Nam pien 3) Exo Travel 4) Discover Laos 5) Salana Hotel	81		
2	ATF in Indonesia, 02 - 05 Feb 2023	4	1) Lao Boutique Travel 2) Crowne Plaza Hotel 3) Landmark Hotel 4) Laotel Hotel			
3	BITE in China, 16 - 18 June 2023	4	1) Laos - China Railway Co., 2) Champamai Travel / Tad Yeuang 3) Green Discovery 4) Namkat & Nam Pien	500		1
Total		13		581	0	1

3.5 Heritage Interpretation Support

This activity is supporting DMNs to carry out: (i) cultural and natural heritage research and interpretation, including the development of heritage trails, signage, leaflets, guidebooks, maps and digital interpretation; and (ii) heritage guide training.

Heritage interpretation strategies for Siphandon (Champasak), Luang Prabang Town and Environs, Vientiane Province and Vang Vieng Town and Environs, finalized during Q2 2020, were designed and printed. Implementation was scheduled to commence in Q1/2 2021. Key tourist sites and routes in the project target areas were prioritized based on the heritage interpretation strategies in Q1 2021.

During Q2 of 2023, the 1st batch of Luang Prabang heritage interpretation panel texts in Lao language has been proof-read, the contents are being reviewed and will be approved by Luang Prabang DICT / PIU in Q3. The 2nd and 3rd batches are being written by the interpretation specialist. Contents for directional signposts for the 4,000 Islands have been prepared and share with Champasak PIU, contents will be finalized in Q3, signs will be designed, produced and installed by Q4. See timeline below.

Heritage Interpretation Key Tasks and Timelines

No.	Project Target Areas	2023		2024
		Q3	Q4	
1	Luang Prabang Town and Environs			
	Interpretation panels			
	- Finalize 1 st batch contents in English and Lao			
	- Design 1 st batch panels			
	- Develop and finalize 2 nd and 3 rd batch contents			
	- Translation and finalize 2 nd and 3 rd batch contents			
	- Produce and install			
	Directional signposts			
	- Finalize contents			
	- Design, produce and install			
2	4,000 Islands (Focus on Don Ded, Khone, Khong)			
	Interpretation panels			
	- Develop and finalize contents in English and Lao			
	- Design, produce and install			
	Directional signposts			
	- Finalize contents			
	- Design, produce and install			
3	Vientiane Province (selected attractions)			
	Interpretation panels			
	- Develop and finalize contents in English and Lao			
	- Design, produce and install			
	Directional signposts			
	- Finalize contents			
	- Produce and install			
4	Vang Vieng Town and Environs (selected attractions)			
	Interpretation panels			
	- Develop and finalize contents in English and Lao			
	- Design, produce and install			
	Directional signposts			
	- Finalize contents			
	- Produce and install			

3.6 Tourism-related SME development

This activity is providing tourism-related SMEs in the project target areas with: (i) business planning, management and marketing training; (ii) hospitality services training; (iii) support for product diversification, quality and safety enhancement; (iv) equipment to improve hospitality services and product quality and safety; and (v) tourism marketing and business networking support.

During Q1 of 2023, further SMEs need assessments were conducted in the project target areas, during Q2 the SME development plan was drafted, discussed, and reviewed by PIUs

and will be finalized in Q3 of 2023. An SME database was developed, and 2019 – 2022 data is being entered by M&E specialists while the 2023 data and onwards will be added during implementation of the planned SME activities. The database will be consolidated and accessible online in Q3 of 2023. A summary report will be included in Q3 2023 quarterly report.

3.7 Establish and Maintain Internet-based Tourism Knowledge Repositories

This activity supports DMNs to establish Internet-based tourism knowledge repositories, including lists of DMN members and contact details, approved DMPs, DMN meeting reports, training materials, opportunities for financial and technical support, tourism statistics, and brand-related artwork, photo libraries, and standard copy promotional materials.

The Laos DMN website was developed in Q2 2021, (www.laos-dmn.com). Documents relevant for the sector, including DMN related document, will be uploaded to the site as they become available. During Q 4 of 2021, relevant documents and news were uploaded into the website, such as MICT Ministerial Agreement on National DMN structure, DMN action plan 2022, DMN and Country Reopening Preparation Committee meetings.

During Q2 of 2023, news and relevant documents from DMN meetings at national level and project target areas were uploaded into the www.laos-dmn.com and posted on its Facebook page and group.

3.8 Develop infrastructure O&M plans with sustainable finance mechanisms

This activity will facilitate preparation of O&M plans for all output 1 infrastructure, incorporating (i) preventative, regular, and emergency maintenance procedures; (ii) O&M staffing and training needs; (iii) administrative requirements; (iv) monitoring requirements and procedures; (v) sustainable income generating mechanisms to finance O&M (e.g. environmental charges or tourist entry fees); (vi) opportunities for public-private partnerships; and (vii) financial management procedures.

Subproject: Vang Vieng Solid Waste Management Improvements:

A site inspection was carried out at the end of June by the Institutional and Environment Team, and actions were agreed with the contractor. In the inspection report, a large number of issues were identified, including eight that present hazards that have high potential impact on health and safety; three hazards that have lower health and safety impacts; and six operational issues. A follow-up meeting was held in Vientiane by all consultants to discuss approaches to landfill cell management, management of leachate, rules for informal workers, improved construction site hygiene, and changes to unsafe working practices.

Institutional consultants continued to provide support to the Procurement team on technical aspects relating to the specifications and requirements for the purchase of equipment, noting the critical importance of obtaining key landfill equipment. It is understood that all procurement will not be undertaken in one batch. Institutional experts have raised concerns about this approach with respect to the timing (noting that final decisions on all equipment can't be made until the procurement of a PPP arrangement for the Materials Recovery Facility since the private operator is likely to invest in capital equipment in this facility, which will free up Project budgets for wider investment). The delay means that it is now challenging to bring UDAA into the direct management of the site, which is a lost opportunity as they could have been provided with support over the next year to become accustomed to managing landfill cells. Furthermore, the delay in procurement has critical impacts on the purchase of PPE, life-saving water equipment, and the purchase of a weighbridge, which is a key part of being able to generate waste data and also introducing landfill gate fees.

Subproject: Kaeng Yui Waterfall Access Improvements: A workshop was convened in May with the Vang Vieng local authorities, private investors, and the local community. The workshop included a series of presentations on the progress of the project and on institutional arrangements. The institutional presentation provided an outline of why tourism infrastructure is important; O&M plans; resources, human and financial capacity; key O&M tasks at Keang Yui; and different options for management of the site (public, private, community). A presentation was also given by the private sector (Green Discovery) on potential approaches and management of the site. Further work is now to be undertaken on proposed concepts for O&M.

Subproject: Nakasang and Don Det-Don Khone Access Improvements: The PMCES Consultants developed further concepts for institutional arrangements based on the earlier consultation held with the local authorities and communities in April 2023. A further round of consultations was held in June to seek agreement on the proposals. The local authorities agreed to the approach of using the private sector to run the car park in Nakasang; the Boat Association to manage the port area; the five Row Car Association to manage the old French Port; and private entrepreneurs to manage the locomotive shelter in Don Kon and the viewpoint at Hang Kon.

A draft O&M Plan has been developed for all sites under this sub-project. The draft O&M Plan includes chapters on the following: introduction to site facilities and project development; institutional arrangements (management and business models); operations and maintenance approaches and tasks for each site; capacity development; dispute resolution; and appendices that provide numerous forms for surveys and record keeping.

3.9 Facilitate Public-Private Partnerships for operations and maintenance.

This activity will: (i) prepare feasibility studies for the operation of public tourist facilities and ancillary services that have the potential to be privately managed under public-private partnerships (PPP); and (ii) establish service contracts, management contracts, and/or lease contracts with private entities through public tender.

Subproject V5: Vang Vieng Solid Waste Management Improvements:

Consultants supported the PPP Consultant, Stanley Boots, in his visit to Vang Vieng. This included arranging a meeting with private companies who already work on SWM in Laos, a meeting with the UDDA, and a visit to the landfill. A second meeting of all development partners engaged in solid waste management (SWM) work in Vang Vieng, which provided an opportunity for updates on projects and for the PPP specialist to get a broader understanding of the sector. A total of 18 participants attended (MICT PCU, PPP Specialist, ZeroWaste Laos, GIZ, SwissContact, GGGI, SETS/Laobiogas, Plan International (SUSTOUR Laos), Tourism Development departments of MICT, and public health consultants.


A bilateral meeting was also held with GGGI regarding more formal collaboration with their AMUSE Project. This includes the potential for looking at joint investment into wider SWM equipment and capacity needs, including collection. The GGGI will update their project ToR and share it with institutional consultants for comment.

3.10 Infrastructure O&M training

Subproject V5: Vang Vieng Solid Waste Management (SWM) Improvements: Consultants have supported engineers in the operations of site, including addressing the challenges of compacting wastes and managing leachate.

Overall progress of Output 3 implementation as of Q1 2023 is 58.4% against 80.9% planned. Implementation suffered some delays due to the travel restrictions during the COVID-19 pandemic. Since travel restrictions have been lifted, implementation has accelerated.

Annex 2 includes a complete overview of Output 3 activities implemented during Q2 of 2023. The DMF, in Annex 3, also includes progress updates on Output 3 activities.

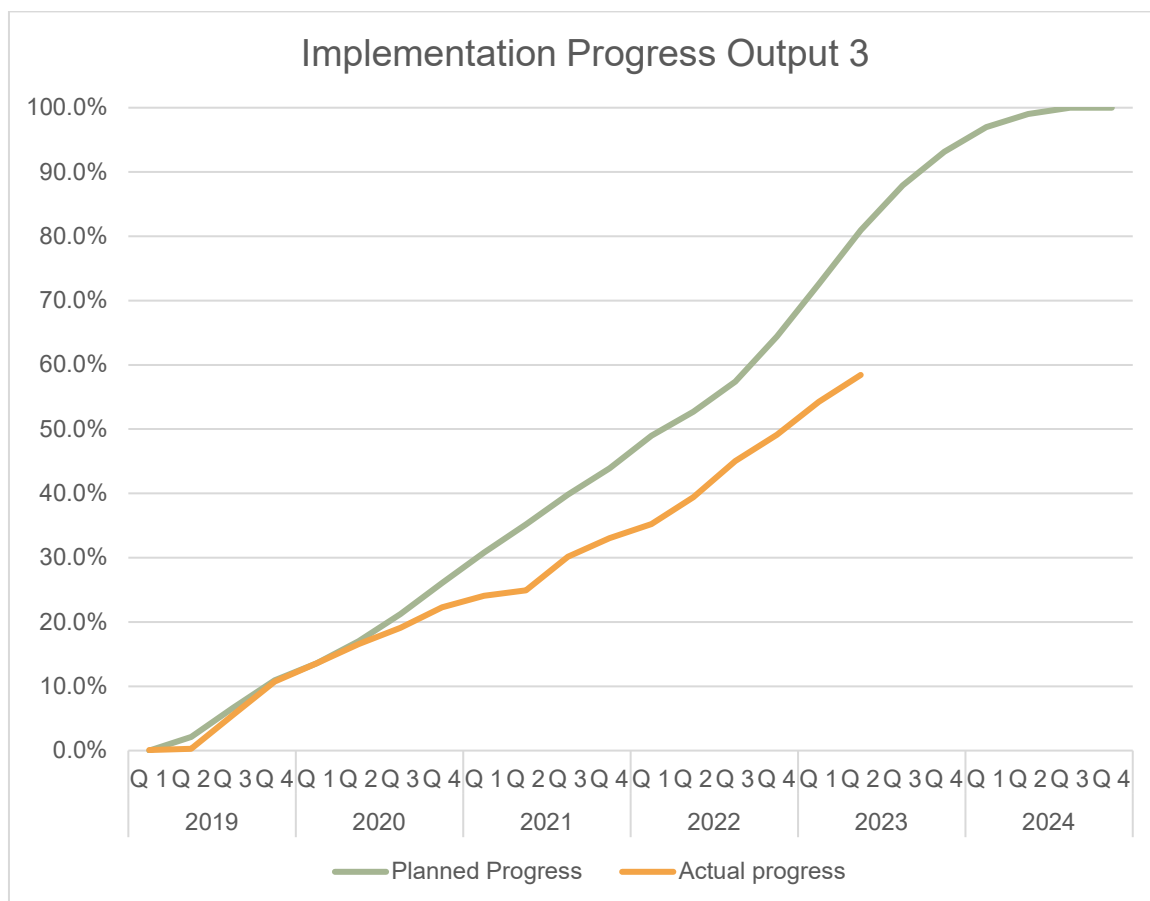

Progress towards realizing contributions to ADB Results Framework:

As of 30 June 2023

No.	Level 2 Results Framework Indicators (Outputs and Outcomes)	Targets (Lao PDR)	Methods / Comments	Actually planned / realized (Lao PDR)
1	Transport			
	a) Roads built or upgraded - provincial, district, and rural roads (kilometers)	62.6 km	Built or upgraded to concrete paving or double bituminous surface treatment.	Contract for Package TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements was signed on 30 December 2019. This package includes 21.11 km of improvement of access roads to tourist sites of which 21.11 km has been fully completed. Contract for Package TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements was signed on 26 April 2021 in Q2 2021. This package includes 7.3 km of concrete road of which 5.59km has been fully completed.

No.	Level 2 Results Framework Indicators (Outputs and Outcomes)	Targets (Lao PDR)	Methods / Comments	Actually planned / realized (Lao PDR)
				<p>Contract for Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements was signed on 23 July 2021. This package includes 6.00 km of concrete road and 26.6 km of DBST road totaling 32.6 km of road improvement of which 5.5 km of Kaeng Yui Access Road Concrete Pavement has been fully completed.</p> <p>Contract for Package TIIGP2-LAO-W03a: Vang Vieng Urban Renewal is scheduled to be signed in Q4 2023. The DED was prepared, and endorsed by ADB and has 0.67 km of concrete road and 0.39 km of DBST road totaling 1.05 km of road improvement.</p> <p>Contract Package for package TIIGP2-LAO-W04: Vang Vieng Landfill Improvements was signed 19 February 2021. It includes 1.55 km of access & internal roads of which 1.53 km has been fully completed.</p> <p>A total 63.5 km road will be improved under these 5 Civil Works packages.</p>
2	Water			
	a) Wastewater treatment capacity added or improved (cubic meters per day)	15.0 m ³	Septage treatment facility	<p>TIIGP2-LAO-W04: Vang Vieng Landfill Improvements was signed on 19 February 2021.</p> <p>This package includes 20m³/day septage sludge treatment facility.</p> <p><i>Additional wastewater treatment capacity under construction under Packages W02 and w03 (Kaeng Yui) will be quantified</i></p>
	b) Land improved through irrigation, drainage, and/or flood management (hectares)	24.5 ha		<p>Contract for Package TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements was signed on 30 December 2019. This package includes 0.5 ha catchment area of flood protection and drainage improvement.</p> <p>The contract for package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements was signed on 23 July 2021. This package includes 24 ha catchment area of flood protection and drainage improvement.</p>

No.	Level 2 Results Framework Indicators (Outputs and Outcomes)	Targets (Lao PDR)	Methods / Comments	Actually planned / realized (Lao PDR)
	c) Households with reduced flood risk (number)	5,132		<p>The project will construct flood protection and drainage for a total of 24.5 ha catchment.</p> <p>Packages TIIGP2-LAO-W01 contains flood management components with a catchment area of around 0.5 ha and TIIGP2-LAO-W03 will contain a 24.0 ha catchment area. Contract TIIGP2-LAO-W01 was awarded on 30 December 2019 and contract TIIGP2-LAO-W03 on 23 July 2021. Resulting number of households with reduced flood risk to be determined.</p>

ha = hectares, m³ = cubic meters, km = kilometers.

Performance monitoring:

The primary tool to monitor project performance is the Project Performance Management System (PPMS), which includes systems and procedures for the systematic collection of baseline, progress and endline data and to report progress towards the project's outcome and output targets defined in the project Design and Monitoring Framework (DMF) and implementation of project activities, gender equity results and data for economic and financial analysis and information needed to prepare photo stories and impact stories. A draft PPMS was prepared and submitted to ADB in April 2020. After several rounds of review, a final draft, incorporating ADB's comments, including feedback provided during the Mid-Term Review Mission, was submitted on 7 November 2022.

The PPMS, which was finalized with delay, describes data collection and reporting procedures and formats developed and implemented by the project alongside the PPMS development process. As a result, the PPMS documents these already existing and tested procedures. Refresher training recommended in the PPMS have been conducted for PCU and PIUs during Q2 2023.

The PCU is responsible for quarterly reporting on the performance of the project through quarterly progress reports to ADB against DMF targets and using the weighted project implementation table included in the PAM (updated from time-to-time). The DMF in the PAM contains outcome and output baseline and targets for Cambodia and Lao PDR combined. Progress towards DMF targets reported in the quarterly progress reports will reflect Lao PDR's contribution to these combined targets.

Progress as of 30 June 2023 towards DMF targets and activity implementation is presented in Annex 3. Note that the DMF has been enhanced with separate gender output indicators and expanded key activities reflecting PAM, and revised milestones matching the updated implementation plan. The updated implementation plan (reflecting latest, updated implementation schedule for all activities and revised assigned weights, provided by ADB) and weighted project progress as of 30 June 2023 are presented in Annex 4.

6. Financial Management

Disbursement Arrangement:

The Ministry of Finance has established a pass-through account for the grant to receive and track grant disbursements before passing funds on to the project's advance account. MICT has established an advance account in US Dollars for the grant at the Banque Pour Le Commerce Extérieur Lao Public (BCEL), which is exclusively used for ADB's share of eligible

expenditures. The four PIUs have set up project subaccounts for the ADB grant at local branches of the BCEL. Liquidation of the sub-accounts is subject to submission of full documentation to the PCU.

Advance Fund Procedure and Statement of Expenditure Procedure:

Upon approval of MICT's first Withdrawal Application and Estimate of Expenditure Sheet for ADB has disbursed \$1.0 million into the advance account on 2 April 2019. The PCU is using the Statement of Expenditure (SOE) procedure for the reimbursement of eligible expenditures or liquidation of advances to the advance account for individual payments up to \$100,000. As of 30 June 2023, the Project has spent the amount \$10.752 million through the advance account. The amount of \$0.431 million for March and April 2023 is still for ADB processing while the expenditure for May and June 2023 will be submitted to ADB soon. ADB has approved the increase in the ceiling of the advance account to \$1,500,000 on 4 December 2020 and to \$2,300,000 on 3 March 2022. As of 30 June 2023, the advance account including the PIU subaccounts have a balance of \$1.868 million.

Counterpart Fund:

The Government provides counterpart funds to finance government counterpart staff salaries and office space (in-kind). The cost of land acquisition and resettlement (in-cash) was originally also planned to be financed by the Government. However, in Q3 2020 it was agreed that LAR costs will be financed from the grant proceeds. The PCU will be responsible for: (i) preparing disbursement projections; and (ii) requesting budgetary allocations for counterpart funds. The counterpart contribution is recorded by the new accounting software.

Accounting:

The Project maintains separate books and records by funding source for all expenditures incurred on the project following international public-sector accounting standard for cash-based accounting and will prepare consolidated project financial statements in accordance with the government's accounting laws and regulations which are consistent with international accounting principles and practices.

The International and National Financial Management and Procurement Specialists (individual consultants engaged by MICT) are supporting procurement activities and have supported the PCU with the establishment of the financial management system, including the preparation of the Financial Management Manual (FFM) for the project, which was completed in December 2019. There were some revisions to the chart of accounts and attached an annex to the FMM. A Lao-language version of the FFM has been prepared by the Internal Auditor and was shared with the PIUs. The Project has procured an accounting software and is now operational. An excel based accounting system is still being used in parallel to record the Project financial transactions to ensure accuracy. The data from the excel based recording are exported to the accounting software on a monthly basis.

Auditing and Public Disclosure:

MICT has appointed an Internal Auditor (individual consultant) to oversee all project financial transactions and advise on measures to improve compliance with ADB and Government financial regulations and the project Financial Management Manual. He is also supporting PCU and PIU financial management staff prepare for annual external audits.

Annual project financial statements (APFS) are audited by the State Auditing Organization of Lao PDR (SAO). The first annual audit to cover the period 25 December 2018 to 31 December 2019 was submitted to ADB on 29 October 2020 after ADB's extension of the deadline to 31 December due to COVID-19. The audited project financial statements and auditor's opinion was disclosed in the ADB website on 18 November 2020. The audited financial statements for Fiscal Year 2020 were due for submission to ADB on 30 June 2021. Due to the COVID lockdown (started in April 2021), the Project in consultation with SAO requested for an

extension in submission to 30 September 2021. The 2020 APFS was submitted to ADB on 21 September 2021 and disclosed in the ADB website on 28 September 2021. The APFS for FY 2021 was submitted to ADB on 28 June 2022 and was disclosed on the ADB website. The financial statements for FY 2022 has been submitted to SAO in February 2023 and currently SAO is finalizing the audit, a bit late for June 30 2023 deadline.

Progress on implementation of the Project Financial Management Action Plan as of 30 June 2023 is presented in Annex 5.

7. Procurement

Procurement Plan:

The project's original 18-month Procurement Plan prepared during project preparation is included in the PAM (version 0, dated 22 May 2018). The Procurement Plan gets updated regularly. The latest version is Version 7, dated 18 March 2023, which was updated following the submission of the 2023 workplan to accommodate additional packages needed to implement to the approved 2023 annual workplan. The updated procurement plan was approved and disclosed by ADB on 18 March 2023.

Procurement of Goods, Works and Non-consulting Services:

During this reporting period, procurement for the following goods, works and non-consulting services contracts was completed and contracts signed:

Goods, Works and Non-consulting Services							
Contract Number	General Description	Estimated Value ^a	Contract Value ^a	Procurement Method	Advertisement Date	Date of ADB Approval of Contract Award	Comments

^a inclusive of taxes and duties

ICB = international competitive bidding; NCB = national competitive bidding; PCU = project coordination unit; PIU = project implementation unit; TBD = to be determined.

During this reporting period, procurement for the following goods, works and non-consulting service packages was initiated and is ongoing on 30 June 2023:

Goods, Works and Non-consulting Services						
Package Number	General Description	Estimated Value ^a	Procurement Method	Advertisement Date	Estimated Contract Award	Comments
TIIGP2-LAO-G04	Vang Vieng landfill management equipment (Landfill bulldozer and crawler type excavator)	\$325,000	NCB	4 April 2023	Q2 2023	Inclusive of taxes and duties.
TIIGP2-LAO-G04b-01	Vang Vieng Landfill Management Equipment (Solid Waste Collection Equipment)	\$99.750	Shopping	21 March 2023	Q2 2023	Inclusive of taxes and duties.
TIIGP2-LAO-G04b-06	General Equipment (Personal protective equipment)	\$14.620	Shopping	21 March 2023	Q2 2023	Inclusive of taxes and duties.

^a inclusive of taxes and duties

ICB = international competitive bidding; NCB = national competitive bidding; PCU = project coordination unit; PIU = project implementation unit; TBD = to be determined.

A goods and works procurement monitoring table is presented in Annex 6.

Recruitment and Utilization of Consulting Services:

During this reporting period, the following consultants were recruited and contracts signed:

Package Number	General Description	Estimated Value ^a	Contract Value ^a	Recruitment Method	Advertisement Date	Date of ADB Approval of Contract Award	Comments

^a Inclusive of income tax on fees and VAT on reimbursable expenses and provisional sums.

Recruitment of the following consulting services were ongoing on 30 June 2023:

Package Number	General Description	Estimated Value	Recruitment Method	Advertisement Date	Estimated Contract Signing Date	Comments

A consultant recruitment monitoring table is presented in Annex 7.

An overview of status of consulting services planned inputs and utilization to date is presented in Annex 8.

8. Safeguards Implementation and Submission of Semi-annual Integrated Safeguards Monitoring Report

Safeguards Implementation:

Environmental Safeguard Inspections

In the course of Q2 2023, the environmental specialists of PMCES Consultant undertook the following field inspections of the ongoing construction works:

Inspections by PMCES Environmental Specialists during the reporting period

	April 2023	May 2023	June 2023
W01			7-9 June
W02	5-April	4-May	28-June
W03	20-April	23-May	29-June
W04	21-April		30-June

Health and Safety Improvements:

During Q2 2023, the PMCES Consultant continued to implement the "Safety Improvement Plan" for all subprojects. PMCES Consultant introduced the contractors to the occupational health and safety hazard assessment checklist and risk assessment template that PMCES had developed in the previous quarter. The actions to be taken by the contractors to improve health and safety are gradually being implemented although at a slower pace than planned. The status of implementation is summarized below for each subproject, and a complete overview is included in Annex 13.

Package TIIGP2-LAO-W01: Subproject C1: Nakasang Access Road and Port Rehabilitation and Subproject C2: Don Det-Don Khone Access Improvements.

Environmental safeguards: The updated IEE and EMP for these two subprojects were approved by ADB in September 2019. With assistance from the PMCES Consultant, the contractor updated the CEMP, which was then approved by PCU on 06 December 2020 and submitted to ADB. The CEMP training for the contractor and the PIU was conducted on 21-23 December 2020.

The status of the roll-out of the contractor’s responsibilities under the safety improvement plan developed by the PMCES Consultant is summarized here below:

Activity	Progress	Plan
Confirm full time employment of an Environmental, Health and Safety Officer	Confirmed	
Conduct work hazard assessment at the construction sites and report the results to PMCES by 30 September 2022	May 2023	
Develop safety procedures and measures for hazardous construction activities and submit these to PMCES for review and approval not later than 10 October 2022		July 2023
Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors	Completed during Q4 2022 and Q1 2023	-
Undertake emergency response drill	Completed in Oct-2022	
Update the CEMP	June 2023	

The PMCES environmental specialist visited the subproject in June 2023. Overall, the contractor for each contract was implementing appropriate environmental, health and safety measures; however, there were some issues identified, and the contractor was instructed to make the necessary improvements:

- The camps, batching plant are in the closure status, and those sites rehabilitation, including the cleanliness, the full agreed hand-over site between the contractor and the land owner shall be prepared and submitted to the PIU/PMCES during July to August 2023.
- All the completed subprojects including Nakhasang and Don Det - Don Khone access roads, Nakhasang Port and other improvement sites shall be cleaned and handed over to PCU/PIU in July 2023.

Social safeguards: In Q2 2022 a Corrective Action Plan compensation phase 2 (CAP 2) was prepared, approved and implemented. Total amount of compensation paid under this final Phase 2 was 153,130,917 LAK. The social safeguard team prepared the Corrective Action Plan (2 phases) and Compensation Completion Report in Q3 and Q4 respectively. After review by PCU it was submitted to ADB in March 2023 and was disclosed in Q2.

An External Monitor mission is due to be carried out early in Q3 and will be reported on in the next reporting period.

Package TIIGP2-LAO-W02: Subproject V1: Nam Ngum Reservoir Access Improvements.

Environmental safeguards: The IEE and EMP for the subproject were updated in July 2020, and Vientiane PONRE issued the Environmental Compliance Certificate for the IEE and EMP on 07 September 2020. ADB issued no-objection with certain conditions to the updated IEE and EMP on 17 September 2020. These conditions including obtaining approval from the relevant government authorities for use the land inside the Phou En District Protection Forest for the subproject were subsequently met and accepted by ADB on 18 December 2020. The PMCES Consultant further updated the IEE and EMP and submitted the documents to MICT and ADB on 29 December 2020. ADB cleared the updated IEE and EMP on 26 February 2021. The UXO Clearance Certificate was issued on 11 March 2021. The contractor produced the

first draft CEMP in June 2021 and during Q4 2021, the contractor revised the CEMP based on comments from PMCES. Following the issuance of a design certificate for the proposed spoil disposal site by the Department of Public Work and Transport of Vientiane Province on 21 March 2022 and the approval of the site by the Provincial Department of Natural Resources and Environment on 29 April 2022, the CEMP was finally approved in May 2022. During the reporting, there was a proposed Rock extraction for retaining wall from contractor. the contractor requested permission to extract 10,000 m³ of rock by excavating a 80 m wide and 160 m long section of the mountain riverside along the loop road currently under construction from National Road No. 10 to the Marina. The contractor has obtained approval from the Provincial Governor and has consulted with relevant provincial departments including Vientiane Provincial Department of Public Works and Transport, Department of Natural Resources and Environment and Department of Energy and Mines. These departments are considering the proposal and are expected to issue their approvals/certificates with certain conditions within April/May 2023. However, the rock extraction still in concern on potential environmental impact to Provincial Protected forestry Phou Arn area. PMCES has agreed on the alternative of rock supply service in Vang Vieng quarry site to supply those rock to the ongoing site construction at Marina and other requires of rock of W02.

During Q2 2023, PMCES Environmental specialists have conducted field missions to monitor the implementation of the EMP/CEMP and to follow-up on implementation of specific measures required by PMCES during earlier missions.

The key results following the site inspections include:

- **Spoil backfilling.** At the backfilled slope at the reservoir shoreline from km 4+200 to 4+350 along the contractor's work site for truck garage, batching plant and aggregate crushing and stockpile, during reporting period the backfilled slope is being stable of bank protection . However, the contractor has continued implementing the bank protection measures including compaction, grass sowing and grading the site. The traffic to and from the batching plant and the garage/workshop, the site terrain has not been graded to direct surface water runoff away from the slope to the road drainage which according to the design should be connected to a sedimentation pond before being discharged into Nam Ngum Reservoir. However, during the dry season this has not caused any significant issues with sediment-laden runoff. PMCES consultant has suggested upgrading the surface drainage system before rainy season with avoid the stagnant water with muddy from truck movement in the area.
- **Batching Plant.** The contractor has operated the batching plant with a pit for concrete washout from the cement trucks and two sedimentation tanks for wastewater from cleaning the concrete mixing drum. However, the area for the batching plant was rather messy with a muddy surface and concrete spills outside the pit. During reporting period, contractor has upgraded by merge the two tank sediment ponds to a bigger pond from batching washing wastewater out. PMCES Consultant, has instructed the contractor has subsequently minimized spills of concrete outside the designated pit (, during periods even a small demand for concrete, the site still appears muddy and messy), and installed guardrails around the sedimentation tanks. The contractor has been further instructed to:
 - Regular clean-up the muddy surface provide a stable surface
 - remove sediments from pits for concrete washout .
 - develop the batching plant site in accordance with the approved design. specially the pavement floor at batching platform where there is mixer drums storage, to ensure no any spillage of mixing material spill out on the ground and keep the cleanliness without any used-fuel spillage on ground.
- **Spoil Disposal Site.** During reporting period, The contractor has continued backfilling spoil materials at the disposal site that was approved by the relevant authorities and

PMCES Consultant in Q2 2022. The backfilling is not being carried out as described in the method statement, the bank protection implementation is pending and the Contractor has still not submitted an updated method statement as earlier agreed with PMCES Consultant.

- **Garage and fuel storage site:** The area is messy and untidy and the wall around the fuel tank has been broken down at one place. The contractor has been repaired the wall. However, during reporting and clean-up small oil spills and overall tidy-up the site.
- Safety and warning signs have been installed at the site, but due to the large area with many different ongoing construction activities, the contractor has to install additional safety signs, workers work onsite has lack of the Personal Protected Equipments and flagmen have to be trained and in place to direct traffic past the construction sites.
- **Batching Plant Health and Safety:** PMCES Consultant has undertaken a hazard assessment of the operation of the batching plant based on earlier site inspections in December 2022. PMCES Consultant found that the main hazards include working at height where trips, slips and falls at the platform or ladder to the mixing drum can result in fall injuries. The contractor has installed guardrails on the mixing drum platform and also the platform for formwork. Sometime, Workers were seen not wearing appropriate PPE and the contractor was reminded to ensure that the workers wear the correct PPE (helmet, safety shoes/boots, high-visible vest, hearing protection, and safety glasses). PMCES has instructed on the health and safety awareness and emergency drill training to carry out for all workers in the batching plant.
- **Rock Extraction for Retaining Wall:** In March 2023, the contractor requested permission to extract 10,000 m³ of rock by excavating a 80 m wide and 160 m long section of the mountain riverside along the loop road currently under construction from National Road No. 10 to the Marina. The reason for the request is due to the demand for rock for the construction of the rock-filled gabion-basket retaining wall at the Marina site which is required according to the revised engineering design and therefore not included in the contractor's original construction plan. The contractor has obtained approval from the Provincial Governor and has consulted with relevant provincial departments including Vientiane Provincial Department of Public Works and Transport, Department of Natural Resources and Environment and Department of Energy and Mines. These departments are considering the proposal and are expected to issue their approvals/certificates with certain conditions within April/May 2023. In parallel, PMCES Consultant is reviewed, the method statement and submit those documents to ADB. However, the proposed rock extraction site still raised environmental concern at Provincial Protected Forestry of Phou Arn. The PMCES team has agreed to the alternative of rock supply service in Vang Vieng quarry site to supply those rock to the ongoing site construction at Marina and other requires of rock of W02.

The status of the roll-out of the contractor's responsibilities under the safety improvement plan developed by the PMCES Consultant is summarized here below:

Activity	Progress	Plan
Confirm full time employment of an Environmental, Health and Safety Officer	Confirmed	-
Conduct work hazard assessment at your construction sites and report the results to PMCES by 30 September 2022	Completed in Dec-2022	-
Develop safety procedures and measures for hazardous construction activities and submit these to PMCES for review and approval by 10 October	Completed in Dec-2022	-

Activity	Progress	Plan
Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors	Completed in Dec-2022	August 2023
Undertake emergency response drill	Completed on 21-Dec-2022	-
Update the CEMP	Ongoing	August 2023

Social safeguards: Following detailed technical discussions and additional attempts by the Project Implementation Unit (PIU) and the Resettlement Committee (RC) to identify suitable replacement land for residential structures, the provision of cash compensation, sufficient to enable access to affordable housing, has been proposed to be the method that is acceptable to households was approved by ADB.

In Q1 2023 the social safeguards team implemented all the necessary surveys and consultations to verify and justify allowances to be provided as part of the self-resettlement package. This, along with the payment for three grievances was made late in Q2 as planned and further reports on this will follow in the next quarter. The full compensation completion report will be drafted after the final payment has been made and it is expected that the marina will be open in June 2024.

Package TIIGP2-LAO-W03: Subproject V2: Kaeng Yui Waterfall Access Improvements and Subproject V3: Western Loop Rural Access Road and Bridge Improvements.

Environmental safeguards: The IEE and EMP for subprojects V2 and V3 were updated in August 2020, and the IEE and EMP were cleared by ADB on 29 September 2020, subject to certain conditions of which the following have been met: (i) Additional public consultations with affected people were organized on 15 and 16 December 2020, (ii) Vientiane Provincial Department of Natural Resources and Environment issued the Environmental Compliance Certificate on 07 April 2021, (iii) The UXO Clearance Certificate for the Western Loop Rural Access Road and Bridge was issued on 16 December 2020, and the UXO Clearance Certificate for Kaeng Yui Waterfall was issued on 18 February 2021, and (iv) follow-up GRM training for the PIU (Vang Vieng District) was carried out on 14 December 2021. PMCES Consultant updated the IEE and EMP and submitted the documents to ABD on 12 February 2021.

It has since come to light that the forest where the waterfall is located is classified as village conservation forest. PMCES Consultant and the PIU have investigated the issue and PMCES Consultant has further updated the IEE and EMP. The updated IEE explains that the parking area, adjacent tourist facilities and the footpath to the waterfall are inside the Na Duang Village Conservation Forest and to formalise the management arrangements and the legal status of the Kaeng Yui Waterfall area, wastewater treatment system as a component under the Project, the Vang Vieng District Governor has issued an Agreement on Land Certificate, No 275, Vang Vieng District Governor's Office, 07-Jul-2021, which allows for the Kaeng Yui Waterfall area to be managed under the Project and which authorises the Vang Vieng District Office of Natural Resources and Environment to issue land use certificates to that effect. Subsequently, the Vang Vieng District Office of Natural Resources and Environment has therefore issued the relevant Land Use Certificates No. 190 and 191 dated 08-July-2021. These documents confirm that the project has obtained the required permissions to be developed inside Na Duang Village Conservation Forest. The updated IEE and EMP have been submitted to ADB in April 2022.

The Site-Specific Environmental Management Plan (SSEMP) for the construction work prepared by the contractor was approved by PMCES Consultant on 11 October 2021 and in accordance with PMCES Consultant's instructions, on 07 December 2021, the contractor

submitted certificates issued by the Vang Vieng District Office of Natural Resources and Environment together with layout maps for the proposed spoil disposal sites and borrow pits.

During Q2 2023, PMCES Consultant has monitored the implementation of environmental, health and safety measures. The key findings are summarized below:

Kaeng Yui Road

- Road works are ongoing and the contractor has installed safety warning signs, but there are still some sections where warning signs and guard rails need to be installed.
- At the section with slope cut along Nam Lao River, slope stabilization work has been done the constructing a gabion retaining wall at the toe of the slope.
- At a section with an approximately 2 m deep trench (km 2+230), PMCES Consultant instructed the contractor to install proper shoring to prevent collapse.

Western Loop

- The contractor has improved the safety by barricading open manholes and installing warning signs at most of the road sections through villages; During reporting period, three causeways (including at section km 2+550; km 2+500; km 6+700) has stalled temporary safety guard drill and warning sign. However, contractor instructed by PMCES consultant to regularly monitors on health and to ensure the safety measures well implemented at sites.
- Nam Song bridge substructure is under construction. No significant environmental issues.
- At entrance of Houay Yae road section, the construction road is ongoing on backfill, install the drainage. The contractor installs warning sign, safety guard drill has installed at open drainage. However, owner of restaurant nearby has usually complaint on progress of construction is slowed and has requested the construction completion as soon as possible. The contractor has instructed by PMCES consultant to avoid temporary impact as much as possible and provides measure immediately after receiving verbal complaint by owner of restaurant.

Batching plant at contractor's camp

- As instructed by PMCES Consultant, the contractor has installed a pole for the power line and removed the power line from contacting the outside ladder on the cement silo.
- As instructed by PMCES Consultant, the silo has been equipped with a dust filter to trap dust generated during filling the silo. However, as observed by PMCES Consultant, the effectiveness of the filter seems limited.
- The ladder to the mixing drum platform has been provided with handrails on both sides and guardrails have been installed all around the platform.

The status of the roll-out of the contractor's responsibilities under the safety improvement plan developed by the PMCES Consultant is summarized here below:

Activity	Progress	Plan
Confirm full time employment of an Environmental, Health and Safety Officer	Confirmed	-
Conduct work hazard assessment at your construction sites and report the results to PMCES by 30 September 2022	Completed in Dec-2022	-
Develop safety procedures and measures for hazardous construction activities and	Completed in Dec-2022	-

Activity	Progress	Plan
submit these to PMCES for review and approval by 10 October 2022		
Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors	Completed in Sep-2022	-
Undertake emergency response drill	Completed in Sep-2022	Early August 2023
Update the CEMP	Completed in Dec-2022	-

Social Safeguards: Social Safeguards: Two monitoring missions were held in this reporting period. A few minor re-occurring outstanding issues were observed, such as: (i) restoration of access to resources and assets for AHs; (ii) timely providing notice to communities about work plan and implications for households; and (iii) safety issues along the road which still need improvement especially where construction materials and plastic sheeting remained on the road posing a risk to road users.

In Q2 2023 the Compensation Completed Report (CCR) was prepared. The CCR has been submitted and disclosed.

Package TIIGP2-LAO-W04: Subproject V5: Vang Vieng Solid Waste Management Improvements.

Environmental safeguards: The IEE and EMP for sub-project V5 were updated in July 2020 based on the re-design of the landfill subproject and cleared by ADB on 15 September 2020. Vientiane PONRE issued the Environmental Compliance Certificate for the IEE and EMP on 22 December 2020. The Governor of Vang Vieng District issued a certificate of no risk of UXOs at the landfill site on 16 December 2020. The contractor submitted the first draft CEMP to PMCES Consultant on 11 March 2021. Following several rounds of comments and revisions, the contractor submitted the final draft CEMP on 25 June 2021 and PMCES Consultant has approved the CEMP with conditions related to installation of groundwater monitoring wells.

Based on technical specifications for construction of groundwater monitoring wells developed by PMCES Consultant, the contractor completed the construction of all monitoring wells in November 2021.

The contractor has conducted three rounds of environmental quality monitoring (December 2021, July 2022 and March 2023). The results of the groundwater quality monitoring in December 2021 showed high levels of COD, BOD5 and TSS potentially indicating groundwater contamination from the dumpsite. However, due to uncertainties on the performance of the sampling and testing, it was not possible to draw any conclusions. In the second round of testing in July 2022, COD and BOD5 were not detected in any of the wells, however one well immediately outside the landfill site had a rather high content iron, phosphate and suspended solids. As of writing this report, the results of the monitoring in March are not yet available.

During Q2 2023, PMCES Consultant has inspected the implementation of the EMP/CEMP. The main findings from the inspections include:

1. As instructed by PMCES Consultant, the contractor has built a low wall around the fuel tank at the camp site thus providing the required secondary containment.
2. Recommend installing handrails on both sides of the steps leading to monitoring well PW2.
3. The contractor shall clean-up of waste along the embankments and on both sides of the perimeter wall.

4. Cell No 5 has been completed and has started receiving waste from 15-Nov-2022 and is expected to be filled by Dec-2024.
5. The contractor shall ensure that the waste pickers wear appropriate PPE including a mask, gloves and high visibility jackets when they are working onsite.
6. Leachate: the current situation is a result of the inability to correctly manage landfill cell 5, poor management of the stormwater drainage system, and the lack of procurement of pumps. The heavy rain already experienced in this wet season has compounded the issue. initial situation requires to control the volume of leachate and apply it in areas where it will not cause environmental or human health impacts. This means pumping the leachate out of the stormwater pond up into the leachate ponds.
7. Leachate pond safety: : As the ponds are now full of water, there are major health and safety concerns. Due to the steep nature and the slippery surface of the HDPE geomembrane, if someone fell into the ponds, therefore PMCES suggests to install fence to avoid people enter without permission and install warning sign at the entrance;
8. General site hygiene: There are concerns about general site hygiene, including maintenance of roads, discarding construction waste around the site, and lack of maintenance in ditches and gutters, which are full of waste, soil and vegetation. The contractor is to clean up then regularly.
9. General site hygiene: There are concerns about general site hygiene, including maintenance of roads, discarding construction waste around the site, and lack of maintenance in ditches and gutters, which are full of waste, soil and vegetation. The contractor is suggested to clean up regularly.
10. Burning: The burning of construction waste has been observed on the site. the contractor is suggested not burning waste, during reporting period , there is improved that no burning waste observed at landfill.
11. The contractor shall prevent cows from entering the landfill.
12. Provide regular soil cover of incoming waste to reduce flies and vermin, malodour, dust and risk of landfill fires.
13. Poor hygienic condition for informal recyclers, flies, and odour.

The status of the roll-out of the contractor's responsibilities under the safety improvement plan developed by the PMCES Consultant is summarized here below:

Activity	Progress	Plan
Confirm full time employment of an Environmental, Health and Safety Officer	Confirmed	-
Conduct work hazard assessment at your construction sites and report the results to PMCES by 30 September 2022	Completed in Mar-2023	-
Develop safety procedures and measures for hazardous construction activities and submit these to PMCES for review and approval by 10 October 2022	Completed in Jan-2023	-
Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors	Completed in Nov-2022	-
Undertake emergency response drill	Completed in Oct-2022	-
Update the CEMP	Completed in Mar-2023	-

Social safeguards: During Q2 one monitoring mission was conducted along with the environment team. An issue regarding the overflow of treated water coming from the landfill was identified. In the future there may be a need for land acquisition to install mitigation measures and reduce flooding risk onto the property. This will be followed up in Q3.

Safeguard Monitoring Reporting: Under ADB Guidelines Category B projects require Semi-Annual Safeguard Monitoring Reports (SMRs) to be submitted once construction starts. The project includes civil works in residential areas, and it is a pro-poor project with a high level of community participation. The SMRs describe Social and Environmental Safeguard Compliance, actions required following issues arising and the handling process of incidents and complaints. For Environmental Safeguard Monitoring, the purpose is to monitor environmental impacts of civil works, by using EMP checklists prepared specifically for the project sites. The SMR furthermore describes planning and implementation of EMP Awareness Training and regularly assesses the project's level of social and environmental safeguard compliance.

The following schedule will be adhered to for the submission of Semi-annual Integrated Safeguards Monitoring Reports.

Semi-annual Integrated Safeguards Monitoring Report	Deadline	Status <i>(Under preparation; Submitted on [date]; Comments from ADB being addressed; Approved)</i>
Report 1: Jan-Jun 2020	31 July 2020	Submitted on 28 September 2020; approved 18 December 2020
Report 2: Jul-Dec 2020	31 January 2021	Submitted on 16 February 2021; approved 4 May 2021
Report 3: Jan-Jun 2021	31 July 2021	Submitted on 1 September 2021; approved 24 November 2021
Report 4: Jul-Dec 2021	31 January 2022	Submitted on 15 March 2022; approved 21 July 2022
Report 5: Jan-Jun 2022	31 July 2022	Submitted on 19 September 2022 (covering period Jan-Jul 2022); approved 27 December 2022
Report 6: Jul-Dec 2022	31 January 2023	Submitted on 25 April 2023 (covering period Aug-Dec 2022); approved on 1 June 2023
Report 7: Jan-Jun 2023	31 July 2023	Under preparation
Report 8: Jul-Dec 2023	31 January 2024	
Report 9: Jan-Jun 2024	31 July 2024	
Report 10: Jul-Dec 2024	31 December 2024	

9. Gender Action Plan Implementation Status

The project is categorized as Effective Gender Mainstreaming.

Progress of implementing the GAP can be summarized as follows:

	Achieved	On track	Not yet achieved
9 Activities	7 (1, 2, 5, 6, 7, 8, 9) = 67 %	2 (3, 4) = 22.3%	0
25 Targets	14 (2, 3, 5, 8, 10, 13, 15, 16, 17, 18, 19, 20, 21, 23) = 56 %	10 (1,4,6,7,9,11,12,14,22,24,25) = 40%	1 (24) = 4%

A detailed progress report on GAP implementation is included in Annex 9.

10. Compliance with Grant Covenants

A table showing status of compliance with Grant Covenants presented in Annex 10.

11. Summary of Workplan for Next Quarter

Procurement packages/consulting services contracts to be awarded next quarter:

Contract	Estimated Amount
Vang Vieng landfill management equipment (Landfill bulldozer and crawler type excavator)	\$325,000
Vang Vieng Landfill Management Equipment (Solid Waste Collection Equipment)	\$99.750
General Equipment (Personal protective equipment)	\$14.620
Total	\$ 439.370

Main activities planned for Q3 2023:

Output 1: Urban-Rural Access Infrastructure and Urban Environmental Services Improved

The primary focus for Q3 2023 for TIIGP2-LAO-W01: this contract was completed on 30th June 2023 and the handing over ceremony was taken on 18 July 2023 in Don Det and a few pending works remain and being completed by the end of July 2023 including (i) drainage system improvement in Nakasang Parking areas; (ii) Boat Ticket Office renovation in Nakasang Parking area; (iii) traffic sign posts installation; (iv) Kilometer posts installation; and (v) sodding. This contract is under defect liability period from 1 July 2023 to 30 June 2024. The Contractor will be responsible for the maintenance of the road during the defects liabilities period.

The primary focus for Q3 2023 for TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements will be continuing with constructing of (i) Landscape Marina (Fill slope protection by using terramesh system, stairs, step landscape, and stone loose riprap for internal access road AL-03 to Circular Pavilion); (ii) Buildings Marina (Shophouses, Public Plaza, and Circular Pavilion); (iii) access road including RC pavement and roadside drains of U-ditches; (iv) slope protection behind the shophouses and access road at Km 1+400 by using Geo-cell; (v) material testing and approval; (vi) Finalization of DED modification & approval of Modified DED; (vii) update the IEE and EMP based on outcome of design modification and continue with updating CEMP; (viii) approval of variation order for additional works; and (ix) work Programme & 14 priority action plans implementation.

For packages of TIIGP2-LAO-W03 focus in Q3 2023 will be on: (i) continuation of the construction of pedestrian bridge No. 03, Kitchen and public toilet at Kaeng Yui Land Scape; (ii) approval of shop drawings; (iii) continuation of testing of RC pipe culverts and approval; (iv) construction of RC pavement and V-ditch construction for Kaeng Yui Access Road; (v) continuation of RC pipe culvert installation; (vi) Updated IEE/EMP for ADB endorsement and disclosure on ADB website; (vii) Compensation completion report (CCR) and closure report; (viii) cast-in-situ of RC girders and prestressing of girders for Nam Xong bridge; (ix) installation of girders for bridge span between abutment A1-Pier P1; (x) continue with cast-in-situ U-ditches and installation of U-ditches; (xi) construction of DBST for road R2 subject to weather condition; (xii) continuation of painting of roofing structures of Dining Pavilion in Kaeng Yui Landscape; and (xiii) 11-priority action plans implementation

For packages of TIIGP2-LAO-W04: Vang Vieng Landfill Improvements focus in Q3 2023 will be (i) groundwater, surface water and leachate water monitoring; (ii) installation of electrical works; (iii) construction of the remaining boundary wall and buildings; (iv) continue with preparing a financial assessment of the Vang Vieng Landfill viability be undertaken for the analysis of economical sustainability to form basis for site management modality O&M Institutional Issues; (v) capacity needs assessment for solid waste management for the basis of the development of O&M capacity building program for the Vang Vieng Landfill; (vi) commissioning for Cell-5 and leachate treatment system; (vii) weighing bridge installation; (viii) continue with building of MRF, Admin Office Building, Workshop and etc.; (ix) continue construction of the planted drying bed; (x) Landfill hazardous waste cell and hazardous store;

(xi) continue construction of incinerator room; (xii) procurement of equipment (Package 1) for landfill improvement; and (xiii) compaction of waste disposal in Cell-5.

Summary of activities planned for Q3 2023 is as follows:

TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvement (C1, C2)		
Some pending activities reported in the punch list	Contractor/PKCC	Jul 2023
All of the completed civil works are under defect liabilities period	Contractor/PKCC	Jul – Sep 2023

TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements (V1)		
Social Safeguard and Implementation (onsite and Self-resettlement)	PMCES/PIU/PCU	Jul - Sep 2023
Compensation payment – Phase 2 and closure report	PMCES/PIU/PCU	Jul - Sep 2023
Updated Work program & 14 priority action plans	Contractor/KFG	Jul - Sep 2023
Updated CEMP	Contractor/KFG	Jul - Sep 2023
Shop Drawings Approval	Contractor/KFG	Jul - Sep 2023
Construction of Landscape Marina	Contractor/KFG	Jul - Sep 2023
Construction of Building Marina	Contractor/KFG	Jul - Sep 2023
Road works	Contractor/KFG	Jul - Sep 2023
Material testing in site LAB	Contractor/KFG	Jul - Sep 2023
Sub-base Construction	Contractor/KFG	Jul - Sep 2023
Concrete Pavement Works	Contractor/KFG	Jul - Sep 2023
Implementation of Contract	MICT/PCU/PIU/PMCES/Contractor	Jul 2021 – Jun 2024
Health & Safety: (i) Confirm full time employment of an Environmental, Health and Safety Officer; (ii) Conduct work hazard assessment at your construction sites and report the results (iii) Develop safety procedures and measures for all hazardous construction activities; (iv) Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors; (v) Conduct drills on emergency response and (vi) Update the CEMP	MICT/PCU/PIU/PMCES/Contractor	Jul 2021 – Jun 2024
Safeguard Monitoring	MICT/PCU/PIU/Social Safeguard Consultants/PMCES	Jul 2021- Jun 2024
Grievance Redress Mechanism (GRM)	MICT/PCU/PIU/PMCES/ Social Safeguard Consultants	Jul 2021- Jun 2024

TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements		
Update IEE/EMP and obtain ADB endorsement	PMCES/PIU/PCU	Jul - Sep 2023
Compensation payment and closure report	PMCES/PIU/PCU	Jul - Sep 2023
11 Priority action plans and updated Work Programm including Personnel's, Equipment's, Organization and S-curve	Contractor/XCR	Jul - Sep 2023
Continue precasting and prestressing of I-Girders for Nam Xong Bridge	Contractor/XCR	Jul - Sep 2023
Continue Sub-base and Base courses	Contractor/XCR	Jul - Sep 2023
Reinforced concrete pavement for Kaeng Yui Access Road	Contractor/XCR	Jul - Sep 2023
Continuation of RC Pipe Culvert installation	Contractor/XCR	Jul - Sep 2023

Continue construction of building in Kaeng Yui Landscape	Contractor/XCR	Jul – Sep 2023
Shop drawings and approval	Contractor/XCR	Jul - Sep 2023
Continue Base-course pavement	Contractor/XCR	Jul - Sep 2023
DBST Pavement in Western Loop	Contractor/XCR	Jul - Sep 2023
Health & Safety: (i) Confirm full time employment of an Environmental, Health and Safety Officer; (ii) Conduct work hazard assessment at your construction sites and report the results (iii) Develop safety procedures and measures for all hazardous construction activities; (iv) Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors; (v) Conduct drills on emergency response and (vi) Update the CEMP	MICT/PCU/PIU/PMCES/Contractor	Sep 2021 – Sep 2023
Safeguard Monitoring	MICT/PCU/PIU/Social Safeguard Consultants/PMCES	Sep 2021 – Sep 2023
Grievance Redress Mechanism (GRM)	MICT/PCU/PIU/PMCES/ Social Safeguard Consultants	Sep 2021 – Sep 2023

TIIGP2-LAO-W03a: Vang Vieng Urban-Renewal

ADB NOL IEE/EMP	PMCES/MICT/ADB	TBA
ADB NOL RP	PMCES/MICT/ADB	TBA
IFB	MICT/FMPS	TBA
DED review and modification	PMCES	Q3 2023
Compensation payment and closure report	PMCES/PIU/PCU	TBA
Pre-bid Meeting	MICT/FMPS	TBA
Site Visit	MICT/FMPS	TBA
Bid Opening	MICT/ FMPS	TBA
Bid Evaluation	MICT/ FMPS	TBA
Contract Award	MICT/ FMPS	TBA
Contract Sign	MICT/ FMPS	TBA
Approved IEE/EMP/Certificate by PONRE	PONRE/PMCES/PIU	TBA

TIIGP2-LAO-W04: Vang Vieng Landfill Improvements (V5)

(i) A financial assessment of the Vang Vieng Landfill viability be undertaken for the analysis of economical sustainability to form basis for site management modality O&M Institutional Issues and (ii) capacity needs assessment for solid waste management for the basis of the development of O&M capacity building program for the Vang Vieng Landfill	PMCES	Jul - Sep 2023
Compensation Completion Report and closure report	PMCES/PIU/PCU	Jul - Sep 2023
Work Program updating and approval	Contractor/CeTeau-PAN JV/PMCES	Jul - Sep 2023
Groundwater Testing & Monitoring	Contractor/CeTeau-PAN JV	Jul - Sep 2023
Waste disposal and compaction in Cell-5	Contractor/CeTeau-PAN JV	Jul - Sep 2023
All Building Facilities	Contractor/CeTeau-PAN JV	Jul - Sep 2023
Weighing Bridge Installation	Contractor/CeTeau-PAN JV	Jul - Sep 2023
Shop drawings and approval	Contractor/PMCES	Jul - Sep 2023
Construction of Landfill Hazardous Waste	Contractor/PMCES	Jul - Sep 2023
Construction of Planted Dry Bed	Contractor/PMCES	Jul - Sep 2023
Implementation of Contract	MICT/PCU/PIU/PMCES/Contractor	Apr 2021 - Apr 2024
Health & Safety: (i) Confirm full time employment of an Environmental, Health	MICT/PCU/PIU/PMCES/Contractor	Apr 2021 - Apr 2024

and Safety Officer; (ii) Conduct work hazard assessment at your construction sites and report the results (iii) Develop safety procedures and measures for all hazardous construction activities; (iv) Develop and implement health and safety training on all safety procedures for the personnel and any subcontractors; (v) Conduct drills on emergency response and (vi) Update the CEMP		
Safeguard Monitoring	MICT/PCU/PIU/Social Safeguard Consultants/PMCES	Apr 2021 - Apr 2024
Grievance Redress Mechanism (GRM)	MICT/PCU/PIU/PMCES/ Social Safeguard Consultants	Apr 2021 - Apr 2024

Output 2: Capacity to implement ASEAN Tourism Standards strengthened

Focus during Q3 of 2023 will be on (i) launching the website for ASEAN Tourism Standards (ii) consultation with the private sector to raise awareness and increase uptake of ASEAN Tourism Standards (iii) re-certification of expired Green Hotel and Homestay Standards (using certified CBT Villages if needed) to make improved progress towards the DMF targets and (iv) update of the Action Plan for achieving ASEAN Clean Tourist City for Vang Vieng.

Output 3 progress: Institutional capacity for tourism destination management and infrastructure O&M strengthened

In Q3 of 2023, DMN work will focus on (i) continuing to support the implementation of the public and private sector action plan on destination management at the national level, Luang Prabang, Vientiane Province, Vang Vieng and Champasak province, (ii) continuing to organize public and private sector consultation meetings to identify key issues and solutions in Lao tourism sector, (iii) continuing to prepare the integrated tourism management and spatial plan for Luang Prabang and the tourism strategic and spatial plans for Nam Ngum Reservoir and Siphandone, (iv) implementing the Laos tourism marketing campaign for Visit Laos Year 2024, support DMNs organizing and participating tourism promotional events and travel trade fairs (v) implementing the detailed thematic heritage interpretation plans for Luang Prabang town and environs and the 4,000 islands, and write interpretation panel texts for Vientiane province and Vang Vieng, (vi) finalizing SME support plans for the project target areas, including SME database, and (vii) updating contents on the Internet based tourism knowledge repository and DMN website.

Regarding institutional arrangements for O&M planning work, the focus during Q3 of 2023 will be on the following:

Subproject: Nakasang Access Road and Port Rehabilitation and Subproject C2: Don Det-Don Khone Access Improvements: The draft O&M plan will be presented to PCU for approval. The document will be translated into the Laos language and presented to the local authorities. The Institutional consultants will support the local authorities in developing the PPP arrangements with the private operator for the management of Nakasang car park.

Subproject V1: Nam Ngum Reservoir Access Improvements. Undertake a field visit to establish concepts for O&M.

Subproject V2: Kaeng Yui Waterfall Access Improvements. The PMCES Consultants will further develop the concepts for Kaeng Yui and seek agreement from the local authorities and local community.

Subproject V3: Western Loop Rural Access Road and Bridge Improvements. No activities are planned for this period.

Subproject V4: Vang Vieng Urban Renewal. No activities are planned for this period.

Subproject V5: Vang Vieng Solid Waste Management Improvements. During the next quarter, it will be critical to agree on the process for continuing to compact waste and utilise intermediate cover, which will reduce leachate production. In the absence of procurement of critical landfill equipment (e.g., bulldozer), consultants will seek to find ways of involving UDAA alongside the contractor in the management of cell 5. This may involve identifying and training a UDAA operator for the bulldozer. Consultants will also work with the local waste collector and UDAA to find ways to improve the safety of operations undertaken by the informal waste pickers. A solution to the management of high volumes of leachate will need to be found since leachate production is likely to be high in this wet season. Further work will be undertaken to develop collaboration with GGGI and other development partners. The PPP arrangements for the management of the materials recovery facility and hazardous waste facilities, as well as the workshop, will be progressed.

Planned disbursements:

For Q2 2023, the following withdrawal applications (WA) are foreseen:

- Replenishment of Advance Account:
 - WA #86 (SOE Mar/Apr2023): \$201,612.70
 - WA #xx (SOE May 2023): 108,891.30 (estimate)
 - WA #xx (SOE Jun 2023): \$121,164.74 (estimate)
- Direct payments:
 - WA #xx direct payment \$200,000 (estimate) IPC Package W01, G21291)
 - WA #xx direct payment \$ 500,000 (estimate) (IPC Package W04 G22778)
 - WA #xx direct payment \$500,000 (estimate) (IPC Package W02 G23079)
 - WA #xx direct payment \$400,000 (estimate IPC Package W03 G0001)

12. Issues and Recommendations

As mentioned, EA and ADB agreed during the Midterm Review that package W03a: Vang Vieng Urban Renewal would be on hold until physical completion of contracts TIIGP2-LAO-W02 and TIIGP2-LAO-W03 were 50%. As reported, this is now the case and planning for W03a has re-started aiming for an issuance of an invitation for bids by October 2023, contract award by April 2024 and commencement of works by July 2024 (see timeline below). To achieve this, agreement on revised scope and land acquisition and resettlement impacts and mitigation measures is urgently needed, as well as processing of a one-year project extension need to complete this subproject. The EA therefore requests ADB to support the quick preparation and approval of a social safeguards due diligence report, and implementation of the recommendations made in this plan so that the target IFB issuance in October 2023 can be achieved, and approval of the proposed project extension .

Updated timeline for TIIGP2-LAO-W03a: Vang Vieng Urban Renewal

W03a: Vang Vieng Urban	Month	2024												2025												2026																							
		7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12						
Confirm revised scope																																																	
Update DED and BOQ																																																	
Conduct Safeguards Due Diligence																																																	
Prepare bidding documents																																																	
IFB issuance & bid period																																																	
Bid opening																																																	
Bid evaluation and BER																																																	
ADB approval																																																	
Contract award																																																	
Pre-construction works																																																	
Mobilization																																																	
Commencement																																																	
Construction																																																	
Defects Liability period																																																	



Approved and Submitted to ADB by:

**Mrs. Phonemaly Inthaphome
National Project Manager
Ministry of Culture, Information and
Tourism**

Annex 1: Progress of civil works by subproject as of 30 June 2023

Subproject	Location and Description	DED and Implementation Progress
Works Package: TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements		
C1: Nakasang Access Road and Port Rehabilitation	<p>Khong District. The subproject will: (i) reconstruct 2.72 km road from Route 13S to the Nakasang Mekong River port and create a turning area for buses; (ii) reinforce 45 m of riverbank protection and reconstruct 60m of riverside path in the port area; (iii) improve footpaths and ramps to floating river pontoons to provide safer passenger access; and (iv) divert the main storm water drainage outlet 15 m downriver from the port.</p>	<p>LAO-W01: Nakasang and Don Det-Don Khone Access Improvements: DED, bill of quantities, technical specification, bidding documents, updated safeguards documents, have been reviewed and updated as needed, by the PMCES Consultant.</p> <p>The contract was awarded on 23rd December 2019 to Phoukhong Construction Sole Co. Ltd. with a contract amount of USD 3,964,308.36 (including Provisional Sums USD 650,000, Contingency USD 333,000.69 and Tax USD 301,300.76).</p> <p>Work commenced 26th May 2020, 24 months' contract with extended time of 13 months up to 30th June 2023.</p> <p>The present status of the project is as follows:</p> <ul style="list-style-type: none"> • The EA further approved 81 days which is approximately 2.7 months or up to 30th June 2023 to complete all of outstanding works on site • Physical progress is 100% (Revised work program of 100%) <ul style="list-style-type: none"> • 21.112 Km Road (2.904 Km at Nakasang, 5.907 Km in Don Det and 12.301 Km in Don Khone) • 3 Bailey Bridges on Access Road IRL-05 in Don Khone • 178.00 m Culvert (16.00 m Culvert at Nakasang) • 3 Parking Areas (1 Nakasang, 1 Don Det old Port and 1 Ban Hang Khone) • 11 Sets of Solar Light (9 Sets Nakasang Port and 2 Sets Railway Bridge _ Both Sides) • 2 Boat Ramps (Nakasang River Port) • 1 Pontoon (Nakasang River Port) • 106.00 m Retaining Wall (Nakasang River Port) upstream side (U/S) & downstream side (D/S) • 140.00 m Slope Protection by Rubble Stones (Nakasang River Port) • 153.00 m Footpath (Nakasang River Port) U/S & D/S • 25.00 m Drainage & Discharge RC Pipe • Locomotive Area Improvements in Don Khone • View Point in Don Det old Port • Safety Guardrail on Approach road to Mekong Bridge in both sides Don Det and Don Khone (French Bridge) • Renovation of Port Ticket Office/Waiting area of the Tourists • Renovation of Ticket Office at Nakasang Parking area • Cross Drainage at end of Nakasang River Port (U/S) • Renovation of wooden bridge to concrete deck slab on access road alone Nakasang Port (U/S) • Road Furniture was completed excluding some traffic sign posts and kilometer posts being installed. • RP's CAP fully implemented and being monitored
C2: Don Det-Don Khone Access Improvements	<p>Khong District. This subproject will (i) pave the main 11 km road network on Don Det and Don Khone islands; (ii) pave the 780 m² Don Det ferry port vehicle parking area; (iii) cycle track/footpaths over the two islands; and (iv) install public lighting and safety rails on the old railway bridge linking the islands.</p>	
Works Package: TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements		
V1: Nam Ngum Reservoir	<p>Keo Oudom District. This subproject will (i) improve the</p>	<p>TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements: Feasibility studies, preliminary designs,</p>

Subproject	Location and Description	DED and Implementation Progress
Access Improvements	existing public marina at the Nam Ngum Reservoir recreational area to safely accommodate 50-60 local tour boats and launch small recreational vessels; (ii) construct a 5.9km loop road extending along the reservoir shore linking to Route 10, and 1,200 m ² parking area; (iii) construct a new 3,860 m ² public market and shophouses to replace existing informal lakeside stalls; (iv) install septic tanks in all public buildings and a wastewater pump-out station/holding tank at the marina; (v) replace abandoned, unsafe public buildings and piers with new public green space; and (vi) renovate the tourist information center.	<p>preliminary cost estimates and safeguards documents prepared during project preparation. DED, bill of quantities, technical specification, bidding documents, updated safeguards documents, O&M plan were prepared by the PMCES Consultant. The DED, Safeguard Documents and Bid Document were endorsed by ADB in Q3 2020. The number of safeguard activities were carried out in Q4 2020.</p> <p>The contract was awarded on 20th April 2021 to Khamfong Group Sole Company Limited with a contract amount of USD \$4,669,065.14 inclusive of tax, and contingency of US\$424,460.47</p> <p>The present status of the project is as follows:</p> <ul style="list-style-type: none"> • Works Commenced 1st July 2021, 24 months Contract with the extended time of 12 months up to 30th June 2024 • Physical progress is 60.51% (Target 100%) <ul style="list-style-type: none"> - Road Improvement: 88.44% (5.59 km completed out of 6.33 km) - Landscape Marina works: 23.95% - Building Marina works: 17.23% - Roadside drains:68.80% • Compensation to AHs fully implemented • Additional slope protection structure, replacement of government structure, water treatment and wastewater treatment required additional 1.8mIn • Work progress is very slow especially marina works and 14 priority action plans are being implemented • Warning letter issued on 22nd May 2023 for expediting the progress
Works Package: TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements		
V2: Kaeng Yui Waterfall Access Improvements	Vang Vieng District. The subproject will (i) upgrade the 6km access road from Vang Vieng Town to Kaeng Yui waterfall; (ii) level and pave the 875 m ² waterfall parking area; (iii) improve surfaces and drainage in the waterfall market area; and (v) improve 300m footpaths, including rehabilitation of steps, small suspension bridges, and signage.	<p>TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements: Feasibility studies, preliminary designs, preliminary cost estimates and safeguards documents prepared during project preparation. DED, bill of quantities, technical specification, bidding documents, updated safeguards documents were prepared by the PMCES Consultant.</p> <p>The DED, Safeguard Documents and Bid Document were endorsed by ADB in Q3 2020. The number of safeguard activities were carried out in Q4 2020. The bid evaluation and additional due diligence were carried out in Q1 2021.</p>
V3: Western Loop Rural Access Road and Bridge Improvements	Vang Vieng District. The subproject will (i) upgrade the 26 km “Western Loop Road” and three village feeder roads; (ii) construct a new road bridge across the Song River, with 2.0km feeder road linking the bridge, Western Loop Road and south end of town; and (iii) provide bio-engineered river bank protection and improve the footpath/cycle track between the new bridge and Huay Yae village.	<p>The contract was awarded on 23rd July 2021 to M/s Xayya Construction and Renovation Sole Company with a contract amount of US\$ 8.829,630.77 Inclusive of tax, and contingency of US\$ 802,693.70</p> <p>The present status of the project is as follows:</p> <ul style="list-style-type: none"> • Works Commenced 1st Sep 2021, 24 months Contract • Physical progress is 56.27% (Target 96.41%) <ul style="list-style-type: none"> ○ Kaeng Yui: 60.37% ○ Western Loop: 53.87% ○ NamXong Bridge: 51.79% • 5.5 Km concrete road surface completed out of 6.0 km for Kaeng Yui Access Road (91.66% completed).

Subproject	Location and Description	DED and Implementation Progress
		<ul style="list-style-type: none"> • 26.6 Km Access Road Preparation in Progress (56.23% completed). • Kaeng Yui Landscape (buildings 56.80% completed and landscape 13.65% completed) • 80 m RCC Namxong Bridge in progress (51.79% completed) • Pre-stressed Concrete I-Girders out of 15 (10 girders completed) • All Integrity & Sonic tests, Static & Dynamic completed (100% completed) • CEMP revision completed • Prepared a health and safety handbook and Emergency contact of project site • Conducted construction toolbox meeting regularly by contractor • Develop safety procedures and measures for hazardous construction activities and Conducted the Hazard Assessment Training • Conducted First-Aid & basic care treatment & safety procedure plans are being implemented
Works Package: TIIGP2-LAO-W03a: Vang Vieng Urban Renewal		
V4: Vang Vieng Urban Renewal	<p>Vang Vieng District. The subproject will (i) rehabilitate 4.0 km of footpaths with suitable surfaces, street lighting, seating and soft landscaping; (ii) install traffic calming measures in streets with high concentrations of tourists; (iii) improve traffic management, including one-way traffic flows (1.5 km); and (iv) resurface roads and improve drains in residential areas (1.0 km).</p>	<p>TIIGP2-LAO-W03a: Vang Vieng Urban Renewal: Feasibility studies, preliminary designs, preliminary cost estimates and safeguards documents prepared during project preparation. Feasibility studies, preliminary designs, preliminary cost estimates and safeguards documents prepared during project preparation. DED, bill of quantities, technical specification, bidding documents, updated safeguards documents were prepared by the PMCES Consultant.</p> <p>The DED was endorsed by ADB in Q3 2020. No activity was carried out in Q4 2022.</p> <p>This subproject was previously included in Package TIIGP-LAO-W03, but recently separated into a new Works Package TIIGP2-LAO-W03a to allow for coordination and alignment with ADB-financed Water Supply and Sanitation Sector Project, for which detailed design for its subproject in Vang Vieng is currently ongoing. Preparation of safeguards documents will be coordinated between the two projects. As of the end of the reporting period, as reported by the PCU, the Water supply project in Vang Vieng will be invested/constructed by Local private company.</p> <p>The present status of the project is as follows:</p> <ul style="list-style-type: none"> • ADB No Objection to the RP, but RP updating is required • ADB No Objection to the IEE and EMP • ADB No Objection to the Bidding Document • The procurement of this package would be processed in Q4 2023 subject to the DED modification and updating of resettlement plan
Works Package: TIIGP2-LAO-W04: Vang Vieng Landfill Improvements		
V5: Vang Vieng Solid Waste Management Improvements	<p>Vang Vieng District. The subproject will transform the existing district solid waste dump site into a managed landfill and includes (i) installation of a perimeter runoff interceptor</p>	<p>TIIGP2-LAO-W04: Vang Vieng Landfill Improvements: Review findings of the DED carried out in Q3 2019 for the landfill subproject revealed that the existing design requires revision, which would entail substantial alterations to the design, drawings, BoQ and technical specification. It was decided that an environmental compliance audit (ECA)</p>

Subproject	Location and Description	DED and Implementation Progress
	<p>drainage system; (ii) cell construction with impermeable liners, leachate collection/treatment system, and a landfill gas recovery system; (iii) construction of a small materials recovery facility for waste separation and recycling and a medical waste treatment area; (v) construction of a septage treatment facility (0.5ha); (vi) construction of site office, toilets, and fencing; (vii) pave the 0.8km access road and provide three new collection trucks, a bulldozer, and two vacuum trucks to support septage collection.</p>	<p>needed to be conducted to test the design information. PMCES Consultant engaged an ECA sub-consultant team to carry out this work. The ECA team submitted its draft report to the PMCES Consultant on 16th January 2020. PMCES reviewed and edited the report and it on 11th February 2020 to MICT and ADB for review, comments and approval. The report was eventually approved on 22nd March 2020.</p> <p>ADB approved additional financial resources to undertake the design revisions, which include design of a closure system of existing landfill site with all precautionary measures and appropriateness of design of MRF system design, admin building and office facilities, leachate treatment design, septage treatment design, effluents and hazardous waste, master drainage management of storm water, additional internal access road to facilities, new boundary wall, new incineration plant, appropriate Electro-Mechanical facilities and tree plantation etc.</p> <p>DED, bill of quantities, technical specification, bidding documents, updated safeguards documents, O&M plan, and recommendations for O&M were prepared by the PMCES Consultant. The DED, Safeguard Documents and Bid Documents were endorsed by ADB in Q3 2020.</p> <p>The bid evaluation and additional due diligence were carried out in Q4 2020.</p> <p>The contract was awarded on 19 February 2021 to CeTeau-Panyathilath Joint Venture with a contract amount of USD \$ 3,156,160.09 including contingency of USD US\$ 286,923.64)</p> <p>Works Commenced 19th Apr 2020, 24 mons Contract Intended Completion was extended from 19th April 2023 to 20 April 2024.</p> <p>The present status of the project is as follow:</p> <ul style="list-style-type: none"> • Physical progress is 75.37% (Target 91.72%) • Existing capped cell is completed • Construction of Cell-5 is under semi-operational stage • Construction of Cell-1 is completed • Manholes & Inspection Pits completed • Leachate ponds completed • 1.53 Km concrete road completed out of 1.55 km Road • Building works are in progress • Work progress is in revision • CEMP revision Completed • Prepared a health and safety handbook and Emergency contact of project site • Conducted construction toolbox meeting regularly by contractor • Develop safety procedures and measures for hazardous construction activities and Conducted the Hazard Assessment Training • Conducted First-Aid & basic care treatment & safety procedure plans are being implemented

Description	Preliminary Design Cost Estimates (US\$) (PAM procurement plan, version 0)	Updated estimates (US\$) (procurement plan 5)	Current estimates (US\$) (based on BOQ DED by PMCES Consultant/Contracted amount)
<u>TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements</u>	7,227,529	5,930,000.00	3,964,308.36 (Contracted Cost with Phoukhong Construction Sole Co. Ltd)
C1. Nakasang Access Road and Port Rehabilitation;	3,613,167		
C2. Don Det-Don Khone Access Improvements	3,614,362		
<u>TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements</u>	6,142,686	7,000,000	4,669,065.14 (Contracted Cost with Khamfong Group Sole Company Limited)
V1. Nam Ngum Reservoir Access Improvements;	6,142,686		
<u>TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements</u>	9,658,377	13,000,000	8,829,630.77 (Contracted Cost with Xayya Construction and Renovation Sole Co.,Ltd)
V2. Kaeng Yui Waterfall Access Improvements;	2,180,747		
V3. Western Loop Rural Access Road and Bridge Improvements;	7,477,630		
<u>TIIGP2-LAO-W03a Vang Vieng Urban-Renewal</u>	1,015,501	2,000,000	2,000,000
V4. Vang Vieng Urban Renewal;	1,015,501		
<u>TIIGP2-LAO-W04: Vang Vieng Landfill Improvements</u>	5,632,000	3,600,000	3,156,160.09 (Contracted cost with CeTeau-Panyathilath Joint Venture)
V5. Vang Vieng Solid Waste Management Improvements.	5,632,000		
Total	29,676,093	31,530,000	22,709,164.36

Annex 2: Record of Output 2 and 3 and Project Management Activities implemented during Quarter 2 of 2023 (1 April – 30 June 2023)

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
2.8.2.a	Re-assess the hotels that have received the ASEAN Green Hotel Standard Award but expired. Champasak province, 17-24/05/2023	17-24/5/2023	Champasak	To assess the quality of services	Provincial committee	45	20	Implemented as plan	29,998,000
2.8.2.a	Assessment of expired ASEAN Green Hotel standards in Luang Prabang Province 1-15 /5/2023	1-15/5/2023	Luang Prabang	Re-assess to propose for award	PIU	20	9	Assessment implemented	22,440,000
2.8.2.a	Assess the new target of 9 ASEAN Green Hotels in Luang Prabang Province, 5-19/5/2023	15-19/5/2023	Luang Prabang	To encourage hotel businesses to receive the ASEAN Green Hotel Standard Award	PIU	33	15	The assessment completed	14,760,000
2.8.2.a	Re-assessment meeting of the hotels that have been awarded the ASEAN green hotel standard. Vang Vieng, 16-19/05/2023	16-19/05/2023	Vang Vieng, VTP	To assess the service quality	Vang Vieng OICT, District Authorities involved	60	25	Completed as plan	12,687,000
3.1.a	Participate in the provincial DMN meeting, Pakse, Champasak province, 27-30/6/2023	29/6/2023	CPS	To review the the first 6-month plan	PCU/EA, TDD	19	5	Fruitfull meeting	30,300,000
3.1.a	Provincial DMN meeting to review the 2023 workplan. Champasak province, 29-30/05/2023.	29-30/5/2023	Champasak district	To review the plan	DMN members	34	17	Key issues discussed	22,800,000
3.2.2	Improve English skills for the term 1, 2023 at UTD EDUCATION, VTE, 15/6/2023-14/9/2023 (TDD staff)	15/6-14/9/2023	UTD EDUCATION	To improve English skills	PCU/EA, TDD	1	0	Ongoing	450
3.2.2	Upgrade English skills for tourism sector staff (Tourism Development Department) in Vientiane College, 8/5-8/8/2023	8/5-8/8/2023	Vientiane Collage	To upgrade English language skills	PCU/EA, TDD	4	1	English skills upgraded	1,520
3.2.3	Support the data/information collection to prepare to draft the master's thesis, 1/7/2022 - 31/3/2023	1/7/2022 - 31/3/2023	Luang Prabang	To collect information for Master's thesis	PIU	2	1	Completed as plan	8,000,000
3.4.1	Public and business sectors meeting to address issues in the tourism sector in Champasak district, Champasak province, 20-21/06/2023	20-21/6/2023	Champasak district	To discuss the solutions	DICT/PIU, Tourism stakeholders	33	14	Completed as plan	15,493,000
3.4.1	Public and business sectors meeting to address issues in the tourism sector, 24/4/2023	24/4/2023	Luang Prabang	To discuss the solutions and address issues	PIU	46	19	The solutions identified	17,020,000
3.4.1	The project EA/PCU and related departments follow up to address issues. Luang Prabang, 7-10/4/2023	7-14/4/2023	LPB	To follow up and address	PCU/EA, TDD	16	5	The issues addressed	22,458,000

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
3.4.1	Workshop on welcoming Chinese tourists in Luang Prabang, 15-19/ 5/2023	15-19/5/2023	LPB	To welcoming Chinese tourists	PCU/EA, TDD	39	17	The welcoming Chinese tourists disseminated	37,500,000
3.4.1	Organize public and business sector meetings, follow up to address issues in the tourism sector at the national level and draft policies to promote tourism. Vang Vieng, 22-25/5/2023	22-25/5/2023	Vang Vang	To discuss the solutions	PCU/EA, TDD	19	7	The solutions discussed	14,961,000
3.4.2	Organize meeting to review, approve and disseminate the tourist boat services standard agreement in Nam Ngum Dam 1 recreation areas. Keo Oudom district, VTP, 27-30/06/2023	30/6/2023	VTP	To improve the draft content	VTP-PIU	33	17	Able to organize review meeting as plan	22,481,000
3.4.3	Dissemination meeting on Vang Vieng urban management regulations. Vang Vieng district, 02/05/2023	02/05/2023	Vang Vieng, VTP	To disseminate the urban management regulations	PIU and District Authorities	132	65	Completed as plan	16,870,000
3.4.4	Workshop to finalize Vang Vieng Tourism Master Plan and Environs for 2023-2033. VTE, 21-22/06/2023	21-22/6/2023	VTE	To finalize the plan	PCU/EA, TDD	56	19	The participants satisfied with the results	52,220,000
3.4.4	Conduct training on "Food and Beverage" to small-medium restaurant providers in Luang Prabang City, 14-16/6/2023	14-16/6/2023	Luang Prabang	To upgrade service quality	PIU	35	17	knowledge and skills upgraded	26,479,000
3.4.4	Organize review meeting on Vang Vieng Tourism Master Plan and Environs for 2023-2033. Vang Vieng, VTP, 11-14/06/2023	11-14/06/2023	Vang Vieng, VTP	To review the draft	National SC, Provincial, District Authorities and Consultant team	224	159	Completed as plan	29,824,000
3.4.4	Organize review meeting on Vang Vieng Tourism Master Plan and Environs for 2023-2033. Vang Vieng, VTP, 11-14/06/2023	11-14/6/2023	Vang Vieng	To review the final draft	PCU/EA, TDD	22	8	Meetings completed	30,102,000
3.5.2.2	Workshop on preparation of Visit Lao Year 2024. VTE, Tourism and Hospitality, Social Science Faculty, 2/6/2023 and 6/6/2023,	02/6/2023 and 6/6/2023	Tourism and Hospitality, Social Science Faculty (NUOL)	To prepare	PCU/EA, TDD	89	28	Preparation of documents completed	7,020,000
3.5.2.2	Organize public and private business in the tourism sector meeting across the country to prepare for tourism campaign for Visit Lao Year 2024. VTE, 8/6/2023	06/08/2023	VTE	To prepare for tourism campaign	PCU/EA, TDD	55	24	Brainstorming and consultation completed	22,945,000

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
3.5.3.1	Participate in Lao New Year activities and survey tourism routes along the Lao-China railway in Luang Prabang province, 12-18/04/2022	12-18/4/2022	LPB	To survey tourism routes	PCU/EA, TDD	15	9	The survey organized	37,470,000
3.5.3.1	Participate in Mekong Tourism Forum (MTF) 2023. Cambodia, 24-28/4/2023	24 - 28/4/2023	Cambodia	To enhance the tourism cooperation	PCU/EA, TDD	4	2	The cooperation enhanced	6,220.00
3.5.3.1	Rental fees for the tourism exhibition booth in "Beijing International Tourism Expo", China, 14-20/06/2023	14-20/6/2023	Beijing, China	To promote Lao tourism	PCU/EA, TDD	2	0	Completed as plan	3,330
3.5.3.1	Per-diem for participating the "Beijing International Tourism Expo". China, 14-20/6/2023	14-20/6/2023	Beijing, China	To promote Lao tourism	PCU/EA, TDD	2	0	Completed as plan	2,510
3.5.3.2	Organize national DMN meeting to discuss tourism promotion activities. VTE, 26/6/2023	26/6/2023	VTE	To prepare tourism campaign	PCU	40	21	Preparation documents completed	1,500,000
3.5.3.2	Tourism promotion activity during Lao New Year (Pi Mai) by supporting the elephant procession in the Lao traditional festival in Luang Prabang province, 13/4/2023	13.4.2023	Luang Prabang	To preserve the traditions of the Luang Prabang people and also to promote tourism in the province,	PIU	0	0	visitors increased	25,745,000
3.8.a	Provincial-level tour guide training in Luang Prabang (2nd training), 2-24/05/2023	2-24/5/2023	Luang Prabang	To develop personnel	PIU	79	37	knowledge upgraded	29,917,000
3.10.1	Follow up and inspect on environmental safeguards and organizational capacity building for Contract No. TIIGP2-LAO-W01 (Nakasang, Dondet - Donkhone access improvement), Khong district, Champasak province, 7-9/06/2023.	7-9/6/2023	Khong dist, Champasak	To strengthen local authorities	Consultants and PIU	32	11	Local authorities strengthened	15,872,000
3.10.1	Workshop to draft the O&M plan in the project target areas, 10-13/05/2023	10-13/05/2023	Vang Vieng, VTP	To discuss and draft	PCU, consultants, PIU	42	15	Completed as plan	7,359,000
3.10.1	Workshop to draft the O&M plan in the project target areas, 10-13/05/2023	10-13/5/2023	Vang Vang	To draft the O&M plan	PCU/EA, TDD	6	2	Completed as plan	8,987,000
4.6.2	Participate in the bidding meeting on equipment for Vang Vieng Landfill administration and management office, 29/06/2023	29/06/2023	Vientiane Capital	Participate in the assessment meeting of the bid	PIU and Procurement Committee	3	1	Completed as plan	2,269,000

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
4.6.2	Participate in equipment bidding meeting to provide to Vang Vieng Landfill Administration Office. Vang Vieng, 02/05/2023	02/05/2023	Vientiane Capital	To provide equipment	Procurement Committee and PIU	3	1	Completed as plan	2,333,000
4.12.1	Annual auditing of the project financial-accounting documents by State Audit Organization (SAO) in Vientiane province for 2022, VTP, 4-6/6/2023	4-6/6/2023	VTP	To build the transparency for the implementation of the project	VTP-PIU	16	9	Implemented as plan	14,980,000
4.12.1	Support Salavan's DICT staff to work with project EA/PCU on SouthernLaos tourism circuite. Salavan, 03/04/2023	03/04/2023	Salavan	To support SouthernLaos tourism	PCU/EA, TDD	30	7	The plan discussed	2,998,000
4.12.1	Participate in monitoring the implementation of the 2023 project activities/workplan ,between PCU and Vientiane province's PIU. VTP, 5-8/06/2023	5-8/6/2023	VTP	To follow up the implementation	PCU/EA, TDD	12	3	Plan reviewed	14,978,000
4.12.3	PCU/EA and national social safeguards committee follow up the civil works progress at the subproject sites: W02, W03 and W04. Vientiane province, 19-22/4/2023	19-22/4/2023	VTP	Field visit to the subproject sites	PCU/EA, TDD	17	6	The outstanding issues addressed	22,300,000
4.13.3	PCU - Consultation meeting and follow up the project implementation progress in the project target areas. Luang Prabang, 20-24/6/2023	20-24/6/2023	LPB	To monitor the progress	PCU/EA, TDD	15	5	Completed as plan	29,404,000
4.13.3	National project steering committee and PCU inspect the 100% completion of the contract W01: Nakasang-Dondet-Don khone access improvement. Khong district, 25-29/6/2023	25-29/6/2023	Khong dist. Champasak	To inspect 100% completion	PCU/EA, TDD	23	8	The subproject W01 completed	50,758,000
4.13.3	Follow up the civil works progress in Khong district, Champasak province, 09-10/05/2023	9-10/5/2023	Khong, Champasak	Follow up civil works progress	CPS-PIU	15	3	Implemented as plan	11,644,000
4.13.3	Follow up the civil works progress in Khong district. Champasak, 16-17/06/2023	16-17/6/2023	Khong dist., Champasak	To follow up the progress	CPS-PIU, District committee	16	3	Completed as plan	12,144,000
4.13.3	Join the inspection the 100% completion of the project to improve access road to Nakasang-Dondet-Don khone. Khong district, 25-29/6/2023	25-29/6/2023	Khong dist., Champasak	To inspect 100% completion	PCU,PIU, District Committee and National Steering Committee	50	15	Completed as plan	32,944,000

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
4.13.3	Consultation meeting and follow up the project implementation progress in the project target areas. Luang Prabang, 20-24/6/2023	20-24/6/2023	Luang Prabang	To follow up the progress	PCU&PIU	30	13	Ongoing	22,490,000
4.13.3	The national project steering committee meeting to encourage, inspect and supervise the implementation of the project with the provincial project steering committee. Vang Vieng 9-10/05/2023	09-10/05/2023	Vang Vieng, VTP	To encourage, inspect and supervise	Committees, PCU, PIU and district Authorities	236	96	Completed as plan	22,243,000
4.13.3	Meeting to follow up the civil works progress in the project target areas with Donor/ADB. Vang Vieng, 19-20/05/2023	19-20/05/2023	Vang Vieng, VTP	To monitor the progress	PCU, PIU and District Authorities involved	48	26	Completed as plan	4,435,000
4.13.3	Organize training on M&E and other related issues. Vang Vieng, 22-25/05/2023	22-25/05/2023	Vang Vieng, VTP	To upgrade knowledge for PIU and DICT concerned	PCU/Consultant, VV and VTP- PIUs	23	11	Completed as plan	15,000,000
4.13.3	Follow up the civil works progress with donor (ADB) in Keo Oudom and Vang Vieng districts, VTP, 7-9/6/2023	7-9/06/2023	Vang Vieng, VTP	To monitor the progress	PCU, PIU and District Authorities involved	50	26	Completed as plan	7,430,000
4.13.3	Site visit to encourage, inspect and supervise the implementation of the project with the provincial project steering committee. Keo Oudom, VTP, 7-8/05/2023	05/08/2023	NamNgum1, Keo Oudom, VTP	To encourage and supervise	VTP-PIU, ADB, PCU	12	5	Implemented as plan	7,478,000
4.13.3	Organize training on M&E and other related issues in the project target areas. Vang Vieng, 22-25/05/2023	05/10/2023	Vang Vieng, VTP	To upgrade knowledge for PIU and DICT concerned	VV-PIU	33	17	Implemented as plan	14,876,000
4.13.3	Follow up the civil works progress in Keo Oudom and Vang Vieng districts with the EA/PCU and Donor/ADB, 7-9/6/2023	06/09/2023	Keo Oudom,	To follow up the progress	VTP-PIU	6	4	Implemented as plan	4,492,000
4.13.3	PCU/EA joins the ADB mission to follow up the social safeguards issues in Keo Oudom, Vang Vieng districts,	18-21/4/2023	Keo Oudom and Vang Vieng districts	To follow up the progress and safeguards issues	PCU/EA, TDD	8	2	Completed as plan	14,628,000
4.13.3	The project EA/PCU and ADB mission follow up the civil works progress in Keo Oudom and Vang Vieng districts, Vientiane province, 4-6/5/2023	4-6/5/2023	Keo Oudom and Vang Vieng districts	To follow up the progress	PCU/EA, TDD	8	4	Completed as plan	7,628,000
4.13.3	National and provincial steering committees follow up, inspect and supervise the civil works in Keo Oudom and Vang Vieng districts, Vientiane province, 7-10/5/2023	7-10/5/2023	Keo Oudom and Vang Vieng districts	To support the civil works	PCU/EA, TDD	15	5	Completed as plan	21,849,000

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
4.13.3	The project EA/PCU follow up/monitor the progress of the implementation of tourism activities in the project target areas. Luang Prabang, 10-13/5/2023	10-13/5/2023	LPB	To follow up the progress	PCU/EA, TDD	16	5	The civil works	13,947,000
4.13.3	Meeting to follow up the civil works progress in the project target areas with Donor/ADB. Vang Vieng, 19-20/05/2023	19-20/5/2023	Vang Vang	To follow up the progress	PCU/EA, TDD	9	0	Completed as plan	5,749,500
4.13.3	Follow up the civil works progress in the project target areas in Vang Vieng, 24-25/05/2023	24-25/5/2023	Vang Vieng	To follow up the progress	PCU/EA, TDD	6	2	Completed as plan	3,767,000
4.13.3	Follow up the civil works progress in Keo Oudom and Vang Vieng districts with the Donor/ADB, 7-9/6/2023	7-9/6/2023	Keo Oudome & Vabg vieng dist.	To monitor the progress	PCU/EA, TDD	6	1	Completed as plan	6,823,000
4.13.4	Meeting to monitor the social safeguards issues, draft and update the resettlement plan in the project target areas. VTE, 19-20/6/2023	19-20/6/2023	VTE	To monitor the progress	PCU/EA, TDD	20	5	Completed as plan	6,832,000
4.13.4	Follow up and inspect the social and environmental safeguards, provide training to the resettlement committee at village and district levels for the contract: W03 and W04. Vang Vieng, 27-30/6/2023	27-30/6/2023	Vang Vieng	To monitor the safeguards issues	PCU, TDD	5	1	#NAME?	7,794,000
4.13.4	Work with the district committee to measure land boundary to compensate affected families in Nakasang, Khong District, Champasak province 10-11/06/2023	10-11/6/2023	Khong dist, Champasak	To compensate affected families in Nakasang	PIU and district committee	18	5	Issues addressed	10,240,000
4.13.4	Follow up the social safeguards work with donor (ADB mission). Vang Vieng, VTP, 20-21/04/2023	20-21/4/2023	Vang Vieng, VTP	To follow up the progress	PCU, PIU, ADB, District Authorities	56	26	Completed as plan	22,500,000
4.13.4	Follow up and inspect the social and environmental safeguards, provide training on mechanism for resolution of complaints/suggestions to the resettlement committee at village and district levels. Vang Vieng, 28-30/06/2023	28-30/06/2023	Vang Vieng, VTP	To strengthen capacity to the resettlement committee	PCU, PIU and District Authorities	81	50	Completed as plan	7,490,000
4.13.4	Follow up the social safeguards work with donor (ADB) at Nam Ngum 1 subproject site. Keo Oudom district, VTP, 19/4/2023	19/4/2023	NamNgum1, Keo Oudom, VTP	Encourage and monitor the social safeguards issues	VTP-PIU, ADB, PCU	8	4	Implemented as plan	7,450,000

Budget Code	Activity	Date	Location	Objective	Implementing Personnel	Participants	Women	Results/Outcome/Comments	Budget (Kip/US)
4.13.4	Organize consultation workshop with villagers (affected people) on the development of resettlement areas with their own capital 10/05/2023	05/10/2023	NamNgum1, Keo Oudom, VTP	To be consensus	VTP-PIU	33	17	Implemented as plan	4,370,000
4.13.4	Organize consultation workshop with villagers (affected people) on the development of self-relocation. Keo Oudom dist. 26/5/2023	26/5/2023	Keo Oudom,	To be consensus	VTP-PIU	31	16	Implemented as plan	4,490,000
4.13.4	Organize consultation meeting on self resettlement model, final decision on electricity connection and water supply system access to the resettlement area for 19 households in Keo Oudom District, Vientiane Province, 26-27/05/2023	26-27/5/2023	Keo Oudom	To discuss the best sample	PCU/EA, TDD	0	2	Completed as plan	3,047,000
4.14.1	Work with SAO on annual financial - accounting audits for 2022. PIU Champasak, 28/05/2023-03/06/2023	28/5-3/6/2023	Champasak	To audit the project financial and accounting system	Implemented as plan	43	24	Implemented as plan	32,780,000
4.14.1	SAO's field mission to Vang Vieng regarding the project financial and accounting audits of 2022. Vang Vieng, 07-11/06/2023	7-11/06/2023	Vang Vieng, VTP	To audit the project financial and accounting system	PCU, SAO, PIU	41	19	Completed as plan	22,470,000
4.14.1	Organize meeting to review the implementation of the project workplan for the first 6-month of 2023, between PCU and PIU. VTP, 5-8/6/2023	5-8/6/2023	Keo Oudom,	To encourage and support	VTP-PIU	36	17	Implemented as plan	11,974,000
4.14.1	Field mission with the State Audit Organization (SAO) on the annual project financial-accounting audit for 2022, 18/5/2023 - 21/6/2023	18/5/2023 - 21/6/2023	VTE, CPS, VTP and VV	To audit the project financial and accounting system	PCU	7	6	Completed as plan	86,340,000
4.14.1	Work with the State Audit Organization (SAO) on the annual project financial-accounting audit for 2022, 18/5/2023 - 21/6/2023	18/5/2023 - 21/6/2023	VTE, CPS, VTP and VV	To audit the project financial and accounting system	SAO	7	4	Completed as plan	51,130,000

Annex 3: Progress towards DMF targets and activity implementation as of 30 June 2023

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
Outcome: Tourism competitiveness of secondary towns in Cambodia and the Lao PDR increased	By 2025			
	e. Cambodia and the Lao PDR's share of ASEAN international visitor arrivals increased (2016 baseline)	3.7%	3.8%	2017: 3.1% 2018: 3.1% 2019: 3.3% 2020: 3.4% 2021: no data 2022: no data
	f. Annual international visitor arrivals in project areas increased (2016 baseline)	820,100	1,263,100	2017: 941,000 2018: 1,210,800 2019: 1,260,000 2020: 331,356 2021: no data (negligible due to COVID-19 pandemic country closure) 2022: 437,481
	g. Aggregate annual visitor expenditure in project areas increased (2016 baseline)	\$380.2 million <i>corrected from \$363.9 million</i>	\$589.0 million	2017: \$337.4 million 2018: \$385.5 million 2019: \$474.3 million 2020: \$133.1 million 2021: no data (negligible due to COVID-19 pandemic country closure) 2022: data not yet available
	h. Women comprise at least 55% of tourism workers in project areas (2016 baseline)	50%	55%	Female workers account for 57% of the total workforce in Lao PDR's tourism and hospitality sector. ³ Champasak Province: 55.9% Vientiane Province: 57.5% Luang Prabang Province: 52.1% Aggregate for the three target provinces: 54.3% This indicator corresponds to Gender Action Plan Target 1

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
Outputs	By 2024:					

³ Ministry of Education and Sports, Lao PDR. 2021. *Tourism and Hospitality Enterprise Survey of Employment and Skills in Lao PDR*. Vientiane.

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
1. Urban-rural access infrastructure and urban environmental services improved	1a. 73 km of access roads to tourist sites improved (2017 baseline)	0	62.6 km	10%	33.73 km	<p><u>Two out of 4 awarded packages are on-track, 2 delayed.</u></p> <p>Contract for Package TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements was signed on 30 December 2019. This package includes 20.99 km of improvement of access roads to tourist sites. The works have been completed 100%, including 21.11km road improvement.</p> <p>Contract for Package TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements was signed on 26 April 2021. It includes 7.3 km of concrete road. Progress was 60.5%. So far, 5.49Km road is fully completed.</p> <p>Contract for Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements was signed on Contract was signed on 23 July 2021. It includes 6.00 km of concrete road and 26.6 km of DBST road totaling 32.6 km of road improvement. Progress was 56.27%. So far, 5.50Km road is fully completed.</p> <p>Contract for Package TIIGP2-LAO-W03a: Vang Vieng Urban Renewal. The DED was prepared, and endorsed by ADB. Includes 0.67 km of concrete road and 0.39 km of DBST road totaling 1.05 km of road improvement. Commencement of the procurement process to be confirmed in Q3 2023 subject to the progress of Contracts TIIGP2-LAO-W02 and TIIGP2-LAO-W03 and modification of the DED.</p> <p>Contract for package TIIGP2-LAO-W04: Vang Vieng Landfill Improvements was signed on 19 February 2021. It includes 1.55 km of access and internal roads. Progress was 75.37%. So far, 1.53Km road is fully completed.</p> <p>A total 63.61 Km road will be improved under these 5 Works packages. Out of 63.61 Km, 33.76 Km of Access Road has been completed (approx. 53% of target)</p>

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
	1b. 4 ferry ports constructed (2016 baseline)	0	2	10%	1	<p>One of 2 awarded packages is on track, one is delayed.</p> <p>Contract for package TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements was signed on 30 December 2019 includes improvement of 1 ferry port. Overall progress of the contract is 100%.</p> <p>Contract for Package TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements was signed on 26 April 2021 includes passenger/ferry port improvement. Overall progress of the contract is 60.15%.</p> <p>A total of 2 passenger/ferry ports will be improved.</p>
	1c. 30 m3/day wastewater treatment capacity constructed (2017 baseline)	0 m3/day	15 m3/day	10%	0	<p>On Track</p> <p>Contract for package TIIGP2-LAO-W04: Vang Vieng Landfill Improvements was signed on 19 Feb 2021. Overall progress of the subproject is 75.37%.</p> <p>This package includes 20m3/day septage sludge treatment facility.</p> <p><i>Additional wastewater treatment capacity under construction under Packages W02 and W03 (Kaeng Yui) will be quantified and added.</i></p>
	1d. Flood protection and drainage constructed for 25-hectare catchment (2017 baseline)	0 ha	24.5 ha	10%	0	<p>On track</p> <p>Contract for package TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements was signed on 30 December 2019 includes 0.5 ha catchment area of flood protection and drainage improvement.</p> <p>Detailed design for package TIIGP2-LAO-W03a: Vang Vieng Urban Renewal was completed during the first half of 2020. This package includes 24 ha catchment area of flood protection and drainage improvement. Commencement of the procurement process to be confirmed in Q3 2023.</p> <p>The project will construct flood protection and drainage for a total of 24.5 ha catchment.</p>

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
	1e. Solid waste management services improved for 5,700 households and businesses (2017 baseline)	1,628	4,100	20%	0	<p>On track Together with construction of landfill under package TIIGP2-LAO-W04: Vang Vieng Landfill Improvements, the project will support improving institutional capacity for enhanced solid waste management in Vang Vieng.</p> <p>The targeted number of households and businesses for improved solid waste management services is 4,100 (number of beneficiaries to be confirmed).</p>
	1f. At least 50% of people consulted to optimize project infrastructure design inclusiveness and gender responsiveness are women (2017 baseline)	0%	50%	10%	50.4%	<p>Achieved 119 (50.4%) out of 236 people consulted are women. Consultations held to date during detailed design preparation, updating of safeguards documents, development of O&M plans for 4 civil works subprojects.</p> <p>Additional consultations are planned, in which women participation will be encouraged to ensure the target of 50% will be maintained. This indicator corresponds to Gender Action Plan Target 3.</p>
2. Capacity to implement ASEAN tourism standards strengthened	2a. 2 national ASEAN tourism standards assessment frameworks and certification boards established with at least 30% women board members (2017 baseline)	0	1	2%	1	<p>Achieved 1 national assessment framework established comprising:</p> <ul style="list-style-type: none"> ○ National and Provincial Assessment and Certification Committees (equivalent to certification boards) for all 7 ASEAN Tourism Standards ○ ASEAN Tourism Standards (5 of them adapted to Lao national context) in English and Lao languages ○ Assessment and certification manuals for all 7 standards

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
	2a-g At least 30% of the standards assessment frameworks and certification board members are women		30%	1%	41%	<p>Achieved National and provincial tourism standard assessment committees (equivalent to the “certification bodies” referred to in the PAM) have been set up for all 7 standards, with this count of membership: Overall, 43.0% (86 out of 200 certification board members are women)</p> <p>National: 51.06% (48 women out of 94 members and assessors):</p> <ul style="list-style-type: none"> • ASEAN Green Hotel: 61.53% (8 women out of 13); dated 21/07/2021 • ASEAN Spa Service: 63.63% (7 out of 11); dated 21/07/2021 • ASEAN Homestay Standard: 33.33% (3 out of 9); dated 27/08/2021 • ASEAN Public Toilet Standard: 44.44% (4 out of 9) (official appointment awaiting signature) • ASEAN Clean City Standard: 47.05% (8 out of 17); dated 11/08/2021 • ASEAN CBT Standard 22.22% (2 out of 9) dated 14/09/2021, Not Achieved • ASEAN MICE Standard: 61.54% (8 out of 13); dated 25/06/2021 • ASTA: 61.53% (8 out of 13) 09/2021 (waiting for signature) <p>Provinces: 35.84% (38 women out of 106 members and assessors):</p> <ul style="list-style-type: none"> • Champasak Province: 34% (14 out of 41) dated 22 June 2021 • Vientiane Province: 33% (6 out of 18); dated 22/07/2021 • Vang Vieng District: 30 % (9 out of 30); dated 14/06/2021 • Luang Prabang Province: 53% (9 out of 17); dated 20/09/2022 <p>This indicator corresponds to Gender Action Plan Target 10.</p>

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)																																																
	2b. 107 hotels in target provinces ASEAN Green Hotel Standard certified (2017 baseline)	24 2017 baseline corrected from 29 to 24	64	2%	32 (out of which 8 are active and 24 are expired)	<p>Ongoing Out of the 32 hotels that have been certified since 2008, 8 have active certification, the others are expired.</p> <table border="1"> <thead> <tr> <th>Province</th> <th>Issued</th> <th>Expired</th> <th>Valid</th> </tr> </thead> <tbody> <tr> <td>Luang Prabang</td> <td>13</td> <td>10</td> <td>3</td> </tr> <tr> <td>Champasak</td> <td>14</td> <td>12</td> <td>2</td> </tr> <tr> <td>Vientiane Province</td> <td>5</td> <td>2</td> <td>3</td> </tr> <tr> <td>Total</td> <td>32</td> <td>24</td> <td>8</td> </tr> </tbody> </table> <p>An effort is being made to re-certify the expired properties, along with certification of additional properties, as follows:</p> <table border="1"> <thead> <tr> <th colspan="4">ASEAN Green Hotel Standard certification plan</th> </tr> <tr> <th></th> <th>Planned for 2024/5</th> <th>Certified*</th> <th>Remaining</th> </tr> </thead> <tbody> <tr> <td>Luang Prabang</td> <td>27</td> <td>13</td> <td>14</td> </tr> <tr> <td>Vientiane Province</td> <td>5</td> <td>1</td> <td>4</td> </tr> <tr> <td>Vang Vieng</td> <td>13</td> <td>4</td> <td>9</td> </tr> <tr> <td>Champasak</td> <td>22</td> <td>14</td> <td>8</td> </tr> <tr> <td>Total</td> <td>67</td> <td>32</td> <td>35</td> </tr> </tbody> </table> <p>* "Certified" includes expired certifications that are being renewed</p>	Province	Issued	Expired	Valid	Luang Prabang	13	10	3	Champasak	14	12	2	Vientiane Province	5	2	3	Total	32	24	8	ASEAN Green Hotel Standard certification plan					Planned for 2024/5	Certified*	Remaining	Luang Prabang	27	13	14	Vientiane Province	5	1	4	Vang Vieng	13	4	9	Champasak	22	14	8	Total	67	32	35
Province	Issued	Expired	Valid																																																			
Luang Prabang	13	10	3																																																			
Champasak	14	12	2																																																			
Vientiane Province	5	2	3																																																			
Total	32	24	8																																																			
ASEAN Green Hotel Standard certification plan																																																						
	Planned for 2024/5	Certified*	Remaining																																																			
Luang Prabang	27	13	14																																																			
Vientiane Province	5	1	4																																																			
Vang Vieng	13	4	9																																																			
Champasak	22	14	8																																																			
Total	67	32	35																																																			

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)																												
	2c. 148 homestays ASEAN Homestay Standard certified (2017 baseline)	23	113	2%	45 (42 in 4 certified homestay villages + 3 homestay service providers in CBT Standard certified villages)	<p>Ongoing 4 homestay villages certified in target provinces, with a combined number of 42 service providers, all are valid:</p> <ol style="list-style-type: none"> 1) Ban Naduang (Kaeng Nyui waterfall site), Vang Vieng District, Vientiane Province (8 Homestays) 2) Ban Hua Don Deng (Don Deng Island), Pa Thoumphone District, Chamapasak Province (6 Homestays) 3) Ban Don Kho (Don Kho Island), Xanasomboun District, Champasak Province (9 Homestays) 4) Ban Nayang Tai, Nambak District, Luang Prabang Province (19 Homestays) <p>An effort is being made in 2022-2024 to certify additional homestay providers in other homestay villages, as follows:</p> <table border="1" style="margin-left: 20px;"> <thead> <tr> <th colspan="4">ASEAN Homestay Standard certification plan</th> </tr> <tr> <th></th> <th>Planned for 2024/5</th> <th>Certified*</th> <th>Remaining</th> </tr> </thead> <tbody> <tr> <td>Luang Prabang</td> <td>55</td> <td>19</td> <td>36</td> </tr> <tr> <td>Vientiane Province</td> <td>18</td> <td>0</td> <td>18</td> </tr> <tr> <td>Vang Vieng</td> <td>24</td> <td>8</td> <td>16</td> </tr> <tr> <td>Champasak</td> <td>36</td> <td>18**</td> <td>18</td> </tr> <tr> <td>Total</td> <td>133</td> <td>45</td> <td>88</td> </tr> </tbody> </table> <p>* "Certified" includes expired certifications that are being renewed ** Includes homestays certified under Homestay Standard and CBT Standard</p> <p>The target for Homestays will be formally reviewed by the end of 2023.</p>	ASEAN Homestay Standard certification plan					Planned for 2024/5	Certified*	Remaining	Luang Prabang	55	19	36	Vientiane Province	18	0	18	Vang Vieng	24	8	16	Champasak	36	18**	18	Total	133	45	88
ASEAN Homestay Standard certification plan																																		
	Planned for 2024/5	Certified*	Remaining																															
Luang Prabang	55	19	36																															
Vientiane Province	18	0	18																															
Vang Vieng	24	8	16																															
Champasak	36	18**	18																															
Total	133	45	88																															

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
	2d. At least 6 towns ASEAN Clean City Standard certified (2017 baseline)	1	3	8%	2 (both active)	On track 1. Luang Prabang City, Luang Prabang Province, was certified in 2018, renewed in 2022. 2. Pakse City, Champasak Province, was certified in 2022. 3. Vang Vieng Town, Vientiane Province, is working towards certification in 2024/2025.
3. Institutional capacity for tourism destination management and infrastructure O&M strengthened	3a. 150 public works and tourism site managers (at least 30% women) reporting increased knowledge on developing and implementing tourism management and infrastructure O&M plans (2017 baseline)	0	90	1%	200	On Track Q2 2023: (April-June 2023) -W01: (1) Consultation Workshop with Khong District Authority (5 April 2023) total: 13 (4 women); (2) Consultation Workshop with Nakasang, Phiengdy communities (8 April 2023) total: 14 (4 women); (3) Final Consultation Meeting with Khong District Authority (7-8 June 2023) total: 6 (2 women). -W03: Consultation Meeting on Site Management and O&M Plan for Kaeng Yui Waterfall, Vang Vieng District (10 May 2023) total 32 (9 women) -W04: Development Partner meeting (13 June 2023) total: 12 (6 women) Q2 2023: total 78 (25 women) As of March 2023, total 200 (61 women)
	3a-g At least 30% of the public works and tourism site managers reporting increased knowledge are women	0	30%	1%	30.5%	Achieved Out of the 200 public works 61 (30.5%) were women. This indicator corresponds to Gender Action Plan Target 21.
	3b. 8 destination management plans and 8 infrastructure O&M plans implemented (2017 baseline)	3	4	5%	5	On track Five destination management plans completed (Lao PDR, Luang Prabang, Southern Laos, Vang Vieng, and Vientiane Province and under implementation. Preparation of O&M plan development for subprojects in 4 awarded civil works contracts (W01, W02, W03, W04) commenced, with the O&M plan for W01 in final draft version.

Result Chain	Performance Indicators	Baseline (Lao PDR)	Targets (Lao PDR)	Weight (%)	Achievement as of 30 June 2023 (Lao PDR)	Progress as of 30 June 2023 (Lao PDR)
	3c. At least 5,000 residents and tourism workers (50% women) participated in destination management training and awareness-raising activities (2017 baseline)	0	3,000	2%	5,733	Achieved To date, 5,733 participants (residents and tourism workers) have participated in destination management training and awareness-raising activities.
	3c-g 50% of residents and tourism workers participated in the training and awareness raising activities are women.	0	50%	1%	46.1%	Not achieved Of the 5,733 residents and tourism workers who have participated in destination management training and awareness-raising activities, 2,643 (46.1%) were women. <i>Efforts will be made to increase women participation in future destination management training and awareness-raising activities to reach the 50% target for this indicator.</i> <i>This indicator corresponds to Gender Action Plan Target 14.</i>
	3d. At least 500 entrepreneurs (60% women) received SME support services (2017 baseline)	0	300	2%	0	On track SME needs assessments were conducted in 2022. Preparation of SME development plan completed . Roll out will commence in Q3 2023. <i>This indicator corresponds to Gender Action Plan Target 4.</i>
	3d-g 60% of entrepreneurs received SME support services are women	0	60%	1%	0	On track SME needs assessments were conducted in 2022. Preparation of SME development plan completed . Roll out will commence in Q3 2023. <i>Data available to date: As of September 2022, the project conducted training on SME services and other SME related activities with participation of 2,390 with 1,152 people, (48.2%) women.</i> <i>This indicator corresponds to Gender Action Plan Target 4.</i>
	3e. 2 internet-based tourism knowledge repositories developed (2017 baseline)	0	1	2%	1	On track Internet-based tourism repository developed and the project continues to upload the information. DMN website https://www.laos-dmn.com .

Key Activities with Milestones	Progress as of 30 June 2023
1. Urban-rural access infrastructure and environmental services improved	
1.1 Prepare civil works design and bidding documents: Q2 2018–Q4 2019	<ul style="list-style-type: none"> • Package TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements (subprojects C1 and C2): Completed Q3 2019. • Package TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements (subproject V1): Detailed design and bidding documents completed in August 2020. DPWT/Vientiane province provided clearance of DED in September 2020. • Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements (subprojects V2 and V3): Detailed design and bidding documents completed in August. DPWT/Vientiane province provided clearance of DED in November 2020. • TIIGP2-LAO-W03a: Vang Vieng Urban Renewal (subproject V4): Detailed design completed in August 2020. Procurement on hold. • Package TIIGP2-LAO-W04: Vang Vieng Landfill Improvements (subproject V5): Detailed design and bidding documents completed in September 2020, DPWT/Vientiane province provided clearance of DED in November 2020.
1.2 Safeguards document approval: Q4 2018–Q4 2019	<ul style="list-style-type: none"> • Package TIIGP2-LAO-W01 (subprojects C1 and C2): updated IEE/EMP and Resettlement Due Diligence Report approved and included, as appropriate, in bidding documents and contract. • Package TIIGP2-LAO-W02: (subproject V1): Updated RP and IEE/EMP report approved and included in the bidding document and contract, however, RP has been revised after contract award following discovery of major flaws in earlier approved version (latest approved version is June 2023). PONRE/Vientiane Province issued Environmental Compliance Certificate (ECC) on (IEE/EMP) on 7 September for the period of 1 September 2020 to 31 August 2021. ECC has been renewed. • Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements (subprojects V2 and V3): Updated EGDRP and IEE/EMP report approved and included, as appropriate, in bidding documents and contract. PONRE/Vientiane Province issued Environmental Compliance Certificate (ECC) on IEE/EMP. • TIIGP2-LAO-W03a: Vang Vieng Urban Renewal (subproject V4): RP and IEE/EMP to be updated once package gets green light. • Package TIIGP2-LAO-W04: (Subproject V5): Updated of IEE/EMP based on ECA and EGDRP report approved and included, as appropriate, in bidding documents and contract. PONRE/Vientiane Province issued Environmental Compliance Certificate (ECC) on (IEE/EMP) on 22 December for the period of 21 December 2020 to 20 December 2021. ECC has been renewed.

Key Activities with Milestones	Progress as of 30 June 2023
1.3 Complete land acquisition and resettlement: Q1 2020	<ul style="list-style-type: none"> • Package TIIGP2-LAO-W01 (subprojects C1 and C2): N/A. LAR CAPs for Phase 1 and 2 prepared and implementation completed, Compensation Completion Report submitted. • Package TIIGP2-LAO-W02: (subproject V1): RP revision completed (latest version June 2023), compensation payment phase 1 and phase 2 and allowance for self-relocation for eligible AHs completed. • Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements (subprojects V2 and V3): Compensation payments based on EGDRP made and Compensation Completion Report submitted. • TIIGP2-LAO-W03a: Vang Vieng Urban Renewal (subproject V4): RP pending decision on if and when to proceed with this subproject. • Package TIIGP2-LAO-W04: (Subproject V5): Compensation payments based on EGDRP completed and Compensation Completion Report submitted.
1.4 Civil works procurement: Q4 2018–Q4 2020	<ul style="list-style-type: none"> • Package TIIGP2-LAO-W01 (subprojects C1 and C2): Completed. Contract signed 30 December 2019. • Package TIIGP2-LAO-W02: (subproject V1): Completed. Contract signed 20 April 2021. • Package TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements (subprojects V2 and V3): Completed. Contract signed 23 July 2021. • TIIGP2-LAO-W03a: Vang Vieng Urban Renewal (subproject V4): Package on hold. • Package TIIGP2-LAO-W04: (Subproject V5): Completed. Contract signed 19 February 2021.
1.5 Civil works construction, supervision, and supply equipment: Q1 2019–Q1 2023	<ul style="list-style-type: none"> • Package TIIGP2-LAO-W01 (subprojects C1 and C2): Commenced on 26 May 2020, completed 30 June 2023. • Package TIIGP2-LAO-W02: (subproject V1): Commenced on 1 July 2021. • Package TIIGP2-LAO-W03: (subprojects V2, V3): Commenced on 1 September 2021. • Package TIIGP2-LAO-W03a: (subproject V4): Package on hold. • Package TIIGP2-LAO-W04: (Subproject V5): Commenced on 19 April 2021. Procurement of equipment ongoing.
2. Capacity to implement ASEAN tourism standards strengthened	
2.1 Establish ASEAN tourism standards assessment frameworks and certification boards: Q1 2018–Q4 2019	<ul style="list-style-type: none"> • All seven ASEAN Tourism Standards translated into Lao and published • ASEAN Clean Tourist City, Homestay, Community-Based Tourism, Public Toilet, Spa Service Standards and MICE Venue Standards adapted to Lao national context and are available in both Lao and English. • Green Hotel will not be adapted but will be used in its original form in Lao PDR.
2.2 Prepare national certification boards and assessor operations manuals: Q2 2019–Q4 2021	<ul style="list-style-type: none"> • Assessment frameworks consist of: (i) the respective Standard (see 2.1 above); (ii) the Auditor's manual for each Standard and (iii) the Certification Committees. • Auditor (assessment and certification) manuals have been prepared for all seven pure ASEAN standards. • National Committees have been established, responsible for audits and implementation (for the Clean Tourist City Standard there are two National Committees: one for the Audit process and one for Implementation). • In each project target province, one Provincial Committee has been established responsible for all standards.

Key Activities with Milestones		Progress as of 30 June 2023
2.3	Train standards assessors (e.g. Green Hotel, Homestay, Clean City, etc.): Q3 2019–Q2 2022	<ul style="list-style-type: none"> • There are seven ASEAN Master Trainers within MICT who can train trainers and assessors from the Provincial Assessment Committees. • Numerous training of trainers and training of national and provincial-level assessors conducted and will be repeated throughout the life of the project.
2.4	Promote ASEAN tourism standards adoption by service enterprises and cities: Q3 2019–Q4 2023	<ul style="list-style-type: none"> • Dissemination workshops with public and private sector participants conducted for all seven ASEAN Tourism Standards in key target destinations • Follow up promotional activities in project target provinces ongoing. • Launch of the Lao ASEAN Tourism Standards website scheduled for September 2023.
2.5.1	Prepare implementation plans for ASEAN Tourism Standards: Q4 2019–Q4 2020	<ul style="list-style-type: none"> • Implementation plans are prepared.
2.5.2.1	Standards inspection and certification: Q4 2019–Q4 2023	<ul style="list-style-type: none"> • (Re-)Assessments are ongoing.
2.5.2.2	Support public sector implementation of ASEAN Tourism Standards (e.g. ASEAN Clean City Standard, ASEAN Public Toilet Standard): Q1 2020–Q4 2023	<ul style="list-style-type: none"> • Support for public sector implementation of ASEAN Public Toilets standard has been completed and for the ASEAN Clean Tourist City standard, ASEAN Homestay standard and ASEAN CBT standard ongoing. • Action Plan for achieving Clean Tourist City Standard by Vang Vieng will be revised in Q3, 2023
3. Institutional capacity for tourism destination management and infrastructure O&M strengthened		
3.1	Establish and strengthen destination management networks: Q2 2019–Q4 2019	<ul style="list-style-type: none"> • DMNs for Lao PDR, Luang Prabang and Southern Laos reviewed and membership updated and DMNs for Vientiane Province and Vang Vieng established in 2019 • DMNs strengthened through training and exchanges. • National level public and private sector action plans on joint destination management for 2021, 2022, 2023 prepared and implemented with various partner organizations. The process is replicated in the project provinces. DMNs have also been restructured ensuring more private sector participation, as well as a better gender balance.
3.2	Prepare and approve tourism destination management plans: Q2 2019–Q2 2023	<ul style="list-style-type: none"> • DMPs, including action plans, for all five project target destinations completed by Q4 2019.
3.3	Support policy dialogue, development of industry standards and regulations and tourism masterplanning: Q4 2019–Q1-2022	<ul style="list-style-type: none"> • DMN Policy Taskforces meet regularly to identify and discuss policy issues affecting tourism sector in project target destinations. • Drafting of various regulations to manage and control tourist activities in target destinations completed and ongoing. • Tourism masterplanning for Siphandone (Champasak), Luang Prabang town and Nam Ngum 1 Dam Recreational Area (Vientiane Province) commenced in Q1 2020 and was scheduled to be completed by Q4 2020, but was delayed due to COVID-19 – now re-started, with Luang Prabang scheduled for completion by Q4 2023 and Siphandone and Nam Ngum by Q2 2024. Tourism masterplan update for Vang Vieng completed in Q3 2023.

Key Activities with Milestones	Progress as of 30 June 2023
3.4 Support destination marketing and promotion: Q1 2020-Q1 2024	<ul style="list-style-type: none"> Information, image and video collection to build up the Lao PDR tourism media database started in 2019 and is ongoing. Destination Laos tourism market research completed and marketing plan prepared. Implementation commenced in 2023.
3.5 Support heritage interpretation planning and implementation Q1 2020-Q1 2023	<ul style="list-style-type: none"> Preparation of heritage interpretation strategies for Siphandon (Champasak), Luang Prabang Town and Environs, Vientiane Province and Vang Vieng Town and Environs completed in Q2 2020. Preparation of detailed implementation plan for Luang Prabang and Siphandone completed, Implementation in Luang Prabang has started. Preparation of detailed implementation plans for Vang Vieng and Nam Ngum commenced.
3.6 Design and implement SME training Q2 2020-Q4 2023	<ul style="list-style-type: none"> Needs assessments are completed related to support for SMEs suffering from the COVID-19 situation. Detailed SME assessments in project target areas completed Q4 2022. SME development plan drafted, to be finalized Q3 2023. Roll out of SME support based on SEM development plan in 2024.
3.7 Establish and maintain Internet-based tourism knowledge repositories: Q1 2020-Q2 2024	<ul style="list-style-type: none"> Laos DMN website developed (www.laos-dmn.com), incorporating document repository allowing users to easily search for documents. The contents are being uploaded.
3.8 Prepare and approve infrastructure O&M plans with sustainable finance mechanisms: Q3 2020-Q4 2023	<ul style="list-style-type: none"> O&M planning is ongoing, alongside civil works detailed design and construction.
3.9 Facilitate public-private partnerships for O&M: Q1 2021-Q4 2023	<ul style="list-style-type: none"> PPP planning ongoing, initially for landfill operation
3.10 Design and implement training programs for infrastructure O&M: Q1 2021-Q2 2024	<ul style="list-style-type: none"> Needs assessment for landfill subproject completed and capacity building plan being implemented
Project Management Activities	
Establish project steering committees, PCUs, and PIUs: Q2 2018- Q4 2018	<ul style="list-style-type: none"> Completed. National Project Steering Committee and Provincial Project Steering Committees. PCU and PIUs established.
Advance actions for consultant recruitment and procurement: Q2 2018-Q1 2019	<ul style="list-style-type: none"> Completed: advance actions were undertaken during Q3-4 of 2018 for the recruitment of the Project Management and Engineering Support Consultant (PMCES), and four individual consultants: International Tourism Specialist – Co-Team Leader, National Tourism Specialist – Deputy Team Leader, and the International and National Financial Management and Procurement Specialists, and for the procurement of PCU and PIU vehicles.
Mobilize consultants and procure equipment: Q1 2019-Q2 2020	<ul style="list-style-type: none"> Completed – all planned consultants recruited and mobilized.
Establish financial management systems: Q2 2019-Q1 2020	<ul style="list-style-type: none"> Completed: <ul style="list-style-type: none"> Financial management team appointed and mobilized Financial management and procurement consultants recruited and mobilized Financial Management Manual prepared Accounting software has been procured and is operational

Key Activities with Milestones	Progress as of 30 June 2023
Financial management and procurement training for PCU and PIU staff: Q1 2019–Q4 2019	<ul style="list-style-type: none"> • PCU staff is receiving on-the-job training • International and National Financial Management and Procurement Specialists recruited and mobilized and are building capacity of project financial management team. • PCU financial management team has opportunities to participate in training at ADB LRM.
Implement sex-disaggregated PPMS, safeguards, and gender action plans: Q1 2019–Q4 2024	<ul style="list-style-type: none"> • Project Performance Monitoring System (PPMS) completed and being used • International and National Gender Specialists are supporting the project with GAP implementation. • Safeguards experts are supporting project with updating and implementation monitoring of social and environmental safeguards documents.
Conduct project planning, monitoring, evaluation and reporting: Q4 2018-Q4 2024	<ul style="list-style-type: none"> • Annual costed workplans are prepared and implemented • Project Performance Monitoring System completed and being used • Quarterly progress reports are being prepared and submitted to relevant government units and ADB, and published on the project website.

Annex 4: Weighted implementation table with progress as of 30 June 2023

No.	Activities	incompleted activities																completed activities (all in past)								(a) Progress (%)	(b) Assigned Weight (%)	(a) x (b) Weighted Progress (%)				
		1 future, orig. plan				2 past, orig. plan (not done)				3 past, actual, orig. plan				4 past, actual, unplanned				5 future, latest plan				6 past, actual, orig. plan							7 past, actual, unplanned			
		2018				2019				2020				2021				2022				2023				2024						
		Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4			
A.	Design and Monitoring Framework																															
	Output 1: Last-mile tourism access infrastructure improved																															
	TIIGP2-LAO-W01 Nakasang and Don Det-Don Khone Access Improvements																															
	1.1 Prepare civil works design and bidding documents																															
	1.2 Safeguards document approval																															
	1.3 Complete land acquisition and resettlement																															
	1.4 Civil works procurement																															
	1.5 Implement civil works construction, supervision, and supply equipment																															
	TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements																															
	1.1 Prepare civil works design and bidding documents																															
	1.2 Safeguards document approval																															
	1.3 Complete land acquisition and resettlement																															
	1.4 Civil works procurement																															
	1.5 Implement civil works construction, supervision, and supply equipment																															
	TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements																															
	1.1 Prepare civil works design and bidding documents																															
	1.2 Safeguards document approval																															
	1.3 Complete land acquisition and resettlement																															
	1.4 Civil works procurement																															
	1.5 Implement civil works construction, supervision, and supply equipment																															
	TIIGP2-LAO-W03a: Vang Vieng Urban Renewal																															
	1.1 Prepare civil works design and bidding documents																															
	1.2 Safeguards document approval																															
	1.3 Complete land acquisition and resettlement																															
	1.4 Civil works procurement																															
	1.5 Implement civil works construction, supervision, and supply equipment																															
	TIIGP2-LAO-W04: Vang Vieng Landfill Improvements																															
	1.1 Prepare civil works design and bidding documents																															
	1.2 Safeguards document approval																															
	1.3 Complete land acquisition and resettlement																															
	1.4 Civil works procurement																															
	1.5 Implement civil works construction, supervision, and supply equipment																															
	Subtotal Output 1:																															

		incompleted activities												completed activities (all in past)																				
		1 future, orig. plan				3 past, actual, orig. plan				6 past, actual, orig. plan																								
		2 past, orig. plan (not done)				4 past, actual, unplanned				7 past, actual, unplanned																								
						5 future, latest plan																												
No.	Activities	2018				2019				2020				2021				2022				2023				2024				(a) Progress (%)	(b) Assigned Weight (%)	(a) x (b) Weighted Progress (%)		
		Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4					
A.	Design and Monitoring Framework																																	
	Output 2: Capacity to Implement ASEAN Tourism Standards Strengthened																															8.43%		
	2.1 National ASEAN Tourism Standards adaptation																															97.9%	1.00%	0.98%
	2.2 Establishment of certification bodies and processes																															96.0%	1.00%	0.96%
	2.3 Assessor training																															95.2%	1.00%	0.95%
	2.4 ASEAN Tourism Standards promotion																															78.5%	1.00%	0.79%
	2.5 Implement ASEAN Tourism Standards and the ASEAN Sustainable Tourism																															79.2%	6.00%	4.75%
	Subtotal Output 2:																															10.00%		8.43%
	Output 3: Output 3: Institutional Arrangements for Tourism Destination Management and Infrastructure O&M Strengthened																																	
	Capacity building for tourism destination management																															7.00%		4.98%
	3.1 Destination management network institutional strengthening																															99.2%	1.00%	0.99%
	3.2 Destination management plan preparation																															100.0%	1.00%	1.00%
	3.3 Policy, Regulation and Master Planning Support																															84.8%	1.00%	0.85%
	3.4 Destination Marketing and Promotion Support																															64.6%	1.00%	0.65%
	3.5 Heritage Interpretation Support																															60.7%	1.00%	0.61%
	3.6 Tourism-related SME development																															32.4%	1.00%	0.32%
	3.7 Establish and maintain internet-based tourism knowledge repositories																															56.0%	1.00%	0.56%
	Capacity building for infrastructure O&M																															3.00%		0.87%
	3.8 Develop infrastructure O&M plans with sustainable finance mechanisms																															50.0%	1.00%	0.50%
	3.9 Facilitate Public-Private Partnerships for operations and maintenance																															23.8%	1.00%	0.24%
	3.10 Infrastructure O&M training																															12.8%	1.00%	0.13%
	Subtotal Output 3:																															10.00%		5.84%
B.	Management Activities																																	
	Establish project supervision and management structure																															100.0%	1.00%	1.00%
	Mobilize consultants and procure equipment																															100.0%	1.00%	1.00%
	Establish financial management arrangements																															100.0%	1.00%	1.00%
	Financial management and procurement training																															100.0%	1.00%	1.00%
	Finalize monitoring arrangements and establish the project website																															100.0%	1.00%	1.00%
	Conduct project planning, monitoring, evaluation and reporting																															79.2%	1.00%	0.79%
	Implementation of environmental, social safeguards and the gender action plan																															77.3%	4.00%	3.09%
	Subtotal Management Activities:																															10.00%		8.88%
	Total																															100.00%		72.49%

Annex 5: Project Financial Management Action Plan progress as of 30 June 2023

Planned Action	Output	Responsible Party	Due Date	Progress	Status of compliance
1. PCU and PIU financial management teams established.	<ul style="list-style-type: none"> Appointment or recruitment of qualified and experienced: PCU national director and PIU project managers; PCU financial controller; PCU and PIU accounting staff, as specified in the PAM. 	EA and IAs	Prior to ADB Board approval of project	<p>Board approval was 31 August 2018.</p> <p>PCU financial management team was established on 18 February 2019 (ref. MICT letter to ADB Ref. Nr. 068/TIIG2-19, dated 19 February 2019). PCU financial management team comprises financial controller (govt. staff), chief accountant (externally recruited, replacement, contract signed 1 November 2021) and internal auditor (externally recruited, contract signed 18 February 2019).</p> <ul style="list-style-type: none"> PIU Champasak finance and accounting staff recruited and commenced on 1 March 2019 PIU Vientiane province finance and accounting staff recruited and commenced on 1 March 2019 PIU Vang vieng finance and accounting staff recruited and commenced on 1 March 2019 PIU Luang Prabang finance and accounting staff recruited and commenced on 1 March 2019 	Completed with delay
2. National Steering Committee established.	<ul style="list-style-type: none"> Project oversight comprised of representatives from national level and participating provinces (Champasak, Luang Prabang and Vientiane), as specified in the PAM. 	EA and IAs	Coincide with ADB Board approval of project	<p>Board approval was on 31 August 2018.</p> <ul style="list-style-type: none"> A 7-member National Project Steering Committee (NPSC), comprising the Vice Minister for Tourism, MICT (Chair), the Director General, Tourism Marketing Department (Vice Chair) and five other senior officials representing various departments of MICT has been established and meets periodically to review progress (ref. MICT letter no. 792 dated 8 Sept 2021). In contrast to what the PAM specifies, MOF, MONRE, MPWT, Lao Women's Union, and representatives from the target provinces, are not on the NPSC, but they are invited to NPSC meetings as appropriate. Further, the project has also established Provincial Steering Committees (PSC) in Champasak, Luang Prabang and Vientiane Province, chaired by the Vice Provincial Governor. In provinces with infrastructure subprojects (Champasak and Vientiane Province), PSC include representatives from DPWT. In districts where infrastructure subprojects are located (Khong, Keo 	Completed

Planned Action	Output	Responsible Party	Due Date	Progress	Status of compliance
				<p>Oudom and Vang Vieng), district-level committees have been established, chaired by the Vice District Governor, with representatives from OICT, OPWT, and ONRE, and in Vang Vieng also the UDAA, to support the implementation of civil works.</p> <p>As of 13 July 2021, the NPSC composition has been revised and comprises the Vice Minister for Tourism, MICT (Chair), DGs of MICT's Planning and International Cooperation Department, Tourism Management Department, Finance Department and Tourism Development Department, and the Deputy DDG of MICT's Cabinet Office (Ref. 792/TIIG2-21, 08/09/2021).</p> <ul style="list-style-type: none"> • A 11-member project coordination committee has also been established, chaired by the project director, with members from various departments and units in MICT involved in project implementation (ref. 207/TWT, 07/03/2018). • Further, the project has established a permanent bid evaluation and consultant selection committee. 	
3. Project funds flow arrangements adopted & operational.	<ul style="list-style-type: none"> • As outlined in the PAM • MOF, EA, PCU, and PIU staff briefed on funds flow arrangements, advance account opened, and project sub-accounts established. 	MOF, EA, PCU, and PIUs assisted by financial management and procurement consultants	Prior to initial disbursement.	<p>The project met condition for withdrawal from the grant account stated in para. 4 of Schedule 2 of Grant Agreement, which ADB acknowledged on 20 February 2019 and advance to the advance account was disbursed on 2 April 2019. MICT has adopted the fund flow arrangement outlined in the PAM without modifications in coordination with MOF and MICT. PCU and PIUs have been briefed on the funds flow arrangements by the financial management consultants. PCU has opened an advance account and PIUs have opened sub-accounts</p>	<p>Completed by due date</p> <p>ADB processed and approved initial disbursement to advance account in April 2019.</p>
4. PCU and PIU financial management capacity established and financial systems operational.	(i) Financial management and procurement support consultants mobilized; project accounting and financial reporting systems established, including dedicated accounting software meeting government FM-EMP and ADB requirements, and a progress report template	EA, assisted by project consultants PCU and PIU, assisted by project consultants PCU, PIU and ADB	Within six months of project effectiveness	<p>(i) International and National Financial Management and Procurement Specialists and National Internal Auditor recruited and mobilized. They are supporting the PCU with the establishment of the project accounting and financial management systems, including dedicated accounting software.</p> <ul style="list-style-type: none"> - The Financial Management Manual (FMM) was finalized in December 2019 and approved/signed later in mid 2021. A Lao version of the Accounting Manual has been prepared (signed in January 2022), and shared with PCU and PIUs for their guidance. 	Ongoing

Planned Action	Output	Responsible Party	Due Date	Progress	Status of compliance
	linking financial with physical progress.				
	(ii) PCU and PIUs attend training on project accounting, including the use of accounting software and compliance with government FM-EMP.	EA and MEF ADB		SAO has recommended to PCU to also prepare other sub manuals including a Fixed Asset manual. However, it was noted and to be raised to SAO that these were included as appendices to the accounting manual.	
	(iii) Project disbursement arrangements and procedures established in accordance with government FM-EMP regulations and procedures; staff trained in their operation.			- The Project accounting software is operational but PCU and PIUs still continue to record transactions daily in an excel template. Then PIUs will submit to PCU for consolidation, who will upload the excel files in the accounting system. The accounting system will create account ledgers and generate financial reports.	
	(iv) Internal audit function established.			- PCU and PIUs record in the excel template for importing into the accounting software in daily basis. Then, at each month-end PCU will gather all the information from each PIU to do consolidation.	
	(v) Independent external auditor appointed.			- A progress report template was agreed that links financial with physical progress.	
	(vi) ADB Inception mission Aide-Mémoire confirms suitable financial management system.			(ii) PCU had participated in following workshops: <ul style="list-style-type: none"> o orientation on financial management of ADB-financed projects delivered by the International Financial Management and Procurement Specialist (IFMPS) on 28-29 March 2019. o a financial management training to discuss the preparation of withdrawal applications and key features of the FMM with PCU finance staff in August 2019. o Training on the FMM and accounting software, conducted from 28-30 June 2020. o ADB FM training in November 2021. o The new set of PCU finance team had participated in a one day training on preparation of WAs/SOEs, financial reporting and on procurement in January 2022. o PCU staff attended a FM workshop conducted by ADB Manila last October 2022. o One of the PCU Finance staff is attending an English course to improve fluency in the English language, 	

Planned Action	Output	Responsible Party	Due Date	Progress	Status of compliance
				<p>(iii) The project's disbursement arrangements have been established (following the example of L3156-LAO, with appropriate modifications).</p> <p>(iv) MICT has recruited and mobilized a National Internal Auditor, who will be responsible for supporting and advising the PCU and PIUs on adherence to the financial management requirements.</p> <p>(v) As per para. 64 of PAM, the State Audit Organization will audit the project financial statements. The combined AFS for December 2018 to December 2019 has been submitted to ADB in October 2020 and has been disclosed in the ADB website on 18 November 2020. The 2020 APFS was submitted to ADB on 29 September 2021, with delay due to covid lockdown and has been disclosed on 29 October 2021. The 2021 APFS was submitted to ADB in June 2022 and disclosed in the ADB website on 30 June 2022. The FY 2022 APFS will be submitted late as was advised by SAO to ADB LRM.</p> <p>(vi) ADB inception mission AM (para. 17–20).</p>	
5. PCU and PIU staff attend disbursement seminar as part of capacity building.	<ul style="list-style-type: none"> At least 1 staff member from the PCU and each PIU attend ADB's in-country disbursement seminar. 	PCU, PIU and ADB	Within one year of project effectiveness	Two PCU staff attended ADB's in-country disbursement seminar in June 2019. However, PIU staff were not invited to the seminar due to limited slots (allocated only 2 staff per project). But PCU staff with the assistance from the consultants has continued to conduct hands-on training to the PIU staff, during their regular visit to the project provinces.	Completed
6. Publicizing grievance redress mechanism.	<ul style="list-style-type: none"> Grievance redress mechanism to report suspected procurement related cases of corruption and collusion established and publicized on project website. Contact details of MOF and ADB's office on Anti-corruption periodically advertised in newspapers and on project website. 	EA	Within six months of project effectiveness	<p>Project effectiveness 25 December 2018.</p> <ul style="list-style-type: none"> Grievance redress mechanism to report suspected procurement related cases of corruption and collusion was established in February 2021 and has been publicized on the project website (https://www.tiigp2-laos.org/article-categories/procurement-grievance-redress-mechanism/) A link to ADB's Anticorruption and Integrity web page containing procedures and a form to report integrity violations is included in the grievance redress mechanism published on the project website. Contact details of MOF will be published on the project website 	Completed

ADB = Asian Development Bank; DICT = Department of Information, Culture and Tourism; EA = executing agency; MOF = Ministry of Finance; PCU = project coordination unit; PIU = project implementation unit.

Annex 6: Goods and works procurement monitoring table as of 30 June 2023

Grant 0599-LAO: Second GMS Tourism Infrastructure for Inclusive Growth Project (49387-002)																	
Status of Procurement - Goods																	
Procurement Plan Approved on: March 2023 (Version 7)																	
Package No.	Description	Mode	Adv Date	Estimate (\$ mil)	Number of Contracts	Bids		Bid		Bid Evaluation		Contract			Name and Consultants		
						Issuance	Closing	Approved	Amount	Signed	Received	PCSS No.	Amount	\$ Equip			
TIIGP2-LAO-G01a	PCU & PIU vehicles	NCB	Q1/2019	255,000	2												
TIIGP2-LAO-G01a	PCU & PIU vehicles (3 units)	NCB	13-Feb-19	155,000		27/Feb/19	22/Mar/19	11/Apr/19	LAK	1,136,220,000	25/Apr/19	10/May/19	G20440	LAK	1,136,220,000	130,633.78	ISUZU LAO SERVICES SOLE CO.,LTD
TIIGP2-LAO-G01b	PIU vehicles (2 units)	NCB	31-Aug-20	110,000		2/Sep/20	6/Oct/20	3/Nov/20	\$	92,880	4/Nov/20	3/May/21	G23062	\$	92,880	92,880.00	Toyota Champa Co. Ltd.
TIIGP2-LAO-G02	PCU office furniture and equipment	Shopping	Q4/2018	25,000	Various											37,452.42	
TIIGP2-LAO-G02	Office Furnitures for PCU										19/Feb/19		G20443	LAK	31,955,000	3,720.00	Panuvat Furniture
TIIGP2-LAO-G02-02	Office Equipment										14/Feb/19		G20860	LAK	17,200,000	1,994.20	Me shop
TIIGP2-LAO-G02-03	Office Renovate										18/Mar/19		G20861	\$	3,500	3,500.00	Thavisouk Construction Co., Ltd
TIIGP2-LAO-G02-05	Office Equipment										9/Apr/19		G20865	LAK	49,170,000	5,724.00	XP Computer Co., Ltd
TIIGP2-LAO-G02-06	Office Furniture										11/Apr/19		G20866	LAK	7,458,000	867.00	Panuvat Furniture
TIIGP2-LAO-G02-07	Office Equipment										11/Apr/19		G20867	LAK	33,000,000	3,836.00	Sing-Lao Engineering Co., Ltd
TIIGP2-LAO-G02-08	Office Equipment										28/Oct/20		G22643	LAK	5,197,500	560.08	LT Sole Co Ltd
TIIGP-LAO-002-09	Office Equipment										16/Mar/21		0003	LAK	170,907,000	17,251.14	Smile Com
TIIGP2-LAO-G03-VV01	PIU office furniture and equipment (4 PIUs)	Shopping	Q1/2019	90,000	Various											71,361.13	
TIIGP2-LAO-G03-VV01	Office Furniture for VV										25/Mar/19		G20868	LAK	45,782,000	5,300.00	Sangchieng Furniture
TIIGP2-LAO-G03-VV02	Office Equipment of VV										26/Mar/19		G20869	LAK	56,760,000	6,318.93	XP Computer
TIIGP2-LAO-G03-VV03	Office Equipment of VV										28/Mar/19		G20870	LAK	23,953,900	2,626.64	SOA Co., Ltd
TIIGP2-LAO-G03-VV04	Office Repair of VV										30/Mar/19		G20871	LAK	39,864,000	4,616.56	Thavisouk Construction Co., Ltd
TIIGP2-LAO-G03-LPB01	Office Renovate of LPB										14/Jun/19		G20876	LAK	67,947,000	7,858.78	Than Van Binh Binh
TIIGP2-LAO-G03-LPB02	Office Furniture & office Equipment (LPB)										27/Jun/19		G20877	LAK	97,746,000	11,290.98	Advice Shop LPB
TIIGP2-LAO-G03-CPS01	Office Equipment of CPS										24/Jun/19		G20878	LAK	63,294,000	7,046.34	Advice Pakse Pakse
TIIGP2-LAO-G03-VP01	Office Furniture for VP										26/Mar/19		G20879	LAK	43,211,300	4,997.84	Somphan Shop
TIIGP2-LAO-G03-VP02	Office Equipment of VP										26/Mar/19		G20881	LAK	60,099,600	6,881.88	Vilayvanh Shop
TIIGP2-LAO-G03-VP03	Office Repair of VP										20/Jun/19		G20883	LAK	62,421,348	9,423.80	Thavisouk Construction Co., Ltd
TIIGP2-LAO-G03-CPS02	Office furniture for Champasak PIU Office	Shopping									28/Aug/20		G22469	LAK	46,387,000	4,999.38	Silisomboun Shop
TIIGP2-LAO-G04	Vang Vieng landfill management equipment	NCB		1,300,000	2												
TIIGP2-LAO-G04-01	Pick-up truck for Vang Vieng UDAA for administrative and management purposes at Vang Vieng Landfill	Shopping		40,300							18/Nov/22		0043	USD	40,300	40,300.00	
TIIGP2-LAO-G04-01				650,000													
TIIGP2-LAO-G05	Equipment for ASEAN Standards certification bodies	Shopping	Q2/2019	45,000	Various											42,532.66	
TIIGP2-LAO-G05-01	Purchasing sets of computers for ASEAN standard implementation Units at the national level, Vientiane Province, and members of Lanexang Cultural Quadrangle networks from public and private sectors of Vientiane Capital and Sayabouli Province 2.4.2b										25/Sep/19		G21439	LAK	206,800,000	23,393.67	BPIT Sole.,Ltd
TIIGP2-LAO-G05-02	Provision of IT equipment and materials for ASEAN standard certification body of Luang Prabang Province 2.4.2.b										15/Oct/19		G21440	LAK	49,632,000	5,610.04	Advice Shop Luang Prabang
TIIGP2-LAO-G05-03	Procurement of IT Equipment for Tourism Destination		Q1/2020								11/Feb/20		G22218	LAK	12,952,500	1,418.73	LaoCom Computer Service Center
TIIGP2-LAO-G05-04	Procurement of computer for the secretariat of ASEAN Standard Implementation										10/Jul/20		G22220	LAK	58,740,000	6,434.00	BP IT Sole.,Ltd
TIIGP2-LAO-G05-05	Provision of IT equipment for ASEAN standard certification body										15/Aug/21		0013	LAK	75,141,000	5,676.23	Micro Info Import-Export Sole Co Ltd
TIIGP2-LAO-G05-06																	
TIIGP2-LAO-G05-07																	

Grant 0599-LAO: Second GMS Tourism Infrastructure for Inclusive Growth Project (49387-002)

Status of Procurement - Goods

Procurement Plan Approved on: March 2023 (Version 7)

Package No.	Description	Mode	Adv	Estimate	Number of	Bids	Bid	Bid Evaluation		Contract			Name and Consultants		
			Date	(\$ mil)	Contracts	Issuance	Closing	Approved	Amount	Signed	Received	PCSS No.		Amount	\$ Equiv
TIIGP2-LAO-G08	Equipment for Heritage Interpretation	Shopping		180,000	Various									19,265.53	
TIIGP2-LAO-G08-VC01	Procurement of Signs of Direction and Information Tourism Destination	Shopping								2/Mar/20		G22249	LAK 33,440,000	3,662.80	F Design Individual
TIIGP2-LAO-G08-LPB02	Procurement of Tourism Promotion Signs for the Tourism Information Room of Xiengman Village	Shopping								29/May/20		G22188	LAK 41,173,000	4,514.61	Luanprabang Tiary Advertising
TIIGP2-LAO-G08-LPB03	Procurement of Tourism Promotion Signs and Amenities for the Tourism Information Room of Chan Neua, Xang Hai and Pak Ou Village	Shopping								2/Jul/20		G22187	LAK 101,123,000	11,088.12	Luanprabang Tiary Advertising
TIIGP2-LAO-G08-04	Directional sign design, production, and installation along the National Highway, access to priority tourism locations, and roads connecting to provincial target areas and neighboring countries									18/Oct/22		0041	USD 20,000	20,000.00	F-Design Individual
TIIGP2-LAO-G09	Equipment for SMEs to Implement Private Sector-Led Actions in the DMPs	Shopping		325,000	Various									25,946.94	
TIIGP2-LAO-G09-01	Equipment for printing tour guide badges		Q1/2020							3-Mar-20		G21584	LAK 70,400,000	7,790.79	Smart Technology Co., Ltd
TIIGP2-LAO-G09-LPB02	Improvement to the Night Market of Luang Prabang	Shopping								29-May-20		G22184	LAK 101,728,000	11,154.46	Sisana Construction Co; Ltd
TIIGP2-LAO-G09-LPB04	Seedling and Amenities for the Landscaping of Pottery Demonstration Center	Shopping								10-Jun-20		G22186	LAK 63,855,000	7,001.69	Noumnim Shop
TIIGP2-LAO-G10	Accounting Software									25/Feb/20		G21571	USD 22,990	22,990.00	LAOSINGAPOR INFORMATION TECHNOLOGY AND COMMUNICATION PROMOTION CO.,LTD
TIIGP2-LAO-G11	Laptop computers for data collection for 18 provincial statistical units	Shopping		18,000						6/Jun/22		0042	USD 18,000	18,000.00	NSV Computer

Grant 0599-LAO: Second GMS Tourism Infrastructure for Inclusive Growth Project (49387-002)
Procurement Monitoring Sheet - Civil Works

Procurement Plan Approved on: March 2023 (Version 7)

Package No.	Description	Mode	Resp Proj Mgt Unit	CA Target Date	Adv Date	Estimate (\$)	Draft Bid Docs		Bids		Bid Evaluation		Contract					
							Received	Approved	Issuance	Closing	Approved	Amount	Signed	Received	PCSS No.	Amount	\$ Equiv	
TIIGP2-LAO-W01	Nakasang and Don Det-Don Khone Access Improvements	ICB		01-Dec-19	18-Sep-19	5,930,000	13-Sep-19	18-Sep-19	18-Sep-19	30-Oct-19	23-Dec-19	\$ 3,964,308	30-Dec-19	30-Dec-19	G21291	\$ 3,964,308	3,964,308	
TIIGP2-LAO-W02	Nam Ngum Reservoir Access Improvements	ICB		Q3/2020	18-Sep-20	8,000,000	05-Sep-20	16 Sep 20	18/Sep/20	30/Oct/20	20/Apr/21	\$ 4,669,065	26/Apr/21	11/May/21	G23079	\$ 4,669,065	4,669,065	
TIIGP2-LAO-W03	Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements	ICB		Q4/2020	01-Oct-20	13,000,000	25-Sep-20	29-Sep-20	01/Oct/20	12/Nov/20	15/Jul/21	\$ 8,829,708	23/Jul/21	08/Aug/21	0001	\$ 8,829,631	8,829,631	
TIIGP2-LAO-W03a	Vang Vieng Urban Renewal	NCB		Q4/2020		2,000,000												
TIIGP2-LAO-W04	Vang Vieng Landfill Improvements	ICB		Q3/2020	15-Sep-20	4,200,000	10-Sep-20	11-Sep-20	15/Sep/20	27/Oct/20	28/Dec/20	\$ 3,156,160	19/Feb/21	25/Feb/21	G22778	\$ 3,156,160	3,156,160	
TIIGP2-LAO-W05	Small works for ASEAN Tourism Standards certification bodies	Shopping		Q4/2020		5,000												
TIIGP2-LAO-W06	Small works for AESAN Tourism Standards implementation (public sector)	Shopping		Q4/2020		350,000												
TIIGP2-LAO-W06-VV03	Renovation of Lom Cave Toilets, Vang Vieng District	Shopping											4-Sep-20		G22466	265,224,000	28,584.64	
TIIGP2-LAO-W06-CPS04	Renovation of Wat Phou Toilets	Shopping											7-Sep-20		G22462	265,187,000	28,573.78	
TIIGP2-LAO-W06-PCU06	Renovation of ASEAN Public Toilets at Lao-Thai International Customs Post on the Road to Luangprabang Heritage Town	Shopping											23-Mar-20		G22461	281,609,202	30,343.25	
TIIGP2-LAO-W06-LPB07	Renovation of Public Toilets at Mekong River Recreational Area, Phonheuang Village, Luangprabang Capital	Shopping											3-Oct-20		G22453	330,941,516	35,678.79	
TIIGP2-LAO-W06-VV07	Procurement of Vang Vieng Urban Landscape Improvements	Shopping											20-Oct-20		G22652	66,330,000	7,140.39	
TIIGP2-LAO-W06-VP05	Renovation of Toilets of Nuanta Fuel Station, Sensoum Village, Phonhong District, Vientiane Province	Shopping											2-Sep-20		G22808	195,381,780	20,899.64	
TIIGP2-LAO-W06-CPS05	Renovation of Public Toilets at Tadfar Waterfall, Parksong District, Champasak Province	Shopping												24/Sep/21		0009	200,645,830	17,950.16
TIIGP2-LAO-W06-VP06	Renovation of Public Toilets at Thongsamsee Temple, Tholakhom District, Vientiane Province	Shopping												28/Sep/21		0010	269,735,900	24,131.09
TIIGP2-LAO-W06-VP07	Renovation of Public Toilets at Savang Village (Kang Temple), Vangvieng District, Vientiane Province	Shopping												29/Sep/21		0011	303,888,750	27,186.47
TIIGP2-LAO-W06-10	Renovation of public toilets at Vat Mai in Luang Prabang Province	Shopping												20/Dec/21		0026	LAK 322,861,000	21,462.54
TIIGP2-LAO-W06-11	Improvement of tourist facilities for ASEAN clean tourist city standard and public toilet standard in the project's target sites in Luang Prabang	Shopping												08/Aug/22		0037	USD 76,965	76,965.00
TIIGP2-LAO-W06-12	Improvement of Public Toilets to meet ASEAN standard at the tourist site of Pu Kham Cave, Vangvieng District, Vientiane Province	Shopping												26/Jul/22		0038	USD 33,958	33,958.00
TIIGP2-LAO-W06-13	Improvement to meet ASEAN standards for (i) Homestay at Lingsan Village, (ii) Community Based Tourism at Phon Village, and (iii) Public Toilets at the park near to Nam Gnum Dam at Sengsavang Village, Keoudom District, Vientiane Province	Shopping												05/Aug/22		0039	USD 41,877	41,877.00
TIIGP2-LAO-W06-14	Improvement to meet the ASEAN Standards for (i) Public Toilets in Phousalao Temple, Phothong District, (ii) Community Based Tourism in Nongluang Village, Pakxong District, and (iii) Homestay at Don Deng Village, Pathoumphone District and Don Kho, Sanasomboun District, Champasak Province	Shopping												30/Sep/22		0040	USD 44,000	44,000.00

Annex 7: Consultant recruitment monitoring table as of 30 June 2023

Package No.	Description	Mode	Adv Date	No. of Contracts	Estimate (\$ million)	Submission 1		RFP	RFP	Submission 2		Submission 3		Submission 4		Submission 5					
						Received	Approved	Issuance	Closing Date	Received	Approved	Received	Approved	Received	Approved	Signed	Received	PCSS No.	Amount	\$ Equiv	
TIIGP2-LAO-C01	Project Management and Civil Engineering Support	QCBS	28/08/2018	1	3,109,134.00	23-Oct-18	07-Nov-18	08-Nov-18	17-Jan-19	12-Feb-19	03-Apr-19	22-Apr-19	03-May-19		20-Jun-19	01-Jul-19	19-Jul-19	G20711	\$	2,602,460	2,602,460
																		G20712	EUR	805,926	870,000
TIIGP2-LAO-C02	International Tourism Specialist/Co-Team Leader	ICS	15/11/2018	1	862,223.00	31-Jan-19	14-Feb-19			21-Feb-19	05-Mar-19					19-Feb-19	21-Feb-19	G20083	\$	930,000	930,000
TIIGP2-LAO-C03	International Tourism Standards Specialist	ICS	06/06/2019	1	100,876.00	24-Jul-19	13-Aug-19			21-Aug-19	22-Aug-19					19-Aug-19	21-Aug-19	G20821	\$	121,000	121,000
TIIGP2-LAO-C04	National Tourism Specialist/Deputy Team Leader	ICS	15/11/2018	1	239,663.00	31-Jan-19	14-Feb-19			21-Feb-19	05-Mar-19					19-Feb-19	21-Feb-19	G20084	\$	242,000	242,000
TIIGP2-LAO-C05	International Gender Specialist	ICS	06/06/2019	1	34,500.00	24-Jul-19	13-Aug-19			21-Aug-19	22-Aug-19					19-Aug-19	21-Aug-19	G20823	\$	34,500	34,500
TIIGP2-LAO-C06	National Gender Specialist	ICS	06/06/2019	1	49,500.00	24-Jul-19	13-Aug-19			21-Aug-19	22-Aug-19					19-Aug-19	21-Aug-19	G20822	\$	49,500	49,500
TIIGP2-LAO-C07	International Financial Management & Procurement Specialist	ICS	15/11/2018	1	71,369.00	31-Jan-19	14-Feb-19			21-Feb-19	05-Mar-19					20-Feb-19	21-Feb-19	G20085	\$	75,000	75,000
TIIGP2-LAO-C08	National Financial Management & Procurement Specialist	ICS	15/11/2018	1	23,510.00	31-Jan-19	14-Feb-19			21-Feb-19	05-Mar-19					19-Feb-19	21-Feb-19	G20086	\$	25,000	25,000
TIIGP2-LAO-C09	International Monitoring and Evaluation Specialist	ICS	06/06/2019	1	45,500.00	24-Jul-19	28-Aug-19			30-Aug-19	25-Sep-19					29-Aug-19	30-Aug-19	G20994	\$	45,500	45,500
TIIGP2-LAO-C10	National Monitoring and Evaluation Specialist	ICS	06/06/2019	1	53,500.00	10-Oct-19	22-Oct-19			20-Nov-19	03-Dec-19					13-Nov-19	20-Nov-19	G21187		53,500	53,500
TIIGP2-LAO-C11	National Internal Auditor	ICS	15/11/2018	1	103,394.00	31-Jan-19	14-Feb-19			21-Feb-19	05-Mar-19					18-Feb-19	21-Feb-19	G20087	\$	102,904	102,904
TIIGP2-LAO-C12	Tourism Experts-Various Resource Persons	SSS	Q2/2019	40	200,000.00																
	TIIGP2-LAO-C12-001	SSS		1												23-May-19	26-Sep-19		\$	3,150	3,150
	TIIGP2-LAO-C12-002	SSS		1												23-Jul-19	26-Sep-19		\$	2,500	2,500
	TIIGP2-LAO-C12-003	SSS		1												30-Jul-19	26-Sep-19		\$	3,150	3,150
	TIIGP2-LAO-C12-004	SSS		1												17-Sep-19	26-Sep-19		\$	2,100	2,100
	TIIGP2-LAO-C12-005	SSS		1												22-Oct-19	04-Nov-19		\$	2,400	2,400
	TIIGP2-LAO-C12-006	SSS		1												09-Jan-23		0051		3,000	3,000
	TIIGP2-LAO-C12-007			1														0052			
TIIGP2-LAO-C13	International Urban Planning and Design Specialist	ICS	Q4 2019	1	93,290.00	29-Oct-19	06-Nov-19			25-Nov-19	03-Dec-19					08-Nov-19	25-Nov-19	G21188	\$	93,258	93,258
TIIGP2-LAO-C14	National Destination Management Specialist	ICS	04-Nov-19	1	57,829.00	12-Apr-19	24-Apr-19			24-Apr-19	23-May-19					24-Apr-19	26-Apr-19	G20442	\$	57,829	57,829
TIIGP2-LAO-C15	International Tourism Management and Development Specialist	ICS	Q4 2019	1	73,880.00	29-Oct-19	06-Nov-19			15-Nov-19	03-Dec-19					21-Nov-19	25-Nov-19	G21189	\$	73,600	73,600
TIIGP2-LAO-C16	International Natural and Cultural Heritage Specialist	ICS	Q4 2019	1	22,311.00	29-Oct-19	06-Nov-19			25-Nov-19	03-Dec-19					21-Nov-19	25-Nov-19	G21190	\$	22,252	22,252
TIIGP2-LAO-C17	National Tourism Destination Development and Management Specialist	ICS	Q3 2020	1	128,057.00	28-Aug-20	03-Sep-20			28-Aug-20	03-Sep-20					10-Sep-20	08-Oct-20	G22209	\$	128,000	128,000
TIIGP2-LAO-C18	International Social Safeguards Specialist	ICS	Q4 2020	1	70,000.00	30-Nov-20	03-Dec-20			07-Dec-20	23-Dec-20					07-Dec-20	07-Dec-20	G22604	\$	75,000	75,000
TIIGP2-LAO-C8a	National Financial Management and Procurement Specialist	ICS	23/Feb/21	1	12,494.00	12-Mar-21	25-Mar-21			23-Apr-21						23-Apr-21	23-Apr-21	G23034	\$	12,494	12,494
TIIGP2-LAO-C19	National Social Safeguards Specialist 1	ICS	28/May/21	1	47,000.00	08-Jun-21	10-Jun-21			20-Jun-21	22-Jun-21					16-Jun-21	20-Jun-21	G23267	\$	52,000	52,000
TIIGP2-LAO-C20	National Social Safeguards Specialist 2	ICS	28/May/21	1	25,000.00	08-Jun-21	10-Jun-21			20-Jun-21	22-Jun-21					16-Jun-21	20-Jun-21	G23268	\$	22,080	22,080
TIIGP2-LAO-C21	National External Monitor (Social Safeguards)	ICS	13/Jul/22	1	39,000.00	09-Aug-22	23-Aug-22			09-Sep-22	23-Aug-22					29-Aug-22	09-Sep-22	0029	\$	42,000	42,000

Annex 8: Utilization of consulting services as of 30 June 2023

Package/Positions	Expert name	Person-Months (pm) as per PAM	Contract signing date	Original contract (total pm)	Current contract incl. variations (total pm)	Current contract closing date	Cumulative person-months utilized as of 30-Jun-23	Balance (pm)	Notes
TIIGP2-LAO-C01: Project Management and Civil Engineering Support (Firm)									
<i>International</i>									
1 International Civil Engineer - Co-Team Leader	Mr. Mrityunjoy Ghosh	54	05/Aug/19	41	54	31/Dec/24	47.00	7.00	
2 International Environmental Specialist	Mr. Peter Gammelgaard Jensen	6	12/Aug/19	6	13	31/Dec/24	9.83	3.17	Replacement
3 International Social Safeguards Specialist (Resettlement & Indigenous People)	Mr. Nils Gardek	6	05/Aug/19	6	6	31/Dec/24	5.74	0.26	<i>Position discontinued</i>
4 International Institutional Development Specialist	Mr. Steven Long	4	05/Aug/19	4	7	31/Dec/24	5.84	1.16	Replacement
Subtotal		70		57	80		68.41	11.59	
<i>National</i>									
1 National Lead Civil Engineer	Mr. Phomma CHANTHIRATH	54	07/Sep/19	41	59	31/Dec/24	44.57	14.43	Replacement
2 National Environmental Specialist	Ms. Phaylin BOUNMANYVONE	12	05/Aug/19	12	25	31/Dec/24	22.71	2.29	Replacement
3 National Social Safeguards Specialist (Resettlement & Indigenous People)	Mr. Misa PHOUTHILATH	12	05/Aug/19	12	12	31/Dec/24	12.00	0.00	<i>Position discontinued</i>
4 National Institutional Development Specialist	Mrs. Baythone Lovanxay	12	22/Jun/20	12	12	31/Dec/24	5.47	6.53	Replacement
5 Resident Engineer 1 (W01 C1 Nakasang + C2 Don Det-Don Khone)	Mr. Vongdeth Frichithavong		22/Jun/20	24	31.5	31/Dec/24	32.63	-1.13	Replacement
6 Resident Engineer 2 (W02 Nam Ngum)	Mr. Xayavath Chanthavongsa		11/Sep/19	24	54	31/Dec/24	42.67	11.33	Replacement
7 Resident Engineer 3 (W04 VV Landfill + W03 Vang Vieng)	Mr. Lueyang SISOMBONG		15/Jun/21	22	39	31/Dec/24	24.50	14.50	Replacement
8 Construction Supervisor 1 (W03 - V3 Western Loop)	Mr. Vilath KHAMVONGSA			24	29	31/Dec/24	19.82	9.18	Replacement
9 Construction Supervisor 2 (W04 Landfill)	Mr. Anikone THAMMAVONG		01/Jun/21	24	30	31/Dec/24	24.85	5.15	Replacement
10 Construction Supervisor 3 (W03 Kang Yui)	Mr. Bounxom VONGSOUTCHAY		13/Sep/21	20	30	31/Dec/24	21.00	9.00	Replacement
11 Construction Supervisor 4 (W01-C2 Don Det-Don Khone)	Mr. Phoumano Khodpanya		15-Jun-20	20	20	31/Dec/24	18.03	1.97	Replacement
Subtotal		90		235	341.5		268.25	73.25	

Package/Positions	Expert name	Person-Months (pm) as per PAM	Contract signing date	Original contract (total pm)	Current contract incl. variations (total pm)	Current contract closing date	Cumulative person-months utilized as of 30-Jun-23	Balance (pm)	Notes
Summary									
<i>Total International</i>		70		57	80		68.41	11.59	
<i>Total National</i>		90		235	341.5		268.25	73.25	
Grand Total TIIGP2-LAO-C01: PMCES Consultant		160		292	421.5		336.66	84.84	
Capacity Building Support (Individuals)									
International									
1	TIIGP2-LAO-C02: International Tourism Specialist - Co-Team Leader	Mr Henricus Braunius PONNE	54	19/Feb/19	54	54	31/Dec/24	40.88	13.12
2	TIIG2P-LAO-C03: International Tourism Standards Specialist	Mr Ross Alexander Corbett	8	19/Aug/19	7	15	31/Dec/24	8.82	6.18
3	TIIGP2-LAO-C05: International Gender Specialist	Ms Luz Lopez Rodriguez	2	19/Aug/19	2	5.5	31/Dec/24	5.49	0.01 <i>Closed</i>
4	TIIGP2-LAO-C07: International Financial Management & Procurement Specialist	Ms Nida Azada CALMA	5	19/Feb/19	5	17.5	31/Dec/24	15.07	2.43
5	TIIGP2-LAO-C09: International Monitoring and Evaluation Specialist	Ms. Irene Villapando (through Ramboll)	3	28/Aug/19	2.5	2.5	31/Dec/24	1.98	0.52 Replacement for Mr Nils Gardek
6	TIIGP2-LAO-C13: International Urban Planning and Design Specialist	Mr Craig Czarny	-	8/Nov/19	lump-sum	lump-sum	30/Jun/24	lump-sum	-
7	TIIGP2-LAO-C15: International Tourism Management and Development Specialist	Mr Paul Rogers	-	21/Nov/19	lump-sum	lump-sum	31/Dec/22	lump-sum	- <i>Closed</i>
8	TIIGP2-LAO-C16: International Natural and Cultural Heritage Specialist	Ms Ester van Steekelenburg	-	8/Nov/19	lump-sum	lump-sum	31/Dec/22	lump-sum	- <i>Closed</i>
9	TIIGP2-LAO-C18: International Social Safeguards Specialist	Mr Paul van Strijp	-	7/Dec/20	4	19	31/Dec/24	19.55	-0.55 <i>New position (moved from PMCES) - to be closed</i>
Subtotal		72		74.5	113.5		91.79	21.71	
National									
1	TIIGP2-LAO-C04: National Tourism Specialist - Deputy Team Leader	Ms Phongisth DAVADING	54	19/Feb/19	54	54	31/Dec/24	45.27	8.73
2	TIIGP2-LAO-C06: National Gender Specialist	Ms Sipaseuth Chanthapanya	12	19/Feb/19	12	15	31/Dec/24	15.00	0.00 <i>Closed</i>
3	TIIGP2-LAO-C08: National Financial Management & Procurement Specialist	Mr Kim XAISANA	6	19/Feb/19	6	6	31/Dec/20	5.94	0.06 <i>Closed</i>
4	TIIGP2-LAO-C08a: National Financial Management & Procurement Specialist	Mr Somphone Siriphanh	-	19/Apr/21	3	9	31/Dec/24	6.09	2.91 Replacement for TIIGP2-LAO-C08

Package/Positions	Expert name	Person-Months (pm) as per PAM	Contract signing date	Original contract (total pm)	Current contract incl. variations (total pm)	Current contract closing date	Cumulative person-months utilized as of 30-Jun-23	Balance (pm)	Notes
5 TIIGP2-LAO-C10: National Monitoring and Evaluation Specialist	Dr Vivath Sauvaly	12	13/Nov/19	11	28	31/Dec/24	24.48	3.52	
6 TIIGP2-LAO-C11: National Internal Auditor	Mr Lomphet PHONGSVANH	-	18/Feb/19	30	33	31/Dec/24	26.00	7.00	
7 TIIGP2-LAO-C12: Tourism experts - various resource persons	Various								22 contracts included in procurement plan.
8 TIIGP2-LAO-C14: National Destination Management Specialist	Mr Vila Chanthavong	-	24/Apr/19	<i>lump-sum</i>	<i>lump-sum</i>	31/Dec/19	<i>lump-sum</i>		<i>Completed - to be closed</i>
9 TIIGP2-LAO-C17: National Tourism Destination Development and Management Specialist	Mr Vila Chanthavong	-	10/Sep/20	32	47.5	31/Dec/24	31.70	15.80	New position
10 TIIGP2-LAO-C19: National Social Safeguards Specialist 1	Mr Misa Phouthilath	-	16/Jun/21	10	31	31/Dec/24	23.61	7.39	New position (moved from PMCES)
11 TIIGP2-LAO-C20: National Social Safeguards Specialist 2	Mr. Khonevilay SAYYAVONG	-	14/Jun/21	5	7	31/Dec/22	7.00	0.00	<i>Completed - to be closed</i>
Subtotal		84		163	230.5		185.09	45.41	
Summary CBS Individual Consultants									
<i>Total International</i>		<i>72</i>		<i>74.5</i>	<i>113.5</i>		<i>91.79</i>	<i>21.71</i>	
<i>Total National</i>		<i>84</i>		<i>163</i>	<i>230.5</i>		<i>185.09</i>	<i>45.41</i>	
Total CBS Individual Consultants		156		237.5	344		276.88	67.12	
Project Summary									
Total International		142		131.5	193.5		160.20	33.30	
Total National		174		398	572		453.34	118.66	
Project Grand Total		316		529.5	765.5		613.54	151.96	

Annex 9: GAP implementation progress as of 30 June 2023

Project Title:	Grant 0599-LAO: Second Greater Mekong Subregion Tourism Infrastructure for Inclusive Growth Project
Country:	Lao PDR
Project No.:	49387-002
Type of Project (Loan/Grant/TA):	Grant
Approval date:	31 August 2018
Project Implementation Duration:	25 December 2018 – 30 June 2025
Gender Category:	Effective Gender Mainstreaming (EGM)
Project Impact:	Sustainable, inclusive, and more balanced tourism development achieved
Project Outcome:	Tourism competitiveness of secondary towns increased

Status of GAP implementation:

	Achieved	On track	Not yet achieved
9 Activities	7 (1, 2, 5, 6, 7, 8, 9) = 67 %	2 (3, 4) = 22.3%	0
25 Targets	14 (2, 3, 5, 8, 10, 13, 15, 16, 17, 18, 19, 20, 21, 23) = 56 %	10 (1,4,6,7,9,11,12,14,22,24,25) = 40%	1 (24) = 4%

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
Outcome		
Target 1: Women account for at least 55% of tourism workers in project areas (2016 baseline: Lao PDR 50%) (DMF outcome indicator d)	<p>On-track</p> <p>As of 2021, 7,578 (54.3%) out of 13,945) tourism workers in three Project's target areas.⁶ were women</p> <ul style="list-style-type: none"> - Champasak Province: 1,838 (55.9%) out of 3,288 were women - Luang Prabang Province: 3,742 (52.1%) out of 7,183 were women - Vientiane Province: 1,998 (57.5%) out of 3,474 were women. <p>This indicator is measured at mid-term (2022) and at end-of-project (2024). A tourism worker is defined as a person employed in tourism and hospitality industry, including hotels, resorts, guesthouses, restaurants, tourist attractions,</p>	The latest available secondary data source was available for 2021 data, in time for the project's mid-term. However, it is unknown at this stage if a similar source will be available again at end-of-project. If not, the project may need to commission a survey to determine end-of-project data for this indicator.

⁴ GAP Activities, Indicators and Targets, Timeframe and Responsibility

⁵ Please include reasons why an activity was not fully implemented, or if targets fall short, or reasons for delay, etc., and provide recommendations on ways to address issues and challenges.

⁶ Ministry of Education and Sports/Skills for Tourism Project (LAO/029). 2021. *Tourism and Hospitality Enterprise Survey of Employment and Skills in Lao PDR, 2021: Research Findings and Employment Projections, 2021-2026*. Vientiane,)

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>entertainment venues, tour companies, travel agents, or as a tour guide or at a tourism-related handicraft business. The project target areas are defined as the provinces of Champasak, Luang Prabang and Vientiane Province.</p> <p>It has been agreed that the PIU Gender Focal Persons will collect annual sex- aggregated data on tourism workers from all stakeholders concerned and submit to the M & E and National Gender Specialist annually.</p> <p>The way forward: To increase the number of female tourism workers in the target provinces, the following are proposed: (a) the project should target at least 60 % women participation in the training for tourism business to be conducted in quarters 2-3 of 2022 and (b) encourage tourism businesses to hire more women based on labor market information that demand more women tourism workers. (c) It has been agreed that the PIU Gender Focal Persons will collect annual sex- aggregated data on tourism workers from all stakeholders concerned and submit to the M & E and National Gender Specialist annually</p>	
Output 1: Urban-rural access infrastructure and urban environmental services improved.		
Objective 1: Strengthen women’s voice in project design.		
<p>Target 2: Two consultations held during detailed design of each infrastructure subproject to optimize inclusiveness, gender responsiveness, and employment opportunities during and after construction.</p>	<p>Achieved The project conducted at least two consultations during detailed design of each infrastructure subproject to optimize inclusiveness, gender responsiveness, and employment opportunities during and after construction.</p> <p>The project has five Works packages/sub-projects, as follows:</p> <p>(i). Works Package: TIIGP2-LAO-W01: Nakasang and Don Det-Don Khone Access Improvements Sub-project C1: Nakasang Access Road and Port Rehabilitation Sub-project C2: Don Det-Don Khone Access Improvements</p> <p>(ii) Works Package: TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements Sub-project V1: Nam Ngum Reservoir Access Improvements</p> <p>(iii). Works Package: TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements</p>	<p>It was recommended during the mid-term review that feedback on gender inclusiveness and responsiveness must be included in the agenda of infrastructure subproject hand-over meetings.</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>Sub-project V2: Kaeng Yui Waterfall Access Improvement Sub-project V3: Western Loop Rural Access Road and Bridge Improvement</p> <p>(iv) Works Package: TIIGP2-LAO-W03a: Vang Vieng Urban Renewal Sub-project V4: Vang Vieng Urban Renewal</p> <p>(v) Works Package: TIIGP2-LAO-W04: Vang Vieng Landfill Improvements Sub-project V5: Vangvieng Solid Waste Management Improvements</p> <p>Details of consultation listed below:</p> <p>(i) Package TIIGP2-LAO-W01 (subprojects C1-C2): The detailed design for this subproject was undertaken during project preparatory technical assistance (PPTA). Two consultation were conducted with 12 (24.48%) out of 49 were women</p> <ul style="list-style-type: none"> • 1st consultation was on 20-21 June 2018, with 5 (41.67%) out of total 12 participants were women. • 2nd consultation was on 17-18 Oct 2018 with 7 (19%) out of 37 participants were women <p>(ii) Package TIIGP2-LAO-W02 (subproject V1): Three consultations Conducted with 17 (43.58%) out of 39 were women.</p> <ul style="list-style-type: none"> • 1st consultation: The Gender Specialists (IGS and SGS) met with the project team and village representatives (total 12; 8 women) on 19 October 2019, on the GAP target of women's representation in consultations and for them to equally benefit from the improvements in infrastructure. • 2nd consultation: Pre-construction, pre-hiring meeting and gender orientation held by the gender specialists on 19 August 2021 with 9 (%) out of 21 participants were women from the construction firm and the village men and women in attendance). • 3rd. consultation: the gender team consulted with women management level in Namngum construction site on 20 May 2022. Total 6 participants, all were women (100%). The main result of consultation (i) women suggested that the project support on market information for selling fish (ii) Women need support on establishing women group for fish processing (iii) Most of 	

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>women from Sengsavang village and Sokpakeo village work on services in restaurant in Namgnum Tourism area, women requested project to support on training of restaurant services.</p> <p>(iii) Package TIIGP2-LAO-W03 (subproject V2): Two consultations conducted with 20 (51.28%) out of 39 were women.</p> <ul style="list-style-type: none"> • 1st consultation: The IGS and SGS met with 18 village residents in xx on 20 October 2019 with 11 (61%) out of 18 participants were women. Women help as collectors of visitors' fees at the entrance of the fall, sell food at the stalls and are part of the 8 groups working on community-based tourism. • 2nd consultation: during pre-construction and labor mobilization on 19 August 2021. The I/NGS met with (9 (43%) out of 21 were women from representatives of Na Douang Village and the contractors. The participants were oriented on the GAP requirement including ensuring of 50 % representation of women and on hiring local unskilled workers, 10% of who are women; and the gender and safety provisions in the work site for women workers. <p>(iv) Package TIIGP2-LAO-W03/3a (subprojects V3 and V4): Three consultations conducted with 26 (42.62%) out of 61 were women</p> <ul style="list-style-type: none"> • 1st consultation: planning and design process consultation workshops held in the VangVieng PIU office on 16 August 2019 with 2(18%) out of 17 participants were women; • 2nd consultation: a follow up workshop on tackled the draft conceptual design report held on 17 September 2019 with 5(20%) out of 25 participants were women • 3rd. consultation: the gender team consulted with women group from Phonvieng village, Kanmak village, Vangmieng village and Naduang village on 20 May 2022. All 19 (100%) participants were women. The women concerns were (i) Women suggested that if job available in the project area, the project should inform them and (ii) suggested project to provide training for waste workers on hygiene and sanitation. Women in 	

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>Naduang village mentioned that they are waiting for completed construction then they will have more income generating activities.</p> <p>(v). Package TIIGP2-LAO-W04 (subproject V5): Three consultations conducted, 38 (52%) out of 73 were women</p> <ul style="list-style-type: none"> • 1st consultation: Public consultations were held in Vang Vieng on 19 June 2018. followed by on site consultations at the landfill location with 4 (33%) out of 12 participations were women from provincial and district office of xxx • 2nd consultation: On-site consultations in Ban Phon Vieng where employment opportunities were discussed with local stakeholders at the improved landfill were held on 13 October 2018, 21(55%) out of 38 participants were women) • 3rd consultation: Preconstruction and pre- labor mobilization were conducted on 20 Aug 2021, 13 (57%) out of 23 participants were omen. The participants from PIU, contractors & stakeholders., At the, meeting, the site engineering represented the gender requirement in construction works such as mobilize and priority local women unskilled labor to work for construction works (at least 10% of unskilled workers hired for construction works are local women). 	Please add information in blank
<p>Target 3: At least 50% of people consulted are women. (DMF output indicator 1f)</p>	<p>Achieved Project conduced total 13 consultation meeting with 119 (46 %) out of 261 people consulted are women. Details as mentioned in target 2 above. Check: 12+19+20+26+38= 113 49+39+39+61+73 = 261</p> <p>113/261 = 43.29% Please recheck (Not achieved)</p>	<p>Comment: Data in target 2 and 3 will be double checked to ensure consistency</p> <p>For further consultations, the project has to ensure at least 65 % of participants are women.</p>
<p>Objective 2. Promote women’s economic employment and safety.</p>		

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>Target 4: At least 300⁷ entrepreneurs (60% women) receive SME support services (2017 baseline:0)</p> <p>(DMF output indicator 3d)</p>	<p>On-track</p> <p>As of June 2023, the project conducted training on SME services and other SME related activities, 1,152 (48.2%) out of 2,390 participants are women. The project will continue to provide SME support services</p>	<p>Comments: Data and information below will be provided in future q-reports:</p> <ul style="list-style-type: none"> (i) Provide number of SME entrepreneurs to be supported by the project (ii) identify the needs for men and women (iii) How the project will address the needs (iv) Update the number of men and women receive SME support services <p>The Gender Specialists will continue coordinating with the project consultants to clarify information on:</p> <ol style="list-style-type: none"> 1. Number and list of training on SME support services conducted 2. Sex-disaggregated number of entrepreneurs who participated in those trainings (add column of entrepreneurs in registration form) and ensure at least 300 entrepreneurs participate in the training (not all entrepreneurs participate every training but all of them at least participate in one SME support services training) 3. The list of targeted SMEs to be supported by the project.

⁷ The previous figure listed is 500 based on the total count of target entrepreneurs *in Cambodia and Laos. This is now disaggregated to 300 for Lao PDR (PAM, annex G page 117 para 22)

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>Target 5: At least 10% of unskilled workers hired for construction works are local women (2017 baseline: ~10%).</p>	<p>Achieved As of June 2023, the total unskilled workers hired for across all 6 sub-projects is 100 of whom 24 are local women (24%)</p> <p>The project's GAP is included in bidding documents and contracts for packages TIIGP2-LAO-W01, TIIGP2-LAO-W02, and TIIGP2-LAO-W03 and TIIGP2-LAO-W04.</p> <p>As of June 2023:</p> <ul style="list-style-type: none"> • TIIGP2-LAO-W01: <ul style="list-style-type: none"> ○ In sub-project C1: Nakasang Access Road and Port Rehabilitation, there are 2 local women (18 %) out of 11 total number of unskilled workers. (Achieved) ○ In sub-project C2: Don Det -Don Khone Access Improvements, there are 2 local women (7%) hired out of the total 28 unskilled workers. (Not achieved). • TIIGP2-LAO-W02: <ul style="list-style-type: none"> ○ In sub-project V1: Nam Ngum Reservoir Access Improvements. there are 5 local women (36%) out of 14 total number of unskilled workers. (Achieved) • TIIGP2-LAO-W03: <ul style="list-style-type: none"> ○ In sub-projects V2: Kaeng Yui Waterfall Access Improvement and V3: Western Loop Rural Access Road and Bridge Improvement, there are 5 local women (23%) hired out of the total 22 unskilled workers. (Achieved). • TIIGP2-LAO-W03a: <ul style="list-style-type: none"> ○ In sub-project V4: Vang Vieng Urban Renewal. Not hiring yet. • TIIGP2-LAO-W04: • In sub-project V5: Vang Vieng Solid Waste Management Improvement there are 10 local women (40%) hired out of the total 25 unskilled workers. (achieved) 	<p>The Gender Specialist will continue coordinating with PIU and contractors to collect data unskilled workers for the subproject TIIGP2-LAO-W03a once the construction commences and to monitor the hiring of more local women among unskilled workers in the follow-up phases of construction.</p>
<p>Activity 1: Contractors ensure separate access to water and sanitation facilities for women and men in construction sites and separate quarters, as well</p>	<p>Achieved Total 4 contractors, all of 8 camps separate access to water and sanitation facilities for women and men and separate quarters, as well as suitable worker safety training, equipment. As details: Champasak Province: sub-project C1: Nakasang Access Road and Port Rehabilitation</p>	<p>The Gender Specialist will continue to coordinate with PIU and contractors to maintain this requirement, particularly for the subproject TIIGP2-LAO-W03a once the construction commences</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>as suitable worker safety training, equipment.</p>	<p>- 1 contractor, 3 Camps: Nakasang Camp, Dondet Camp & Donkhone Camp</p> <p><u>Vientiane Province</u> sub-project V1: Nam Ngum Reservoir Access Improvements. - 1 contractor, 1 Camp: Km 4+200 Camp</p> <p><u>Vang Vieng District:</u> sub-projects V2: Kaeng Yui Waterfall Access Improvement and sub-projects V3: Western Loop Rural Access Road and Bridge Improvement, - 1 contractor, 2 camps sub-project V5: Vang Vieng Solid Waste Management - 1 contractor (Cetuea-Panyathilath joint venture) 2 camps:</p>	
<p>Activity 2: Contractors provide gender-responsive information on HIV/AIDS, STI, human trafficking and child labor exploitation prevention information to all workers.</p>	<p>On-track/more information needed</p> <p>In all sub-project areas, the Contractors provide gender-responsive information on HIV/AIDS, STI, human trafficking and child labor exploitation prevention via meeting/training and IEC campaigns</p> <p>Relevant GAP provisions are included in bidding documents and contracts for packages TIIGP2-LAO-W01, TIIGP2-LAO-W02, and TIIGP2-LAO-W03 and TIIGP2-LAO-W04. The contracts also included budget in the BOQ for the contractor to conduct consultations and awareness raising activities during construction on gender-responsive information on HIV/AIDS, STI, human trafficking and child labor exploitation prevention.</p> <p>The IGS prepared the slides of core messages that the NGS translated and explains as appropriate to the site. There is also a list of Gender / HIV-AIDS resource persons in the province that are listed in the resource pool.</p> <p>The Gender specialists also compiled lists of gender resource persons/service providers and information materials on HIV-AIDS, STI, gender-based violence and child labor exploitation to be used for these activities.</p> <p>The first of the series of gender safeguards orientation was conducted in TIIGP2-LAO-W01 subproject (Nakasang) with the participation of the National Gender specialist on February 8-11, 2021. For the series of 3 consultations, the NGS reported that a total of 93 persons attended, of who 33 were women or 35.48%.</p>	<p>The Gender Specialist will continue coordinating with PIU and contractors to keep this activity implemented regularly (at least twice per year)</p> <p>No of participants will double-checked and confirmed.</p> <p>As of June 2023, the total unskilled workers hired for across all 6 sub-projects is 100 of whom 24 are local women (24%)</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>Conducted IEC campaign in Nam Ngum Reservoir on 21-22 December 2021 (Works Package: TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements-Subproject V1: Nam Ngum Reservoir Access Improvements. (Total participants 31, women: 8)</p> <p>Conducted IEC campaign in Vang Vieng on 23-25 December 2021 (Works Package: TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements. (Total participants 106, women: 46).</p>	
Objective 3. Improve gender design features of tourism facilities to support economic empowerment.		
<p>Target 6: All women vendors return to improved market space after construction (2017 baseline: ~80% (120 women).</p>	<p>On-track</p> <p>The project is improving 3 market sites (i) Kaeng Yui Waterfall (ii) Nam Ngum Reservoir and (iii) Nakasang Access Road and Port Rehabilitation. Constructions are ongoing.</p> <p>(i) Kaeng Yui Waterfall: total 3 vendors (rotation based, there is no owner, so it cannot identify men and women vendors (ii) Nam Ngum Reservoir: total 28 vendors (19 vendors were household base and 9 vendors women headed of household) (iii) Nakasang Access Road and Port Rehabilitation: total 10 vendors (9 vendors were household base and 1 vendors woman headed of household)</p> <p>The project will ensure all vendors return to improved market space after construction</p>	<p>The Gender Specialist will continue coordinating with PIU and social safeguard team to follow up and accomplish this target.</p>
<p>Target 7: At least 80% (80 women) of newly constructed shop owners/operators are women.</p>	<p>On-track</p> <p>All constructions are ongoing, and the project noted that 80% of newly constructed shop owners/operators must be women.</p>	<p>The Gender Specialist will continue coordinating with PIU and social safeguard team to follow up and accomplish this target.</p>
<p>Activity 3: Infrastructure subproject gender design features include suitable road shoulders, access for people with disabilities, public</p>	<p>On-track</p> <p>All infrastructure subproject, gender design features include suitable road shoulders, access for people with disabilities, public lighting, separate male and female toilets, lockable kiosks, road safety instruction, and others identified during consultations. The project will check after construction completed.</p>	<p>The Gender Specialist will continue coordinating with PIU and social safeguard team to</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>lighting, separate male and female toilets, lockable kiosks, road safety instruction, and others identified during consultations.</p>	<p>For detailed designs for packages TIIGP2-LAO-W01 (subprojects C1, C2) and TIIGP2-LAO-W04 (subproject V5) prepared during project preparation: Road shoulders, access for people with disabilities were designed as follows.</p> <ul style="list-style-type: none"> • Roads are designed according to established and recent national standards and guidelines. • Roads and foot paths are also designed to maximize available area in the available alignments. • Public lighting is included at the Vang Vieng Landfill (V5), in the Nakasang town/port improvement (C1), and on the bridge between Don Det and Don Khone (C2). • Separate areas with showers, toilets, lockers etc. for male and female workers are planned for the Vang Vieng landfill subproject (V5). • Site buildings at the Vang Vieng landfill site will be accessible for disabled, included HCWC (V5). • Road safety instructions will be a part of subsequent project phases, however the design criteria used have road safety as a key basis. • No specific issues related to gender design features were raised during the consultations with the IAs and other stakeholders. <p>These provisions have been integrally retained in the final DED for TIIGP2-LAO-W01 (subprojects C1&C2) and in the revision of DED for TIIGP2-LAO-W04 (subproject V5).</p> <p>For TIIGP2-LAO-W02 (subproject V1), TIIGP2-LAO-W03 (subprojects V2, V3) and TIIGP2-LAO-W03a (subproject V4): Gender and disability design features have been considered and incorporated in the detailed design. For example, for subprojects V1 (Nam Ngum) and V2 (Kaeng Yui), main areas and facilities, including public toilets, will be wheelchair - accessible. The IGS reviewed the project design and found that the gender features included.</p>	<p>follow up and accomplish this target.</p>
<p>Activity 4: Infrastructure user charges (e.g. market stall rent and waste collection fees) are affordable to male and female users.</p>	<p>On-track</p> <p>Constructions are ongoing, the project will consider of market stall rent and waste collection fees after construction completed. The project consulted with:</p> <p>TIIGP2-LAO-W04 (subproject V5): Residents of Vang Vieng expressed concerns about affordability of garbage collection fees during a dialogue with GAD specialists and PIU on 10 October 2019. Affordability of user charges has</p>	<p>The Gender Specialist will continue coordinating with PIU and social safeguard team to follow up and accomplish this target.</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>been considered in the outline and detailed design. The PMCES Consultant institutional specialists will conduct consultations with users on user charges and include the results in O&M planning.</p> <p>TIIGP2-LAO-W02 (subproject V1): Affordability of replacement shops and residences for the affected businesses and households at the marina at Nam Ngum has been carefully considered and consultations held with affected men and women. The updated resettlement plan now specifies that the first-year rent will be waived, years 2-3 will be reduced by 50%, to ensure affordability and allow time for the businesses to build up and generate sufficient revenue to afford the full rental fee which will kick in in year 5.</p>	
Objective 4. Ensure women's equal participation in gender-sensitive IEC programs to mitigate tourism's social risks.		
<p>Target 8: 50% of IEC facilitators trained by the project are women.</p>	<p>Achieved</p> <p>There are 9 gender focal persons composed of 4 male and 5 female (55 %) who serves as the lead on-site IEC facilitators. They participated in the one-day gender-responsive training that the gender specialists' team conducted in the provinces from 13 – 30 June 2022 by the project gender team (Luz Lopez Rodriguez / International Gender Specialist; Vivath Sauvaly / M & E and NGS; and Bounkheua Chansy, MICT Gender Focal Person).</p>	<p>A follow-up training of gender focal persons as gender training facilitators, gender analysis in project implementation and monitoring is recommended to follow-up and sustain the gender-responsive tourism elements.</p>
<p>Target 9: At least 50% of people reached by gender-sensitive IEC campaigns are women (2017 baseline: 0% women).</p>	<p>On-track/more information needed</p> <p>87 (38%) out of 230 participants attended the IEC campaigns in the 3 sub-project sites were women</p> <p>(i) Sub-project W01: Nakasang Access Road and Port Rehabilitation on 8-11 February 2021, 33 (35%) out of total 93 participants were women;</p> <p>(ii) Conducted IEC campaign in Nam Ngum Reservoir for Works Package TIIGP2-LAO-W02: Subproject V1: Nam Ngum Reservoir Access Improvements on 21-22 December 2022: 8(26%) out of 31 were women</p> <p>(iii) Conducted IEC campaign in Vang Vieng for Works Package: TIIGP2-LAO-W03: sub-projects V2: Kaeng Yui Waterfall Access Improvement; and V3: Western Loop Rural Access Road and Bridge Improvement on 23-25 December 2021 - 46 (43%) out of 106 were women</p>	<p>The project will conduct more campaigns and ensure more women participation.</p> <p>- The Gender Specialist will continue coordinating with PIU and contractors to keep this activity implemented regularly (at least 1 campaign per year)</p> <p>Following will be confirmed/provided:</p> <p>(i) These data are repeat to Activity 2, please ensure that gender-sensitive IEC campaigns is provided to communities live in vicinity</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
		<p>along the infrastructure subprojects sites</p> <p>(ii) Provided list if the IEC campaign topics</p> <p>(iii) To ensure 50% of participants are women, coordination will be done with the LWU, and relevant government agencies such as district officers from traffic police, public health, etc.</p>
<p>Activity 5: IEC materials are gender-sensitive (i.e. without gender bias/stereotypes) and published for each topic covered, e.g. (i) traffic and boating safety, (ii) HIV/AIDS prevention, (iii) human trafficking prevention and (iv) solid waste management</p>	<p>Achieved/more information needed GAD specialists have scanned and identified appropriate gender-sensitive campaign materials from UNFPA, and national government agencies. IEC reference/training Manual is being prepared by the International Gender Specialist.</p> <p>National Gender Specialist collected 50 copies of each type of brochures, flyers, posters and others related materials on HIV- AIDS, human trafficking prevention, violence against women and children, from different related national and international organizations such as ILO, UNFPA etc. These were allocated at least 10 of each material per worksite.</p> <p>Based on this, IEC material packages have been distributed in the construction sites and to the surrounding communities during IEC Campaigns conducted in Vientiane Province for works packages TIIGP2-LAO-W02: Nam Ngum Reservoir Access Improvements and TIIGP2-LAO-W03: Kaeng Yui Waterfall Access Improvements and Western Loop Rural Access Road and Bridge Improvements (21-25 December 2021).</p>	<p>More IEC materials will be gathered and reproduced based on the follow-up assessment of needs. Coordination will be done with the LWU, the provincial CAWs of relevant government agencies on these materials.</p> <p>The Gender Specialist will continue coordinating with PIU and contractors to accomplish this activity</p> <p>Comment: Clear information will be provided that show IEC materials prepared by project are gender-sensitive</p>
<p>Output 2: Capacity to implement ASEAN Tourism Standards strengthened</p>		
<p>Objective 5. Promote women’s leadership.</p>		

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>Target 10: At least 30% of ASEAN tourism standards certification board members and assessors are women (2017 baseline: 0).</p> <p>(DMF output indicator 2a)</p>	<p>Achieved 86 (43%) out of 200 of ASEAN tourism standards certification board members and assessors were women</p> <p><u>National: 51.06 % (48 women out of 94 members and assessors):</u></p> <ul style="list-style-type: none"> • ASEAN Green Hotel: 8 (62%) out of 1 were omen; dated 21/07/2021 • ASEAN Spa Service: 7 (64%) out of 11 were women; dated 21/07/2021 • ASEAN Homestay Standard: 3 (33%) out of 9); dated 27/08/2021 • ASEAN Public Toilet Standard: 4 (44%) out of 9) (official appointment awaiting signature) • ASEAN Clean City Standard: 8(47%) out of 17 were women; dated 11/08/2021 • ASEAN CBT Standard 2 (22%) out of 9 ere women- dated 14/09/2021 Not Achieved • ASEAN MICE Standard: 8(62%) out of 13 were women; dated 25/06/2021 • ASTA: 8 (62%) out of 13 were women dated 09/2021 (waiting for signature) <p><u>Provinces: 38 (36%) out of 106 members and assessors were women:</u></p> <ul style="list-style-type: none"> • Champasak Province: 14(34%) out of 41 were women; dated 22 June 2021 • Vientiane Province: 6(33%) out of 18 were women; dated 22/07/2021 • Vang Vieng District: 9(30%) out of 30 were women; dated 14/06/2021 • Luang Prabang Province: 9(53%) out of 17 were women; dated 20/09/2022. 	<p>The project will re-establish of ASEAN CBT and Luang Prabang province (why LPB, since it already reached target “53%:”) “to meet the target of board member and assessors’ members- Please put expected time and responsibility? - The Gender Specialist will continue coordinating with project consultants, MICT ASEAN Tourism Standard Secretariat , PIU to accomplish this target.</p>
<p>Target 11: At least 35% of ASEAN tourism standards trainers are women (2017 baseline: 0)</p>	<p>On-track 72 (40.2%) out of 179_trainers at different levels (Master Trainers, National trainers and Provincial trainers are women.</p> <ul style="list-style-type: none"> • Master Trainers: Overall 5(42%) out of 12 were women <ul style="list-style-type: none"> - ASEAN Green Hotel & ASEAN Spa Service: 1 (50%) out of 2 was woman; - ASEAN Homestay Standard: 1 (50%) out of 2 was woman; - ASEAN Public Toilet Standard: 0% (0 out of 1) -Not Achieved - ASEAN Clean Tourist City Standard: 67% (2 out of 3); - ASEAN CBT Standard 0% (0 out of 1) -Not Achieved - ASEAN MICE Standard: 0% (0 out of 2); -Not Achieved - ASTA: 100 % (1 out of 1) • National Trainers: Overall 34 (55%) out of 62 were women 	<p>The project has to ensure to meet target 35 % of trainers are women</p> <p>(i) Master trainers include more women in the training on (a) ASEAN Public Toilet Standard (b) ASEAN CBT Standard and (c) ASEAN CBT Standard.</p> <p>(ii) National Trainers include more women in the training on (a) ASEAN Public Toilet Standard and (b) ASEAN CBT Standard</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<ul style="list-style-type: none"> - ASEAN Green Hotel: 2(67%) out of 3 were women; - ASEAN Spa Service: 2(67%) out of 3 were women; - ASEAN Homestay Standard: 100% (2 out of 2); - ASEAN Public Toilet Standard: 1 (33%) out of 3 was woman- Not Achieved - ASEAN Clean Tourist City Standard: 100% (2 out of 2); - ASEAN CBT Standard 2(22%) out of 9 were women -Not Achieved - ASEAN MICE Standard: 20(67% out of 30 were women; - ASTA: 3(30%) out of 10 were women- Not Achieved • Provinces: 31 (43%) of 105 were women: <ul style="list-style-type: none"> - Champasak Province: 14(34%) out of 41 were women, dated 22 June 2021 Not Achieved - Vientiane Province: 6(33%) out of 18 were women ; dated 22/07/2021 Not Achieved - Vang Vieng District: 9(30%) out of 30 were women; dated 14/06/2021 Not Achieved - Luang Prabang Province: 4(25%)out of 16 were women; dated 03/07/2019 2021- Not Achieved 	<p>(iii)Provincial trainers, the project should include more women (a) Chanpasak (b) Vientiane province(c) Vangvieng and (d) Luangprabang</p> <p>- The Gender Specialist will continue coordinating with project consultants, MICT ASEAN Tourism Standard Secretariate , PIU to accomplish this target.</p>
<p>Target 12: At least 45% of ASEAN tourism awards selection panel members are women (2017 baseline: 0).</p>	<p>On-track ASEAN tourism standards certification board members, assessors and ASEAN tourism awards selection panel members have the same set of members, as enumerated in target 10.</p> <p>There are 86 (43 %) out of 200 ASEAN tourism awards selection panel members are women.</p> <p>Challenge of meeting qualification standards also apply in the shortfall of women targets. The gender specialists, will continue advocating for additional women members, in coordination with the MICT officers and PCU consultants</p>	<p>The project gender team will dialogue with the TDD & TMD offices to encourage more women appointments to ASEAN tourism awards selection panel to reach at least 45 % target by Q4, 2022- Please update</p> <p>The Gender Specialist will continue coordinating with project consultants, MICT ASEAN Tourism Standard Secretariat, PIU to accomplish this target.</p>
<p>Objective 6. Promote equal access to ASEAN tourism standards training and information</p>		
<p>Activity 6: ASEAN tourism standards manuals translated to Lao language.</p>	<p>Achieved Translation of all seven ASEAN Tourism Standards were completed. All seven final standards were published in Lao language.</p>	
	<p>Achieved As of September 2022, 1,046 (40%) out of 2,618</p>	<p>Source of data will be provided</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>Target 13. At least 40 % of women participants in ASEAN tourism standards training for businesses are women.</p>	<p>are women participated in ASEAN tourism standards training for businesses. <u>Source of data: Record of Activity (2019-June 2023)</u></p>	
<p>Output 3: Institutional arrangements for tourism destination management and infrastructure O&M strengthened</p>		
<p>Objective 7. Promote gender- balanced project management.</p>		
<p>Target 14: At least 3,000⁸ residents and tourism workers (50% women) participated in destination management training and awareness-raising activities. (2017 baseline: 0) (DMF output indicator 3c)</p>	<p>On track As of June 2023, 5,733 (2,643 women or 46%) participants (residents and tourism workers) have participated in destination management training and awareness-raising activities. <u>Source of data: Record of Activity (2019-June 2023)</u></p>	<p>The project will coordinate with TDD and TMD on targeting more than 55 % participants in the succeeding training activities to achieve the 50 % target. It is recommended that the training will include modules on gender-responsive tourism. This will be undertaken from Q2 to Q4 2023.</p>
<p>Target 15: Women comprise at least 30% of project steering committee (PSC) members. (2017 baseline: ~25% (4 women))</p>	<p>Achieved 4(36%) out of 11 PSC members were women The Project Steering Committee is composed of national members and representatives of provinces that host the sub-projects. National: Agreement dated 13 July 2021 with 3(50%) out of total 6 were women Provinces: 1 (20%) out of 5 were women (i) Champasak Province (Agreement February 2022) 1 male and 1 female (50%) (ii) Vientiane Province (Agreement 16 February 2022): 1 male (iii) Vang Vieng District (Agreement 2 March 2022) 1 male (iv) Luang Prabang province (Agreement 2 February 2022): 1 male</p>	
<p>Target 16: Women hold 30% of project director and deputy director positions. (2017 baseline: 20%). (In financing agreement 40%)</p>	<p>Achieved: The overall total for national and provincial levels is 4 (40%) out of total 10 members were women National: 1 female (50%) out of total 2, Provinces: 3 (37.5%) out of 8 were women,</p>	

⁸ The previous figure listed is 500 based on the total count of Cambodia and Laos. This is now disaggregated to 300 only for Lao PDR (PAM, Annex G, para 21)

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	(i) Champasak Province: Project director and project manager- 2 males; 0 female (ii) VTE Province: (50%)-1 female Project Director and 1 male: Project manager (iii) Vang Vieng District (50%)- 1 male Project Director; 1 female Project manager (iv) Luang Prabang province: (50%)-1 female Project Director; 1 male Project manager.	
Target 17: At least 40% of overall PCU and PIU staff positions are held by women (2017 baseline: 34%). (In financing agreement 30%)	Achieved: Of the overall total of 19 (46.3%) out of total 41 PCU and PIU staff were females National PCU: 4 (67%) out of 6 were women Provincial PIU: 15 (42.8%) out of total of 35 were women (i) Champasak Province, 3 (37.5%) out of 8 were women (ii) VTE Province: 4 (40%) out of 10 were women (iii) Vangvieng District, 4 (44%) out of 9 were women (iv) Luang Prabang province, 4 (50%) out of 8 were women	
Target 18: At least 30% of PCU and PIU staff that attend technical and project management training are women.	Achieved: As of June 2022, 201(46%) out of 4,35 participants among PCU and PIU staff, who attended technical and project management training are women. Such as: <ul style="list-style-type: none"> ▪ Training of trainers on tourism management ▪ Training on "how to organize workshop and meeting professionally" and using IT system to support organizations operation and tourism promotion work ▪ Training on the implementation of the DMPs for Vientiane province and Vang Vieng PIUs and other tourism sector staff ▪ Training on implementation of destination management ▪ Training of trainer on tourism and hospitality services for all DICTs (across the country) ▪ Training on destination management planning and DMP Action Plan preparation for national level DMN Taskforces ▪ Training of Trainers on Presentation Skills for tourism sector staff (public and business sectors) along NSEC ▪ The 1st annual Training of Trainers on how to draft Destination Management Plan for 4 Tourism Departments in Vientiane Province. ▪ Conduct training on tourism development planning for tourism sector staff at provincial and district levels 	Expected time will be provided that the Gender specialist will coordinate with PCU and PIU to collect data on: <ul style="list-style-type: none"> (i) How many technical and project management trainings project conducted? (excl. workshops) (ii) Each member of PCU and PIU participate in each training (iii) Each training how many participants from PCU and PIU (men, women and %)

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<ul style="list-style-type: none"> ▪ Training on how to develop the photo galleries and tourism information files ▪ Training on the use of assessment form and pilot/trial assessment on tourist attractions classification standard for four tourism departments ▪ Training on drafting the destination management plan ▪ Training on application of filing system (documents) ▪ Training on preparation and conduct of meetings and workshops for tourism management staff ▪ Training on project proposal ▪ Provide training on grievance redressal mechanisms for the Arbitration Committee ▪ Training on mobile application management and maintain for the members of Lan Xang Culture Quadrangle Network. 	
Objective 8. Promote women's representation in destination management network (DMN) and infrastructure O&M entities.		
Target 19: DMN managers comprise at least 30% women (2017 baseline: ~30%).	Achieved 17 (48.5%) out of total 35 National & Provincial DMN were female Detail: (i) National: 5(50%) out of 10 were female (Agreement dated 25 November 2021) (ii) Champasak: 3(43%) out of 7 were female (Agreement dated 3 Dec 2021) (iii) Vientiane Province: 4(50%) out of 8 were female (Agreement dated /m/y.) (iv) Vang Vieng District: 2(40%) out of 5 were female (Agreement dated 28 March 2022) (v) Luang Prabang province: 3(60%) out of 5 were female (agreement dated 31 December 2021)	Agreement date for Vientiane province will be added
Target 20: Women comprise at least 40% of total DMN membership (2017 baseline: ~30%).	Achieved 28 (60%) out of 55 National & Provincial DMN membership were female. Detail: (i) National: 6 (50%) out of total 12 were female (ii) Champasak Province: 6 (54%) out of total 11 were female (iii) Vientiane Province: 4 (40%) out of total 10 were female (iv) Vang Vieng District: 6 (50%) out of total 12 were female (v) Luang Prabang province: 6 (60%) out of total 10 were female	
Target 21: At least 30% of 150 public works and tourism site	Achieved	Expected time will be provide for the project to review the content

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>managers (90 public works and tourism site managers in Lao PDR) are women, with skills, equipment, and budget needed to effectively develop and implement tourism management plans and infrastructure O&M (2017 baseline: 0) (DMF output indicator 3a)</p>	<p>Q1 2023: (Jan-March 2023) - 3 workshops for W04 VV Landfill: (1) Workshops for lesson sharing on SWM and landfill operation with VCOM; (2) Workshops for lesson sharing on SWM and landfill operation with Kaysone Phomvihanh City UDAA (3) Technical Workshop on proposed new SWM and Landndfill O&M Approach for Vangvieng with VTE Province PCU and Vangvieng Authorities. - 4 workshops and meetings for W01 Nakasang: (1) Consulting meeting on preference O&M approach with Khong District Authority; (2) Consulting meeting on preference O&M approach with Nakasang and Phiengdy community; (3) Meeting on proposed O&M approach for Nakasang River Port and parking area with Khong authorities; (4) Meeting on proposed O&M approach for Nakasang River Port and parking area with Nakasang and Phiengdy community Total: 99 (30 women or 30%) As of March 2023, total 122 (36 women or 29.5%)</p> <p>Q2 2023: (April-June 2023) -W01: (1) Consultation Workshop with Khong District Authority (5 April 2023) total: 13 (4 women); (2) Consultation Workshop with Nakasang, Phiengdy communities (8 April 2023) total: 15 (4 women); (3) Final Consultation Meeting with Khong District Authority (7-8 June 2023) total: 6 (2 women). -W03: Consultation Meeting on Site Management and O&M Plan for Kaeng Yui Waterfall, Vang Vieng District (10 May 2023) total 32 (9 women) -W04: Development Partner meeting (13 June 2023) total: 12 (6 women) Q2 2023: total 78 (25 women)</p> <p>As of June 2023, total 200 (61 women or 30.5%)</p>	<p>of site management plans and O&M plans and provide feedback / suggestions on gender responsiveness and ensure meeting this target</p> <p>Each of capacity building activities for public works and tourism site managers on site management and O&M plan will set a quota for at least 30% of female participants.</p> <p>- The Gender Specialist will continue supporting women participation in future capacity building activities to reach the 30% target for this indicator</p>
<p>Target 22: Community tourism groups involving women and youth (at least 40% women and girl's membership) are established or strengthened in all sites with community-managed tourist attractions.</p>	<p>On track The numbers of sites in the project target areas that are community managed. It will be identified through site management and O&M plan development process. Once identified, their membership will be recorded. During project implementation additional community-managed tourism groups may be established, and their capacity built.</p> <p>Activities not yet started</p>	<p>The project gender team will work with Tourism specialist to coordinate with PIU to ensure community tourism groups involving women and youth (at least 40% women and women's membership) Gender specialist will coordinate with the project consultants and PIU to collect data on the name list of the sites with community-managed tourist attractions and</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>Target 23: At least 50% of participants in tourism-related service training are women (2017 baseline: ~70%).</p>	<p>Achieved As of June 2023. 345 (53%) out of 649 participants in tourism-related service training are women such as:</p> <ul style="list-style-type: none"> ▪ TOT on hotel management (accommodation) ▪ Training of trainer on entertainment and restaurant management ▪ Training of trainer on tourism and hospitality services for all DICTs (across the country) ▪ Training on English Language skills for effective services of Tour Guide, Hotel, Guesthouse and Restaurant ▪ Training on human relations and service psychology for tourism business providers (tour operators, hotel and restaurant owners/providers...) ▪ Training for site guides ▪ Training for heritage tour guides ▪ World heritage tour guide training in Champasak. ▪ Training on tour guides in LPB LPB, 2-24 May 2023 total: 70 (37 women) <p>Needs assessment was recently conducted as basis for training programs to be updated by Q1-2023</p>	<p>number of women and girl's membership.</p> <p>The project gender team will coordinate with the project consultants to collect data on the name list of tourism-related service trainings as well as the number of participants to ensure 50% of participants are women-Pls. put the expected time</p>
<p>Objective 9. Improve gender mainstreaming capacity to implement and monitor the GAP and report gender impacts.</p>		
<p>Target 24: 50% of 10 gender focal persons appointed to PCU, and PIUs are men.⁹</p>	<p>Not achieved yet. Of the total 9 gender focal persons, 5 (55%) were female and 4 (45%) were men.</p> <ul style="list-style-type: none"> - Four (4) male and 4 female focal persons at the PIU and - One female focal person at the national level. 	<p>PCU will appoint one male gender focal to meet the target 10 gender focal persons and 50% are men. The Gender Specialist will continue coordinating with project manager to accomplish this target. Pls. put the expected time</p>
<p>Activity 7: Gender specialists and social development consultants provide gender equality training and GAP</p>	<p>Achieved The International Gender Specialist (IGS) was recruited on 26 August 2019 and has been working closely with the National Gender Specialist (NGS). After the initial 2-person months contract is used up, her second contract variation for</p>	

⁹ The project established one PCU and 4 PIUs

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
<p>implementation training to all project supervision, management, and coordination entities.</p>	<p>additional 1.5 person-months was approved on 12 February 2022. The overall total from the original contract to the second contract variation is 5 person-months.</p> <p>The contract of the first National Gender Specialist (NGS), who served the post since TIIGP1, was used up after several contract variations until December 2021 and was no longer extended. The tasks of the NGS are taken over by the M & E Specialist who has gender experience. The MICT Gender Focal person is also tapped to support provincial gender training.</p> <p>They consulted with the PCU officers, the PMCES Consultant and M&E consultants.</p> <p>During the IGS' first in-country mission, she provided gender orientation training to PCU members and project consultants (18 attended, 10 were women) on 21 Oct. 2019. This was followed by a series of gender consultation workshops on 9-10 Oct 2019 with PIU-Vang Vieng, Ban Naduang and Ban Phon Vieng (target sub-project sites) and Sengsavang village authorities. A total of 103 participated, 40 (39 %) of whom were women.</p> <p>A series of one-day trainings on GAP Implementation and Documentation to PIUs and gender focal persons in Vientiane Province (Nam Ngum and Vang Vieng) on 29-31 January 2020, in Champasak on 3-6 February 2020, and Luang Prabang on 10-12 February 2020, to discuss with GAD focal persons the GAP indicators that they have to monitor, document and report quarterly, and the case study outline of GAD impact stories they have to identify, monitor and document towards the mid-term project review. A total of 86 participated, 55 (64%) of whom were women.</p> <p>A series of trainings in gender-responsive tourism was conducted in the provinces from June 13 – 30 2022 and Vientiane capital on 1 July 1 2022</p>	
<p>Activity 8: GAP targets and actions are reflected in annual project work plans and reported in quarterly progress reports.</p>	<p>Achieved.</p> <p>The annual project plans (2019, 2020 and 2021) were reviewed along with the overall Gender Action Plan. Gender focal persons (one male and one female) were appointed for each PIU.</p> <p>The project's annual workplan for 2021 and 2022 included GAP targets and activities and the budget has been allocated for GAP activities.</p>	<p>The Gender Specialist will continue coordinating with project consultants to accomplish this target.</p> <p>In future reports there will be a confirmation that:</p>

Gender Action Plan (GAP) ⁴	Progress to date (up to June 2023)	Issues and Challenges ⁵
	<p>All GAD focal persons were oriented on the ADB and Lao PDR gender equality policies and principles in sustainable tourism. Specific women participation targets have been incorporated in the project workplan from 2021 onwards.</p> <p>The GAD specialists drafted their individual and team workplans for 2021 and 2022 based on the GAP.</p>	<p>(i) GAP targets and actions are reflected in 2023 project work plans</p> <p>(ii) GAP targets and actions are reflected quarterly progress reports.</p>
<p>Activity 9: PPMS includes sex-disaggregated indicators and templates to track GAP progress, implementation, and project benefits.</p>	<p>Achieved. The PPMS and baseline report were submitted to ADB in Q2 2020. PPMS is being improved and agreed to be finalized by Q1 2022. The International and National Gender Specialists support the monitoring of GAP indicators and alignment and report on GAP progress accordingly.</p>	<p>Comment: Confirm PPMS includes sex-disaggregated indicators</p>
<p>Target 25: At least 3 human impact stories on GAP implementation, including women's understanding of, and satisfaction with project design, and improved economic opportunities are documented for publication.</p>	<p>On-track The GAD specialists consulted with PCU and PIU gender focal persons on the draft template of gender impact stories.</p> <p>PIU-GFPs had orientation on gender guidelines for case studies but will need follow-up refresher and materials when GAD specialist does provincial visits. This case study guideline was shared with them.</p> <p>The project will:</p> <p>(i) Identify 3 human impact stories by Q2 – 2023 demonstrating positive changes brought by the project interventions. The stories could be about (a) a woman, or a group of women who have upgraded her/their knowledge and capacity after project interventions; (b) livelihood improvement because of project interventions by comparing income and/or living conditions before and after project activities; (c) strategic change such as the changes of institution's strategy to support women. This could be a story of woman who got promotion or has opportunity to work at the decision-making level.</p> <p>(ii). All 3 human impact stories will be completed by Q1-2024</p>	<p>Suggest to</p> <p>(i) Identify three human impact stories by Q2 – 2023 All 3 human impact stories completed Q1-2024</p>

Annex 10: Status of compliance with Grant Covenants as of 30 June 2023

Item	Covenants	Status of Compliance
	Grant Agreement Article IV: Particular Covenants	
1	Section 4.01. In the carrying out of the Project and operation of the Project facilities, the Recipient shall perform, or cause to be performed, all obligations set forth in Schedule 4 to this Grant Agreement.	Compliant
2	Section 4.02. (a) The Recipient shall (i) maintain separate accounts and records for the Project; (ii) prepare annual financial statements for the Project in accordance with financial reporting standards acceptable to ADB; (iii) have such financial statements audited annually by independent auditors whose qualifications, experience and terms of reference are acceptable to ADB, in accordance with auditing standards acceptable to ADB; (iv) as part of each such audit, have the auditors prepare a report, which includes the auditors' opinion(s) on the financial statements and the use of the Grant proceeds, and a management letter (which sets out the deficiencies in the internal control of the Project that were identified in the course of the audit, if any); and (v) furnish to ADB, no later than 6 months after the end of each related fiscal year, copies of such audited financial statements, audit report and management letter, all in the English language, and such other information concerning these documents and the audit thereof as ADB shall from time to time reasonably request.	Compliant <ul style="list-style-type: none"> • PCU and PIUs maintain separate accounts and records for the Project • PCU prepares annual financial statements for the Project • Annual project financial statements (APFS) are audited by the State Auditing Organization of Lao PDR (SAO). The first annual audit to cover the period 25 December 2018 to 31 December 2019 was submitted to ADB on 29 October 2020 after ADB's extension of the deadline to 31 December due to COVID-19. The 2020 APFS was submitted to ADB on 22 September 2021. The APFS for FY 2021 was submitted on 28 June 2022.
3	Section 4.02. (b) ADB shall disclose the annual audited financial statements for the Project and the opinion of the auditors on the financial statements within 14 days of the date of ADB's confirmation of their acceptability by posting them on ADB's website.	Compliant. <ul style="list-style-type: none"> • The first audited APFS (25 December 2018 to 31 December 2019) and auditor's opinion were disclosed on the ADB website on 18 November 2020. • The 2020 APFS was disclosed on the ADB website on 29 September 2021. • The 2021 APFS was disclosed on the ADB website in June 2022.
4	Section 4.02. (c) The Recipient shall enable ADB, upon ADB's request, to discuss the financial statements for the Project and the Recipient's financial affairs where they relate to the Project with the auditors appointed pursuant to subsection (a)(iii) hereinabove, and shall authorize and require any representative of such auditors to participate in any such discussions requested by ADB. This is provided that such discussions shall be conducted only in the presence of an authorized officer of the Recipient, unless the Recipient shall otherwise agree.	Compliant
5	Section 4.03. The Recipient shall enable ADB's representatives to inspect the Project, the Goods and Works, and any relevant records and documents.	Compliant
	Grant Agreement Schedule 4	
6	<u>Implementation Arrangements</u> The Recipient shall ensure that the Project is implemented in accordance with the detailed arrangements set forth in the PAM. Any	Compliant

Item	Covenants	Status of Compliance
	subsequent change to the PAM shall become effective only after approval of such change by the Recipient and ADB. In the event of any discrepancy between the PAM and this Grant Agreement, the provisions of this Grant Agreement shall prevail.	
7	<u>Environment</u> The Recipient shall ensure that the preparation, design, construction, implementation, operation and decommissioning of the Project and all Project facilities comply with (a) all applicable laws and regulations of the Recipient relating to environment, health and safety; (b) the Environmental Safeguards; and (c) all measures and requirements set forth in the IEE, the EMPs, and any corrective or preventative actions set forth in a Safeguards Monitoring Report.	Compliant
8	<u>Land Acquisition and Involuntary Resettlement</u> The Recipient shall ensure that all land and all rights- of-way required for the Project are made available to the Works contractor in accordance with the schedule agreed under the related Works contract and all land acquisition and resettlement activities are implemented in compliance with (a) all applicable laws and regulations of the Recipient relating to land acquisition and involuntary resettlement; (b) the Involuntary Resettlement Safeguards; and (c) all measures and requirements set forth in the RP, and any corrective or preventative actions set forth in the Safeguards Monitoring Report. Without limiting the application of the Involuntary Resettlement Safeguards or the RP, the Recipient shall ensure that no physical or economic displacement takes place in connection with the Project until: (a) compensation and other entitlements have been provided to affected people in accordance with the RP; and (b) a comprehensive income and livelihood restoration program has been established in accordance with the RP.	Compliant All subprojects have up to date safeguards instruments in place including RP and CCRs.
9	<u>Indigenous Peoples</u> The Recipient shall ensure that the preparation, design, construction, implementation and operation of the Project and all Project facilities comply with (a) all applicable laws and regulations of the Recipient relating to indigenous peoples; (b) the Indigenous Peoples Safeguards; and (c) all measures and requirements set forth in the IPP, and any corrective or preventative actions (i) set forth in a Safeguards Monitoring Report, or (ii) subsequently agreed between ADB and the Recipient.	Compliant
10	<u>Human and Financial Resources to Implement Safeguards Requirements</u> The Recipient shall make available necessary budgetary and human resources to fully implement the EMPs, the RP and the IPP.	Compliant
11	<u>Safeguards - Related Provisions in Bidding Documents and Works Contracts</u> The Recipient shall ensure that all bidding documents and contracts for Works contain provisions that require contractors to: (a) comply with the measures relevant to the contractor set forth in the IEE, the EMPs, the RP and the IPP (to the extent they concern impacts on affected people during construction), and any corrective or preventative actions set forth in a Safeguards Monitoring Report; (b) make available a budget for all such environmental and social measures; (c) provide the Recipient with a written notice of any unanticipated environmental, resettlement or indigenous peoples risks or impacts that arise during' construction, implementation or operation of the Project that were not considered in the IEE, the EMPs, the RP and the IPP;	Compliant IEE/EMPs, RPs and EGDRPs are included in Works bidding documents and contracts, and contracts include provisions that require contractors to make available budget and comply with these documents, and to promptly report any safeguards risk or impacts.

Item	Covenants	Status of Compliance
	(d) adequately record the condition of roads, agricultural land and other infrastructure prior to starting to transport materials and construction; and (e) reinstate pathways, other local infrastructure, and agricultural land to at least their pre- project condition upon the completion of construction.	
12	<u>Safeguards Monitoring and Reporting</u> The Recipient shall do the following: (a) submit semi- annual Safeguards Monitoring Reports to ADB and disclose relevant information from such reports to affected persons promptly upon submission; (b) if any unanticipated environmental and/or social risks and impacts arise during construction, implementation or operation of the Project that were not considered in the IEE, the EMPs, the RP and the IPP, promptly inform ADB of the occurrence of such risks or impacts, with detailed description of the event and proposed corrective action plan; and (c) report any actual or potential breach of compliance with the measures and requirements set forth in the EMPs, the RP or the IPP promptly after becoming aware of the breach.	Compliant.
13	<u>Prohibited List of Investments</u> The Recipient shall ensure that no proceeds of the Grant are used to finance any activity included in the list of prohibited investment activities provided in Appendix 5 of the SPS.	Compliant
14	<u>Labor Standards, Health and Safety</u> The Recipient shall ensure that the core labor standards and the Recipient's applicable laws and regulations are complied with during Project implementation. The Recipient shall include specific provisions in the bidding documents and contracts financed by ADB under the Project requiring that the contractors, among other things: (a) comply with the Recipient's applicable labor law and regulations and incorporate applicable workplace occupational safety norms; (b) do not use child labor; (c) do not discriminate workers in respect of employment, sex and occupation; (d) do not use forced labor; (e) allow freedom of association and effectively recognize the right to collective bargaining; and (f) disseminate, or engage appropriate service providers to disseminate, information on the risks of sexually transmitted diseases, including HIV/AIDS, to the employees of contractors engaged under the Project and to members of the local communities surrounding the Project area, particularly women. The Recipient shall strictly monitor compliance with the requirements set forth in paragraph 10 above and provide ADB with regular reports.	Compliant
15	<u>Gender and Development</u> The Recipient shall ensure that (a) the GAP is implemented in accordance with its terms; (b) the bidding documents and contracts include relevant provisions for contractors to comply with the measures set forth in the GAP; (c) adequate resources are allocated for implementation of the GAP; (d) progress on implementation of the GAP, including progress toward achieving key gender outcome and output targets, are regularly monitored and reported on quarterly basis to ADB; and (e) key gender outcome and output targets include: (i) 30% of the overall staff positions and 40% of the management positions in the PCU and PIUs to be filled by women; (ii) appointment of gender focal points in the PCU and each PIU; (iii) at least 40% of training participants under the Project are women; and (iv) disaggregation of all monitoring and evaluation (M&E) data by sex and ethnicity.	Compliant <ul style="list-style-type: none">• GAP is being implemented with support from Gender Specialists (individual consultants)• GAP is included as binding document in bidding documents and works contracts• GAP implementation is adequately resourced• Updated GAP implementation progress reports are attached to quarterly reports.
16	<u>Counterpart Support</u>	Compliant

Item	Covenants	Status of Compliance
	<p>The Recipient shall: (a) through the Project Executing Agency, ensure that counterpart funds for Project implementation are available on time; and (b) ensure that the Project Executing Agency has sufficient funds to satisfy its liabilities arising from any Works, Goods and Consulting Services contract.</p> <p>The Recipient shall (a) through the Project Executing Agency cause each Participating Provinces, prior to their physical completion, prepare and adopt a plan for achieving full cost recovery of the operation and maintenance expenditures of each Project facility within their province; and (b) finance through budget allocation any shortfall in the operation and maintenance of the Project facilities within each Participating Province.</p>	<p>On 24 August 2020 the Ministry of Finance requested ADB to approve financing land acquisition and resettlement (LAR) costs from the grant proceeds, instead of government's counterpart funds. The justification for this request was fiscal constraints due to the COVID-19 pandemic, during which the government has been experiencing challenges meeting its revenue targets, and budget has been reallocated for the emergency COVID-19 pandemic response and recovery. These constraints are impeding the government's ability to make available and thus timely disburse the required LAR compensation payments to the project's affected households.</p> <p>On 27 August 2020, ADB approved a minor change in the project's financing plan to facilitate this, reducing government's counterpart funding from \$1.8 million (3.7% of total project costs) to \$1.68 million (3.5% of total project costs), and consequently, reducing the total project cost from \$48.8 million to \$48.68 million.</p>
17	<p><u>Consultation with Stakeholders</u></p> <p>The Recipient shall ensure that consultation with the Project stakeholders takes place during Project implementation, in accordance with the stakeholder communication strategy set out in the PAM.</p>	Compliant
18	<p><u>Governance and Anticorruption</u></p> <p>The Recipient shall (a) comply with ADB's Anticorruption Policy (1998, as amended to date) and acknowledge that ADB reserves the right to investigate directly, or through its agents, any alleged corrupt, fraudulent, collusive or coercive practice relating to the Project; and (b) cooperate with any such investigation and extend all necessary assistance for satisfactory completion of such investigation.</p> <p>The Recipient shall ensure that the anticorruption provisions acceptable to ADB are included in all bidding documents and contracts, including provisions specifying the right of ADB to audit and examine the records and accounts of the executing and implementing agencies and all contractors, suppliers, consultants, and other service providers as they relate to the Project.</p>	Compliant

Annex 11: ASEAN Tourism Standards Certification in Target Provinces Since 2008

Standard (CPS, VV, LPB, VTP)	Awarded
Homestay	
5) Ban Naduang (Kaeng Nyui waterfall site), Vang Vieng District, Vientiane Province (8 Homestays)	1) 2016, 2019, 2023
6) Ban Hua Don Deng (Don Deng Island), Pa Thoumphone District, Champasak Province (6 Homestays)	2) 2017, 2019, 2023
7) Ban Don Kho (Don Kho Island), Xanasomboun District, Champasak Province (9 Homestays)	3) 2017, 2019, 2023
8) Ban Nayang Tai, Nambak District, Luang Prabang Province (19 Homestays)	4) 2023
Clean Tourist City	
1) Luang Prabang City, Luang Prabang Province	1) 2018, 2022
2) Pakse Champasak	2) 2022
Community-Based Tourism	
1) Ban Nong Luang (Dong Huasao National Protected Area), Paksong District, Champasak Province	1) 2017, 2023
2) Tad Gneung Waterfall, Champasak Province	2) 2023
3) Nathong Village, Vang Vieng District	3) 2023
4) Nayang Tai Village, Luang Prabang Province	4) 2023
Clean Public Toilet	
1) Phousi mountain tourist site, Luang Prabang City, Luang Prabang Province	1) 2019 (expired)
2) Tat Nyeuang waterfall site, Paksong District, Champasak Province	2) 2019 (expired)
3) Khon Phapheng waterfall site, Khong District, Champasak Province	3) 2019 (expired)
4) Public Toilet, Vat Phou Champasak Lao 2nd World Heritage, Champasak Province	4) 2023
5) Public Toilet, Kuangsi Waterfall, Luang Prabang Province	5) 2023
6) Public Toilet, Tham Nang Fa Tourist Site, Vientiane Province	6) 2023
7) Public Toilet, Vat Mai, Luang Prabang Province	7) 2023
8) Public Toilet, Vat Xiengthong, Luang Prabang Province	8) 2023
9) Public Toilet, Mekong River Bank (Phonheuang village), Luang Prabang Province	9) 2023
10) Public Toilet, Electric Car Station, Luang Prabang Province	10) 2023
11) Public Toilet, Kuangsi Waterfall (2)	11) 2023
12) Public Toilet, Vat Phrathong Samsi, Vientiane Province	12) 2023
13) Public Toilet, Nuanta Gas Station, San Sum Village, Vientiane Province	13) 2023
14) Public Toilet, Vat Kang, Vientiane Province	14) 2023
15) Public Toilet, Numngum Dam 1, Vientiane Province	15) 2023
16) Public Toilet, Tad Fane Waterfall, Champasak Province	16) 2023
Green Hotel Champasak Province	
1) Champasak Palace, Pakse City	1) 2008 (expired)
2) Champa Resident, Pakse City	2) 2010 (expired)
3) Champasak Grand, Pakse City	3) 2010 (expired)
4) Khon Phapheng Resort, Khong District	4) 2010 (expired)
5) King Fisher Eco-lodge, Pathoumphone District	5) 2010 (expired)
6) Pakse Hotel, Pakse City	6) 2010 (expired)
7) La Folie Lodge, Champasak	7) 2012 (expired)
8) Atina Hotel, Pakse City	8) 2014 (expired)
9) River Resort, Pakse City	9) 2014 (expired)

10) Sisouk Resident, Pakse City 11) Arawan Riverside Hotel, Pakse City 12) Bachieng Resort, Bachieng District 13) Paksong Danngarm Hotel 14) Pon Arina Luang Prabang Province 1) Phou Vao, Luang Prabang City 2) Souvannaphoum, Luang Prabang City 3) The Grand Luang Prabang, Luang Prabang City 4) Villa Santi, Luang Prabang City 5) 3 Nagas Hotel, Luang Prabang City 6) Luangxay Resident, Luang Prabang City 7) Santi Resort and SPA, Luang Prabang City 8) LPB View 9) Chitchareune Mueang Luang Hotel, Luang Prabang City 10) Kiridara Hotel, Luang Prabang City 11) Sofitel Luang prabang, Luang Prabang City 12) Avani Hotel, Luang Prabang City 13) Pullman Hotel, Luang Prabang City Vientiane Province 1) Riverside Boutique Resort 2) Thavy Souk Hotel 3) Inthira Hotel, Vang Vieng 4) Amari Hotel 5) Long Ngum Resort	10) 2016 (expired) 11) 2016 (expired) 12) 2018 (expired) 13) 2020 14) 2022 1) 2008, 2014 (expired) 2) 2008, 2012, 2014, 2022 3) 2008, 2014, 2022 4) 2010, 2012 (expired) 5) 2010 (expired) 6) 2012 (expired) 7) 2014 (expired) 8) 2016 (expired) 9) 2016 (expired) 10) 2016 (expired) 11) 2018 (expired) 12) 2018 (expired) 13) 2020 1) 2016 (expired) 2) 2018 (expired) 3) 2020 4) 2022 5) 2022
Spa 1) SPA at Kiridara Hotel, Luang Prabang City Expired 2) SPA at Avani Hotel, Luang Prabang City Expired 3) Pullman Spa, Pullman Luang Prabang, Luang Prabang Province 4) Le Spa, Sofitel Luang Prabang, Luang Prabang Province 5) Sanakeo Boutique Hotel and Spa, Luang Prabang Province 6) Angsana Spa, Maikson Souvannaphoum, Luang Prabang Province	1) 2019 (expired) 2) 2019 (expired) 3) 2023 4) 2023 5) 2023 6) 2023
MICE Venue 1) Luang Prabang View Hotel, Luang Prabang City expired 2) Pullman Hotel, Luang Prabang exp 3) Champasak Grand Hotel, Champasak Province expired 4) Amari Vientiane Province valid 5) Aravan Champasak valid	1) 2018 (expired) 2) 2020 (expired) 3) 2020 (expired) 4) 2022 5) 2022
ASEAN Sustainable Tourism Award 1) Phou Si Mountain, Luang Prabang City - Urban Tourism Award 2) Tree Top Explorer, Paksong District, Champasak Province - Rural Tourism Award 3) Wat Xieng Thong, Luang Prabang City – Urban Award 4) Wat Phou, Champasak – Rural Award 5) Tad Nyeuang Champasak – Urban Award 6) Koungsi Waterfall – Rural Award	1) 2018 (expired) 2) 2018 (expired) 3) 2020 (expired) 4) 2020 (expired) 5) 2022 6) 2022

Annex 12: Eligible Project Support for ASEAN Tourism Standards

ASEAN Standard	Eligible Support
Green Hotel	<ul style="list-style-type: none"> • Technical Assistance / Advice to properties to meet ASEAN Green Hotel Standard • Industry training, workshops, or seminars • <i>No assistance for purchase of equipment, materials or upgrade to facilities</i>
Clean Tourist City	<ul style="list-style-type: none"> • Technical Assistance / Advice to meet Standard • Training, workshops, or seminars for public and private stakeholders involved in implementation of the ASEAN Clean Tourist City Standard • Equipment and small works related to public aspects of ASEAN Clean Tourist City Standard (e.g. rubbish bins, public toilet upgrade, signs and visitor information, recycling bins, waste management infrastructure and vehicles where these are publicly owned and managed)
Homestay	<ul style="list-style-type: none"> • Technical Assistance / Advice to meet ASEAN Homestay Standard • Training, workshops, or seminars for homestay operators • Community-owned and operated homestay services only (private sector-managed/operations homestays not eligible) • Improvement to facilities to meet ASEAN Homestay Standard (includes equipment and small works)
Community Based Tourism (CBT)	<ul style="list-style-type: none"> • Training and Technical Assistance to meet ASEAN CBT Standard • Training, workshops, or seminars for CBT operations • Community-owned and operated products only (private sector operations not eligible): Improvement to facilities to meet ASEAN CBT Standard (includes equipment and small works)
Public Toilets	<ul style="list-style-type: none"> • Technical Assistance / Advice to meet ASEAN Public Toilet Standard to public and private toilet operators • Training, workshops, or seminars for public and private stakeholders involved in implementation of the ASEAN Public Toilet Standard • Improvement of publicly owned public toilets (incl. publicly owned toilets operated by private sector through a PPP where per the PPP agreement the public is responsible for maintenance and repair) to meet the ASEAN Public Toilet Standard (includes equipment and small works).
MICE (Meeting Room, Exhibition, Event Venue)	<ul style="list-style-type: none"> • Technical Assistance / Advice to meet ASEAN MICE Standard(s) • Industry training workshops or seminars • <i>No assistance for purchase of equipment, materials or upgrade to facilities</i>
Spa Services	<ul style="list-style-type: none"> • Technical Assistance / Advice to meet Standard • Industry training workshops or seminars • <i>No assistance for purchase of equipment, materials or upgrade to facilities</i>
Sustainable Tourism Award	<ul style="list-style-type: none"> • Training and Technical Assistance to meet Award • Improvement to public and community owned facilities to meet Award criteria (equipment and/or small works)

Annex 13: Progress of Accident Report's Preventive and Corrective Actions

As of 31 July 2023

1. Summary of Planned Preventive and Corrective Actions (Table 4 of Accident Report)
2. Compliance Monitoring by PMCES-PCU (Table 5 of Accident Report)
3. Contractor safety training plan (Appendix 4 of Accident Report)

1. Summary of Planned Preventive and Corrective Actions (Table 4 of Accident Report)

Item	Timing	Activities	Responsible Implementor	Progress as of 31 June 2023	Plan
1	Before 30 Sept 2022	Conduct work hazard assessment at all construction sites under W01, W02, W03 & W04	All contractors with Assistance from PMCES	W01: Conducted on 16 February 2023 W02: conducted on 12 December 2022 W03: conducted on 23 December 2022 W04: conducted in May 2023	-
2	8 Sept 2022	Prepare safety procedure for operation, maintenance and cleaning of mixing plant. Detail improvement plan for mixing including electrical system, the air pump, water pump, the platform of mixing plant, the sedimentation pond.	W03 contractor	W03: Completed on Oct & Nov 2022	-
3	First week of Sept 2022	Drill on the emergency response	W03	W03: Completed on 22 September 2022	August 2023
4	3 rd week of Sept 2022	Frist Aid Training of the contractor's staff	W03 Contractor	Completed on 22 September 2022	Refresh in July 2023
5	By 31 Dec 2022	Develop safety procedures and measures for hazardous construction activities and submit these to PMCES for review and approval	All contractors	W01: Completed (June 2023) W02: Completed (April 2023) W03: Completed (April 2023) W04: Completed (June 2023)	To be continued the hazardous risk assessment which was required control measure actions onsite.
6		Provide health and safety training to their staff including operation, maintenance and cleaning of the mixing plant. 1. Electricity safety training at mixing plant.	All contractors	W01 Completed: Action 2. 30 Oct 2022 Action 3. 30 Oct 2022 Action 4. not required as there is no bridge construction under this package. Action 5. 30 Oct 2022 and Mar 2023	August 2023

Item	Timing	Activities	Responsible Implementor	Progress as of 31 June 2023	Plan
		2. Emergency/training on first aid and safety for workers 3. Construction safety training 4. Safety working at height training for bridge construction. 5. Electricity safety at bridge construction		W02 Completed: Action 1. Sep 2022 Action 2. 21 Dec 2022 Action 3. Oct 2022 Action 4 and 5. Not required due to no bridge W03: 1. Sep 2022 2. May 2022 3. 22 Sep 2022 4. 22 Sep 2022 W04 Completed: Action 1. Not required as there is no batching plant Action 2. 07 Nov 2022 Action 3. 07 Nov 2022 Action 4 and 5 not required due to no bridge construction	Se-annually refresher training in Q3-Q4 2023
7	Daily	Health and Safety staff to record PPE checklist onsite daily.	All contractors	Completed. The EHS Officer of each package W01, W02, W03, W04 have checked and recorded the daily use of PPE	To be continued
8	By 31 Dec 2022	Drill on the emergency response	All contractors	W01: 30 Oct 2022 W02: 21 Dec 2022 W03: 22 Sept 2022 W04: 29 Oct 2022	August 2023
9	By 31 Dec 2022	Updated the CEMP	All contractors	W01: Done in March 2023 W02: Ongoing W03: Done in Dec 2022 W04: Done in March 2023	W02: to be completed by July 2023

2. Compliance Monitoring by PMCES-PCU (Table 5 of Accident Report)

Item	Date	Activities	Responsible Implementor	Progress as of 31 June 2023	Plan
6	Monthly	Monthly the RE of PMCES inspect health and safety (using checklists record) report to PMCES environmental specialist	RE of PMCES	During Aug-Dec 2022 W01: 1 visit in Nov 2022. W02: Yes, carried out at least once a month W03: Yes, carried out at least once a month W04: Yes, carried out at least once a month	The project construction period
7	Monthly	Monitor and follow up on the EHS officer's health and safety inspections (daily checklist)	RE of PMCES	Partly Done W01: Done W02: Partly, EHS officer has inspected the PPE checklist not fully every day, the PPE checklist recorded could be done twice a month. W03: Partly, EHS officer has inspected the PPE checklist not fully every day, the PPE checklist recorded could be done twice a month W04: Partly EHS officer has inspected the PPE checklist not fully every day, the PPE checklist recorded could be done twice a month. Noted: the EHS Officer of each package W01, W02, W03, W04 have checked and recorded the daily use of PPE	Continue throughout the project construction period

Monthly inspection by PMCES consultants on safety management at construction sites.

Updated 31 June 2023

	Aug 2022	Sept 2022	Oct 2022	Nov 2022	Dec 2022
W01	x	x	x	17 Nov	x
W02	23 Aug	15 Sep	05 Oct 27 Oct	30 Nov	22 Dec
W03	19 Aug 24 Aug	14 Sep 22 Sep	x	9 Nov 22 & 23 Nov	15 Dec 23 Dec
W04	x	14 Sep	x	9 Nov	x

	Jan 2023	Feb 2023	Mar 2023	Apr 2023	May 2023	Jun 2023	Jul 2023	Aug 2023	Sep 2023
W01	x	15-17 Feb	x	24-25 April	15-16 May	Project completion	Project completion	Project completion	Project completion
W02	23 Jan	x	23 Mar 27 Mar	06 April 10-11 April	4 May	28 June	2 Jul & 8 Jul	10 Aug	9 Sep
W03	24 Jan	10 Feb	24 Mar 28 Mar	10-11 April	5 May	29 June	3 Jul & 9 Jul	11 Aug	10 Sep
W04	24 Jan	x	24 Mar 28 Mar	10-11 April	5 May	30 June	3 Jul & 9 Jul	12 Aug	10 Sep
